

Cedar Lee Middle School Expansion Renovation (2)
Full Layout Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023															
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug				
Cedar Lee Middle School Expansion & Renovation (2)		408	07-Oct-21	01-May-23	0	01-May-23, Cedar Lee Middle School Expansion & Renovation (2)																											
Milestones		408	07-Oct-21	01-May-23	0	01-May-23, Milestones																											
Contractual Milestones		408	07-Oct-21	01-May-23	0	01-May-23, Contractual Milestones																											
10	NTP	0	07-Oct-21*		0	◆ NTP, 07-Oct-21*																											
						◆ Phase I Start Adm/Classroom Addition, 07-Oct-21																											
						◆ Phase II Start All Site improvements Kit Add, Reno & Collab, 31-May-22*																											
						◆ Phase III Start Aux Gym Addition, 31-May-22*																											
144	Phase II End	0		29-Jul-22*	0	◆ Phase II End,																											
36	Phase I End	0		23-Nov-22*	0	◆ Phase I End,																											
						◆ Phase IV Start Admin Demo & Renovation, 24-Nov-22*																											
231	Phase IV End	0		31-Mar-23*	0	◆ Phase III End,																											
412	Close-out Phase Start	0	03-Apr-23*		0	◆ Phase IV End,																											
232	Project Completion	0		01-May-23	0	◆ Close-out Phase Start, 03-Apr-23*																											
422	Close-out Phase End	0		01-May-23*	0	◆ Project Completion,																											
General Milestones		233	10-May-22	31-Mar-23	21	◆ Close-out Phase End,																											
21	Completion of Bus Loop	0		10-May-22	254	31-Mar-23, General Milestones																											
12	Completion of Demolition Works	0		04-Jul-22*	74	◆ Completion of Bus Loop,																											
19	Completion of Kitchen Add. & Kit /Caf Renovation	0		29-Jul-22	196	◆ Completion of Demolition Works,																											
432	Completion of Site Works	0		29-Jul-22*	0	◆ Completion of Kitchen Add. & Kit /Caf Renovation,																											
18	Completion of Classroom Addition	0		23-Nov-22	113	◆ Completion of Site Works,																											
20	Completion of Auxiliary Gymnasium Addition	0		31-Mar-23	21	◆ Completion of Classroom Addition,																											
Construction		387	07-Oct-21	31-Mar-23	21	◆ Completion of Auxiliary Gymnasium Addition																											
Sitework		44	31-May-22	29-Jul-22	0	31-Mar-23, Construction																											
Demo of Sitework		44	31-May-22	29-Jul-22	0	29-Jul-22, Sitework																											
16	Remove Fencing	10	31-May-22	13-Jun-22	0	29-Jul-22, Demo of Sitework																											
37	Demolish Culvert	6	14-Jun-22	21-Jun-22	0	■ Remove Fencing																											
38	Demolish Driveway & Apron	8	14-Jun-22	23-Jun-22	2	■ Demolish Culvert																											
40	Remove Hydrant	4	22-Jun-22	27-Jun-22	0	■ Demolish Driveway & Apron																											
43	Demolish of Storm Pipes	8	22-Jun-22	01-Jul-22	15	■ Remove Hydrant																											
41	Demolish of Sidewalks	5	28-Jun-22	04-Jul-22	0	■ Demolish of Storm Pipes																											
39	Remove Light Poles	6	05-Jul-22	12-Jul-22	0	■ Demolish of Sidewalks																											
47	Remove Ex. Bike Rack	2	05-Jul-22	06-Jul-22	14	■ Remove Light Poles																											
						■ Remove Ex. Bike Rack																											
						■ Remove Freezers & Fencing																											
						■ Remove Water Meter																											
						■ Remove Overhead Power Poles																											

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023															
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug				
Phase I		295	07-Oct-21	23-Nov-22	113	23-Nov-22, Phase I																											
Erosion & Sediment Control At Classroom Addition Area		20	07-Oct-21	03-Nov-21	57	03-Nov-21, Erosion & Sediment Control At Classroom Addition Area																											
52	Temporary Sediment Trap	4	25-Oct-21	28-Oct-21	57																												
53	Outlet Protection	4	25-Oct-21	28-Oct-21	57																												
54	Temporary Seeding	3	29-Oct-21	02-Nov-21	57																												
55	Tree Preservation & Protection	4	29-Oct-21	03-Nov-21	57																												
56	Construction Entrance With Wash Rack	3	29-Oct-21	02-Nov-21	57																												
Bus Loop Construction		139	03-Nov-21	16-May-22	54	16-May-22, Bus Loop Construction																											
Stage 01		14	03-Nov-21	22-Nov-21	57	22-Nov-21, Stage 01																											
252	Grade footprint of addition	6	15-Nov-21	22-Nov-21	57																												
Stage 02		22	15-Apr-22	16-May-22	54	16-May-22, Stage 02																											
262	Rough Grade Portion of Bus Loop	6	15-Apr-22*	22-Apr-22	54																												
272	C&G at Bus Loop and Concrete V Ditch	5	25-Apr-22	29-Apr-22	54																												
282	Base Stone at Bus Loop	7	02-May-22	10-May-22	54																												
292	Grade front of Addition	4	11-May-22	16-May-22	54																												
Classroom Addition		295	07-Oct-21	23-Nov-22	113	23-Nov-22, Classroom Addition																											
Earthworks		27	07-Oct-21	12-Nov-21	0	12-Nov-21, Earthworks																											
64	Survey Building	5	07-Oct-21	13-Oct-21	0																												
66	Excavation	12	14-Oct-21	29-Oct-21	0																												
67	Backfilling	10	01-Nov-21	12-Nov-21	0																												
Architectural Demolition		14	07-Oct-21	26-Oct-21	13	26-Oct-21, Architectural Demolition																											
1000	FA & Security Relocation from Lobby	5	07-Oct-21	13-Oct-21	13																												
1010	Insulated Tempory Wall at Lobby	2	14-Oct-21	15-Oct-21	19																												
1020	Demo ACT & Soffit Ceilings	3	15-Oct-21	20-Oct-21	13																												
1030	Demo Roof Structure	3	15-Oct-21	20-Oct-21	13																												
1040	Demo SOG & Sidewalk	4	20-Oct-21	26-Oct-21	13																												
Foundation		63	15-Nov-21	09-Feb-22	318	09-Feb-22, Foundation																											
74	Place Footing Concrete	32	02-Dec-21	14-Jan-22	0																												

Cedar Lee Middle School Expansion Renovation (2)
Full Layout Schedule

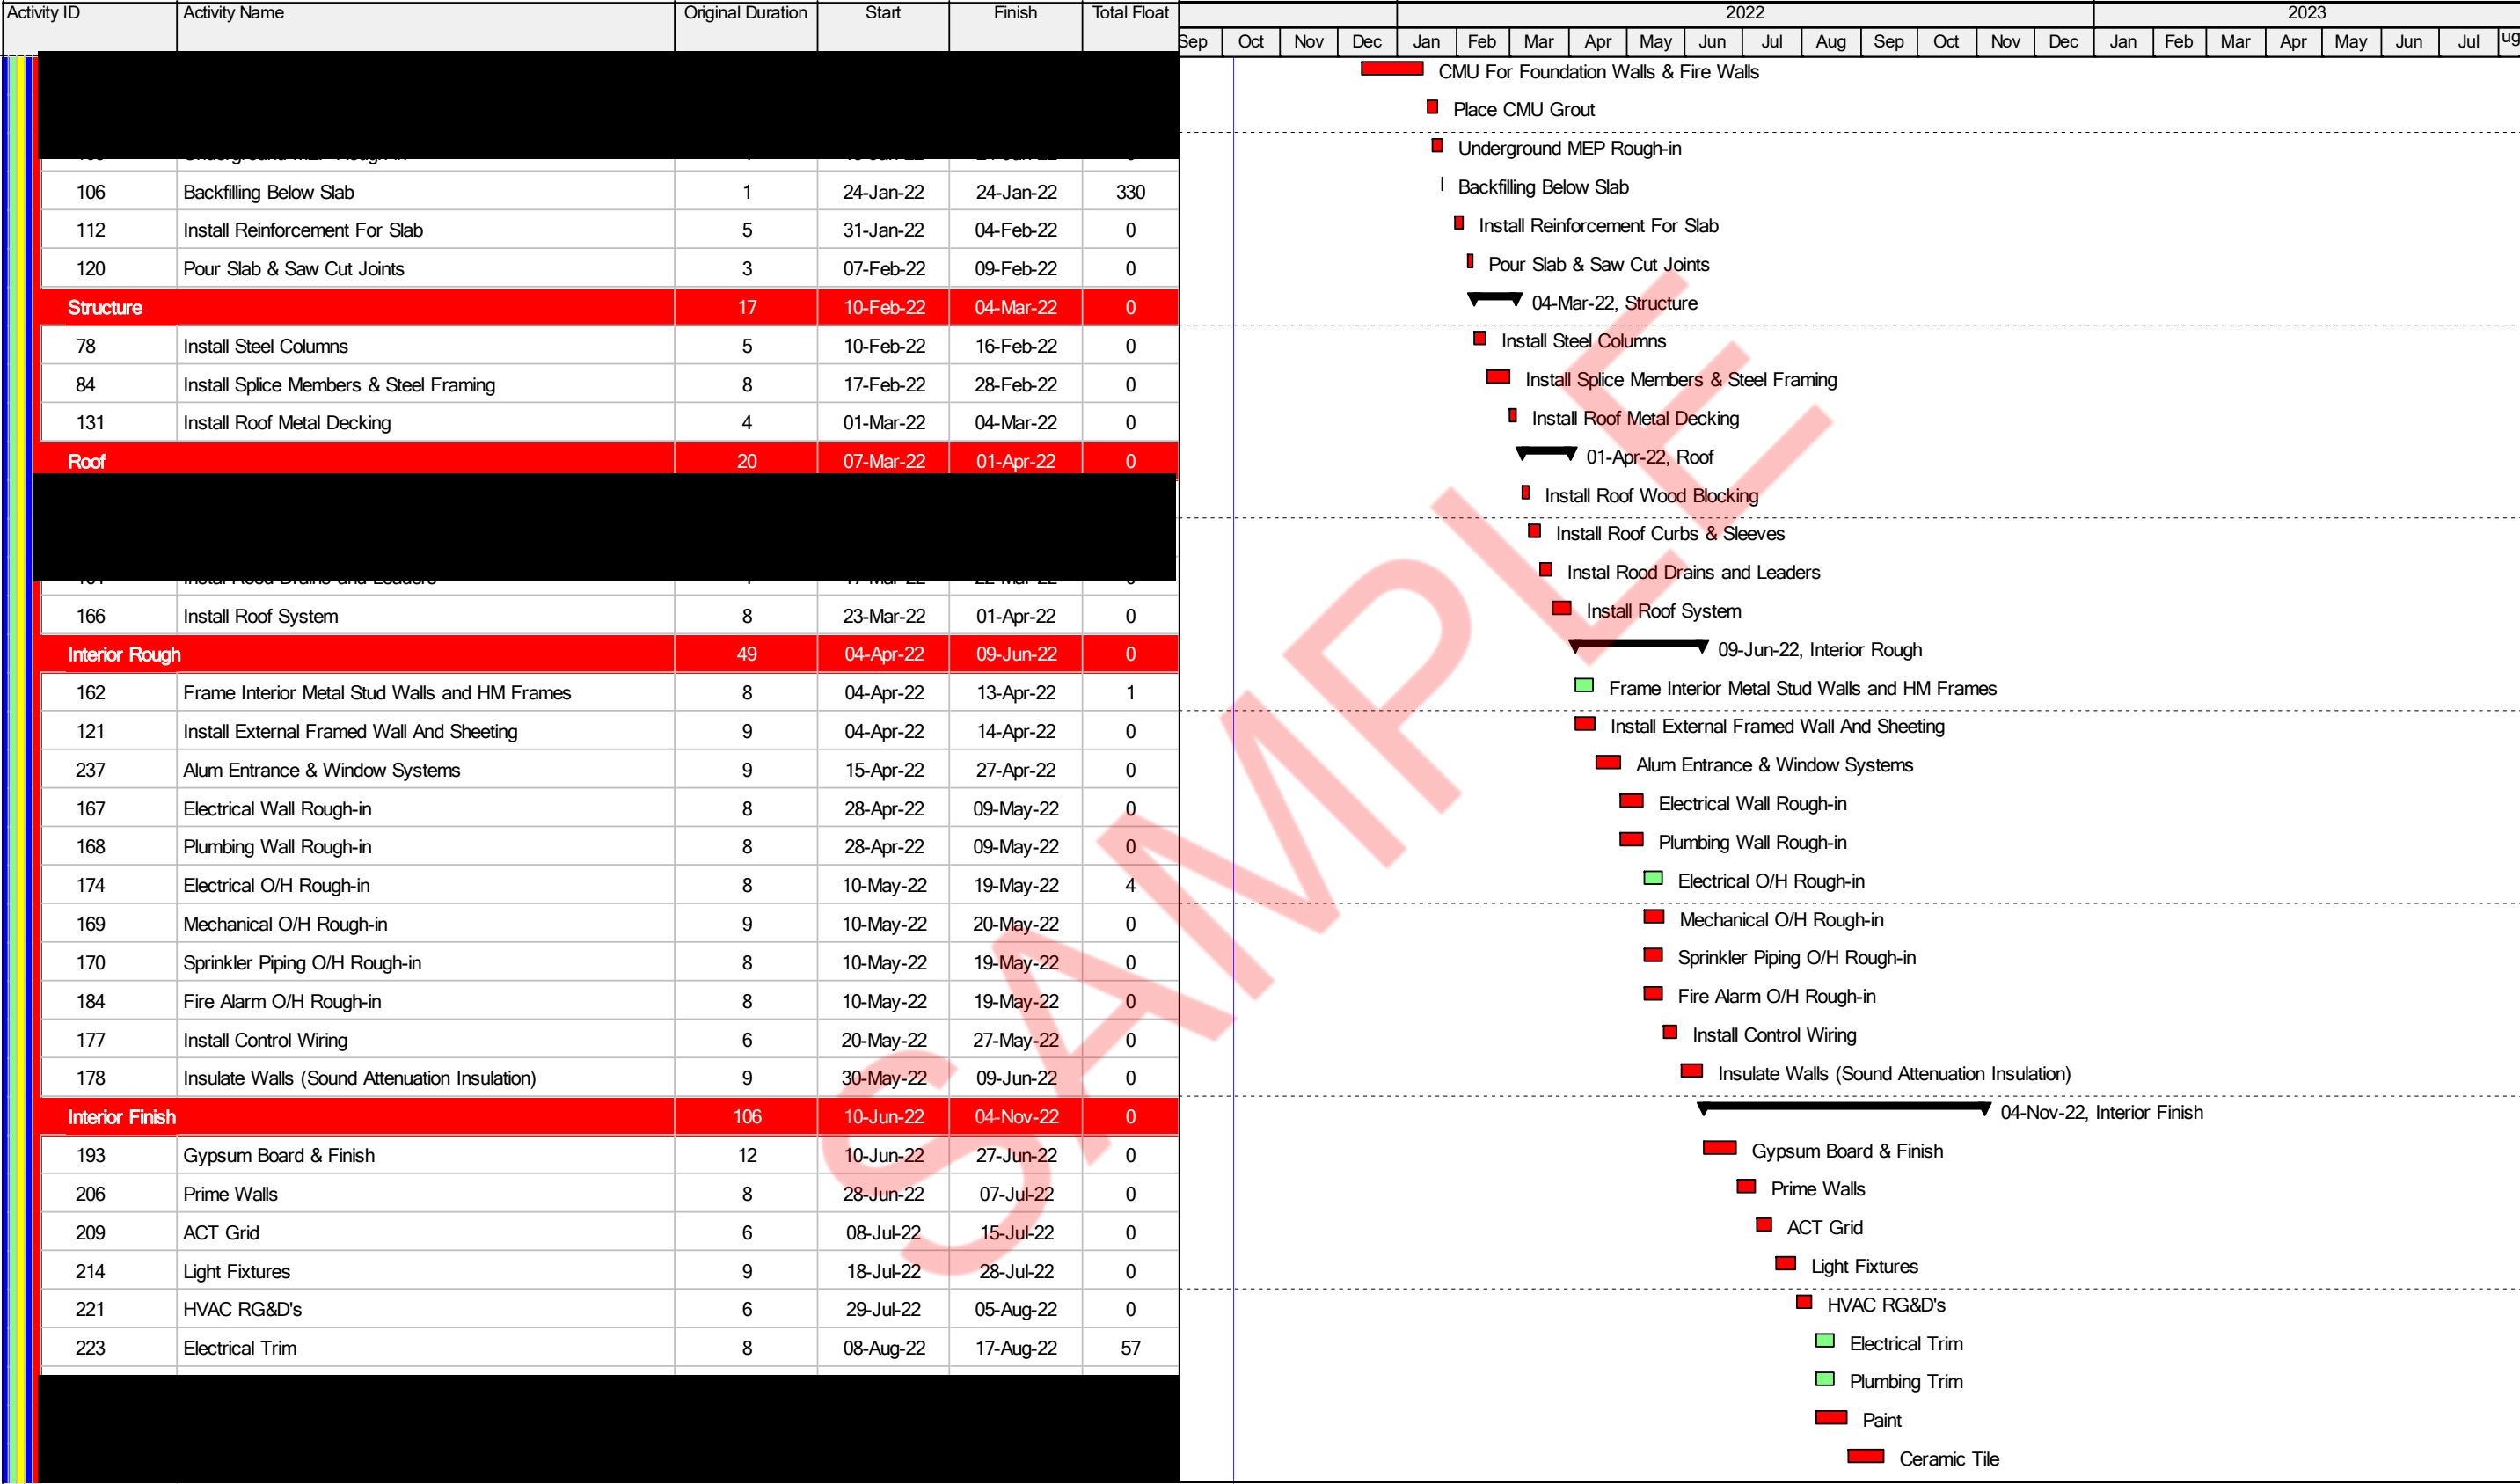

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

[illegible]

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023																
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug					
1	Structure		4	17-Jun-22	22-Jun-22	0	▼ 22-Jun-22, Structure																											
						CMU Addition Walls																												
						■ Install Roof Metal Decking																												
						Veneer at Addition																												
	Roof		4	23-Jun-22	28-Jun-22	0	▼ 28-Jun-22, Roof																											
						Roof Drains and Leaders																												
						Roof Blocking																												
						Install Roof System																												
						Metal Copings & Flashing																												
	Interior Rough		6	29-Jun-22	06-Jul-22	0	▼ 06-Jul-22, Interior Rough																											
						Layout and Demo Concrete Floors																												
						Abatement																												
						Demo Kitchen Equipment																												
						Demo Walls & Ceiling																												
						Plumbing & Elect Gnd Works																												
						Concrete SOG																												
						■ CMU Walls & HM Frames																												
						Reinforce Roof Openings																												
						Electrical Rough-in																												
						Mechanical O/H Rough-in																												
						Plumbing Rough-in																												
						Fire Alarm O/H Rough-in																												
						Install Control Wiring																												
	Interior Finish		14	07-Jul-22	26-Jul-22	0	▼ 26-Jul-22, Interior Finish																											
						Install Gypsum Bulkheads																												
						Install Primer																												
						ACT Grid																												
						RG&D's																												
						Lighting																												
						Paint																												
						Ceramic and QT Finishes																												
						■ ACT Tile																												
						Casework																												
					Doors & Hardware																													
					■ Floor Finishes																													
					Kitchen Equipment																													
					Plumbing & Electric Terminations & Trim																													

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023											
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
265	Punchout & Final Clean	1	26-Jul-22	26-Jul-22	0																								
Inspection		3	27-Jul-22	29-Jul-22	0																								
159	Pre-Final Inspection	2	27-Jul-22	28-Jul-22	0																								
172	Final Inspection	1	29-Jul-22	29-Jul-22	0																								
Phase III		219	31-May-22	31-Mar-23	0																								
Erosion & Sediment Control At Auxiliary Gymnasium Area		8	31-May-22	09-Jun-22	0																								
Renovation of Utilities At Auxiliary Gymnasium		33	10-Jun-22	26-Jul-22	0																								
86	Install of New Spliced WF-Beams Between Existing	8	10-Jun-22	21-Jun-22	0																								
91	Install New Ceiling	8	22-Jun-22	01-Jul-22	0																								
82	Install New Sanitary Line	6	04-Jul-22	11-Jul-22	0																								
251	Install New Flooring At New Sanitary Line	6	12-Jul-22	19-Jul-22	0																								
95	Install Sanitary Fixtures	5	20-Jul-22	26-Jul-22	0																								
Auxiliary Gymnasium		178	27-Jul-22	31-Mar-23	0																								
Earthworks		15	27-Jul-22	16-Aug-22	0																								
100	Survey Building	5	27-Jul-22	02-Aug-22	0																								
104	Excavation	6	03-Aug-22	10-Aug-22	0																								
108	Backfilling	5	10-Aug-22	16-Aug-22	0																								
Foundation		38	17-Aug-22	07-Oct-22	0																								
113	Building Pad	4	17-Aug-22	22-Aug-22	0																								
119	Excavate Footings	6	23-Aug-22	30-Aug-22	0																								
123	Pour Concrete Footings	4	31-Aug-22	05-Sep-22	0																								
127	CMU For Foundation Walls	4	06-Sep-22	09-Sep-22	0																								
130	Place Grout For CMU	3	12-Sep-22	14-Sep-22	0																								
133	Backfilling Below Slab	5	15-Sep-22	21-Sep-22	0																								
135	Underground MEP Rough-in	4	22-Sep-22	27-Sep-22	0																								
138	Install Reinforcement For Slab	6	28-Sep-22	05-Oct-22	0																								
141	Pour Slab & Saw Cut Joints	2	06-Oct-22	07-Oct-22	0																								
Structure		25	10-Oct-22	11-Nov-22	0																								

Equipment Start-Up

Kitchen Cleaning & Sealants

Signage & Specialties

Punchout & Final Clean

29-Jul-22, Inspection

Pre-Final Inspection

Final Inspection

31-Mar-23, Phase III

09-Jun-22, Erosion & Sediment Control At Auxiliary Gymnasium Area

Temporary Fence

Storm Drain Inlet Protection

Temporary Seeding

26-Jul-22, Renovation of Utilities At Auxiliary Gymnasium

Install of New Spliced WF-Beams Between Existing

Install New Ceiling

Install New Sanitary Line

Install New Flooring At New Sanitary Line

Install Sanitary Fixtures

16-Aug-22, Earthworks

Survey Building

Excavation

Backfilling

07-Oct-22, Foundation

Building Pad

Excavate Footings

Pour Concrete Footings

CMU For Foundation Walls

Place Grout For CMU

Backfilling Below Slab

Underground MEP Rough-in

Install Reinforcement For Slab


Pour Slab & Saw Cut Joints

11-Nov-22, Structure

Install External CMU With Vert Bars

Install Wool Insulation

Brick Veneer

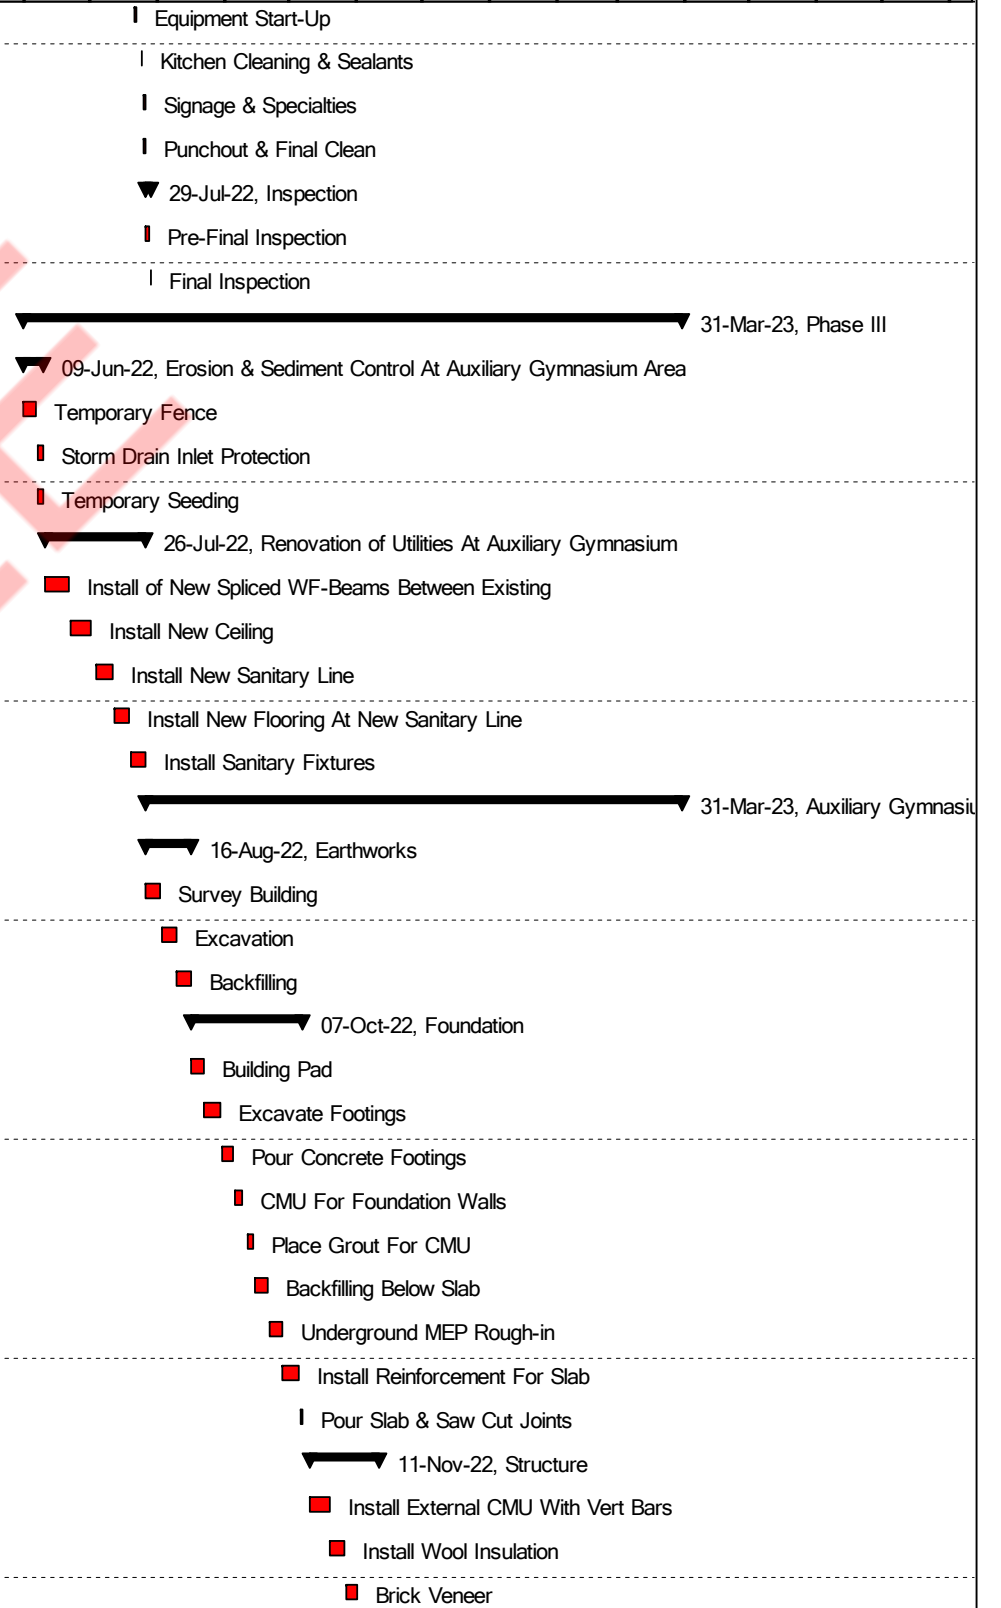

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023															
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug				
149	Install Roof Metal Decking	8	02-Nov-22	11-Nov-22	0	Install Roof Metal Decking																											
Roof		12	14-Nov-22	29-Nov-22	0	29-Nov-22, Roof Roof Drains and Leaders Roof Blocking																											
Interior Rough		26	30-Nov-22	04-Jan-23	0	04-Jan-23, Interior Rough CMU Interior Walls & HM Frames Plumbing Wall Rough-in Electrical Wall Rough-in																											
187	Fire Alarm O/H Rough-in	5	21-Dec-22	27-Dec-22	0	Fire Alarm O/H Rough-in																											
182	Electrical O/H Rough-in	5	21-Dec-22	27-Dec-22	6	Electrical O/H Rough-in																											
180	Mechanical O/H Rough-in	5	23-Dec-22	29-Dec-22	4	Mechanical O/H Rough-in																											
183	Install Control Wiring	6	28-Dec-22	04-Jan-23	0	Install Control Wiring																											
Interior Finish		49	05-Jan-23	14-Mar-23	0	14-Mar-23, Interior Finish																											
196	Install Ceiling Finish	8	05-Jan-23	16-Jan-23	0	Install Ceiling Finish																											
203	Install Primer	5	17-Jan-23	23-Jan-23	0	Install Primer																											
204	ACT Grid & Ceiling Framing	5	24-Jan-23	30-Jan-23	0	ACT Grid & Ceiling Framing																											
205	Lights & RG&D's	4	31-Jan-23	03-Feb-23	0	Lights & RG&D's																											
207	Interior Paint	5	06-Feb-23	10-Feb-23	0	Interior Paint																											
208	Install Doors & Windows	5	06-Feb-23	10-Feb-23	2	Install Doors & Windows																											
210	Electrical Trim	4	13-Feb-23	16-Feb-23	0	Electrical Trim																											
211	Plumbing Trim	4	13-Feb-23	16-Feb-23	18	Plumbing Trim																											
212	Install E-Score Board & E-Shot Clock	4	13-Feb-23	16-Feb-23	2	Install E-Score Board & E-Shot Clock																											
213	Install Basketball Backstop	6	13-Feb-23	20-Feb-23	2	Install Basketball Backstop																											
216	Special Systems Trim	4	17-Feb-23	22-Feb-23	0	Special Systems Trim																											
218	Baffles & Fabric Panels	4	23-Feb-23	28-Feb-23	0	Baffles & Fabric Panels																											
228	Signage & Specialties	4	01-Mar-23	06-Mar-23	0	Signage & Specialties																											
248	Punchout & Final Clean	6	07-Mar-23	14-Mar-23	0	Punchout & Final Clean																											
Exterior Enclosure		49	21-Dec-22	27-Feb-23	11	27-Feb-23, Exterior Enclosure																											
153	Aluminum Windows & Doors	8	21-Dec-22	30-Dec-22	11	Aluminum Windows & Doors																											
179	Install Wool Insulation	5	02-Jan-23	06-Jan-23	11	Install Wool Insulation																											
185	Brick Veneer	6	09-Jan-23	16-Jan-23	11	Brick Veneer																											
186	Exterior Framing & Composite Panels	5	17-Jan-23	23-Jan-23	11	Exterior Framing & Composite Panels																											
188	Metal Flashing / Copings	6	24-Jan-23	31-Jan-23	11	Metal Flashing / Copings																											
						Concrete Sidewalks																											
						Install Stainless Steel Handrail																											
						Paint Exterior																											

Cedar Lee Middle School Expansion Renovation (2)

Full Layout Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2022												2023																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
						Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
	Inspection	13	15-Mar-23	31-Mar-23	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

