


# IMPROVEMENTS FOR GROUNDWATER REMEDIATION CERRITOS CIVIC CENTER PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	2023												2024												
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		
<b>IMPROVEMENTS FOR GROUNDWATER REMEDIATION - CERRITOS CIVIC CENTER</b>					<b>IMPROVEMENTS FOR GROUNDWATER REMEDIATION - CERRITOS CIVIC CENTER</b>																								
<b>PRELIMINARIES</b>					<b>PRELIMINARIES</b>																								
PRE-110	Permit Approval	7	Aug-26-22	Sep-02-22	[Redacted]																								
PRE-120	Mobilization	3	Sep-06-22	Sep-08-22	[Redacted]																								
<b>EXECUTION</b>					<b>EXECUTION</b>																								
<b>LOCATION#1 BLOOMFIELD AVE.</b>					<b>LOCATION#1 BLOOMFIELD AVE.</b>																								
<b>SEWER WORKS</b>					<b>SEWER WORKS</b>																								
BA-SW-100	Trench Repair & Bedding Installation	3	Sep-09-22	Sep-13-22	[Redacted]																								
[Redacted]					[Redacted]																								
BA-SW-170	Construction of Curb Drain Outlets	4	Oct-20-22	Oct-25-22	[Redacted]																								
[Redacted]					[Redacted]																								
BA-SW-240	Replacement of Light Standard	3	Nov-30-22	Dec-02-22	[Redacted]																								
BA-SW-250	Cut & Cap Portions of Abandoned Line	3	Dec-05-22	Dec-07-22	[Redacted]																								
BA-SW-260	Construction of Sewer Lift Station Works	18	Sep-30-22	Oct-25-22	[Redacted]																								
BA-SW-270	Construction of Stomwater Lift Station Works	18	Oct-26-22	Nov-18-22	[Redacted]																								
BA-SW-280	Replacement of Damage Turf, Ground Covers, Planting & Irrigation Lines	10	Nov-21-22	Dec-02-22	[Redacted]																								
<b>PLUMBING WORKS</b>					<b>PLUMBING WORKS</b>																								
BA-PW-100	Abandon of Existing Wall Penetration & Floor Drain	5	Sep-30-22	Oct-06-22	[Redacted]																								
BA-PW-110	Construction of Drain Pipe Bend	5	Oct-07-22	Oct-13-22	[Redacted]																								
BA-PW-120	Costruction of Terminal Cleanout	5	Oct-14-22	Oct-20-22	[Redacted]																								
BA-PW-130	Construction of Pipe Supports	4	Oct-21-22	Oct-26-22	[Redacted]																								
BA-PW-140	Construction of PVC & DCML Drain Pipe	7	Oct-27-22	Nov-04-22	[Redacted]																								
BA-PW-150	Construction of DI Floor Drain & Bend	7	Nov-07-22	Nov-15-22	[Redacted]																								
BA-PW-160	Installation of Pipe Bollard	5	Nov-16-22	Nov-22-22	[Redacted]																								
BA-PW-170	Installation of Chain Link Fence & Gate	5	Nov-23-22	Nov-29-22	[Redacted]																								
<b>DRAINAGE WORKS</b>					<b>DRAINAGE WORKS</b>																								
BA-DW-100	Adjustment of Existing Drop Inlet Frame & Covers	7	Oct-14-22	Oct-24-22	[Redacted]																								
<b>CANOPY WORKS</b>					<b>CANOPY WORKS</b>																								
BA-CW-100	Installation of Canopy at East Stairs	7	Sep-09-22	Sep-19-22	[Redacted]																								
BA-CW-110	Installation of Canopy at West Stairs	7	Sep-20-22	Sep-28-22	[Redacted]																								
BA-CW-120	Installation of Canopy at North Mechanical Intake & Light Shaft	10	Sep-29-22	Oct-12-22	[Redacted]																								

SAMPLE

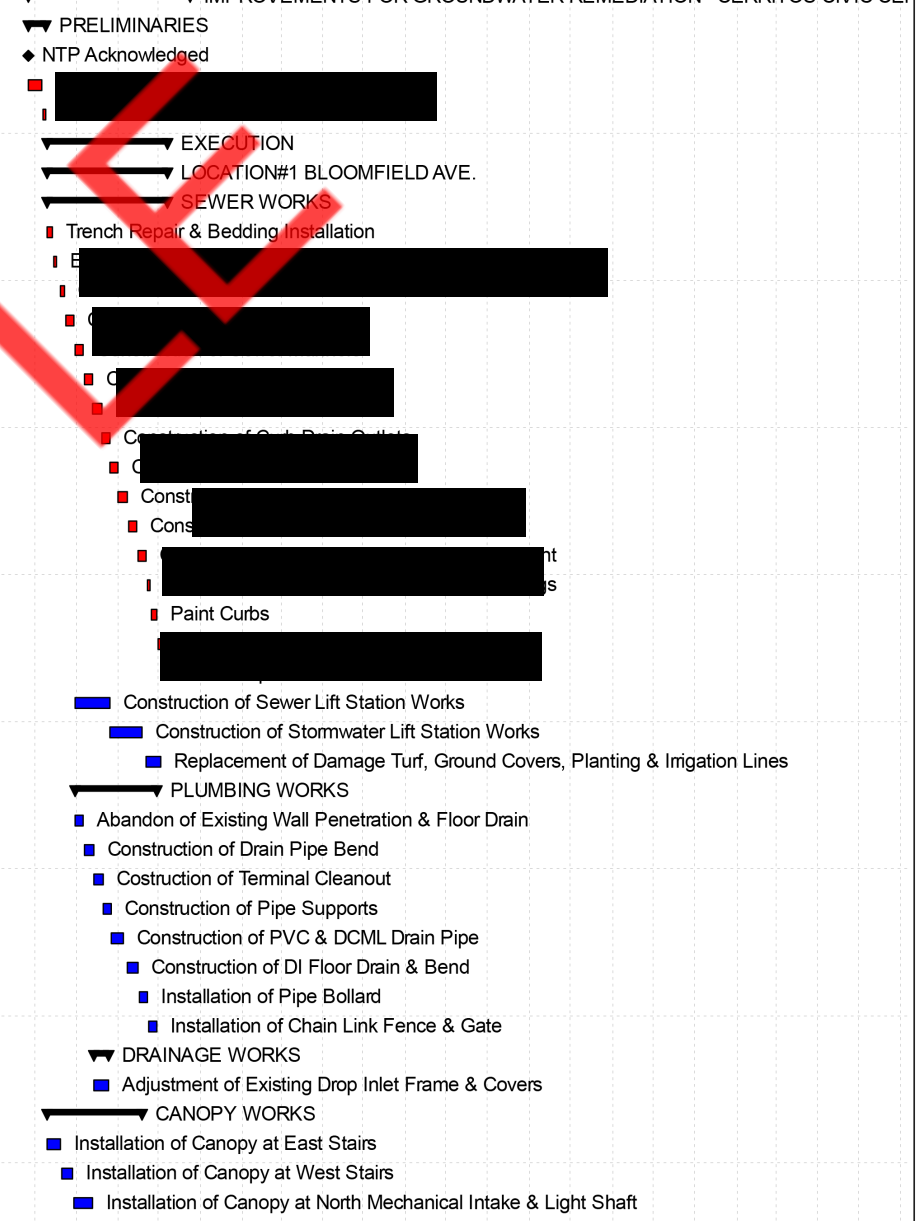

█ Actual Work   
 █ Critical Remaining Work   
 █ Remaining Work   
 ◆ Milestone

Date	Revision	Checked	Approved
Sep-08-22	00		



