

# SCHOLL CANYON LANDFILL GEOSYNTHETIC CLAY LINER FINAL COVER PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Expense Cost	2023												2024												2025											
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun								
<b>SCHOLL CANYON LANDFILL - GEOSYNTHETIC CLAY LINER FINAL COVER</b>						<b>SCHOLL CANYON LANDFILL - GEOSYNTHETIC CLAY LINER F</b>																																			
<b>MILESTONES</b>						<b>MILESTONES</b>																																			
<ul style="list-style-type: none"> <li>◆ NOTICE TO PROCEED (NTP)</li> <li>◆ Mar-06-23, INSURANCE &amp; BID BOND</li> <li>◆ Mar-06-23, ACCEPTANCE OF BASELINE SCHEDULE</li> <li>◆ START OF PHYSICAL WORK</li> <li>■ MOBILIZATION</li> </ul>						<ul style="list-style-type: none"> <li>◆ Jun-13-24, SUBSTANTIAL COMPLETION</li> <li>◆ Jul-01-24, FINAL COMPLETION</li> </ul>																																			
<b>SUBMITTALS</b>						<b>SUBMITTALS</b>																																			
<ul style="list-style-type: none"> <li>■ 40 LLDP</li> <li>■ CORRUGATED PIPE 6 INCH</li> <li>■ CORRUGATED PIPES 8 INCH</li> <li>■ CORRUGATED PIPES 36 INCH</li> <li>■ CLAY LINER</li> <li>■ GCL</li> <li>■ GEOMEMBRANE PIPE 1 INCH</li> <li>■ HYDROSEEDING</li> <li>■ SWPPP</li> <li>■ SITE GENERATOR</li> <li>■ SURVEYOR</li> <li>■ EROSION CONTROL MATT</li> <li>■ EROSION CONTROL PINS</li> <li>■ AS BUILT DRAWINGS</li> </ul>						<ul style="list-style-type: none"> <li>■ 40 LLDP</li> <li>■ MANAGEMENT TEAM</li> <li>■ CORRUGATED PIPE 6 INCH</li> <li>■ CORRUGATED PIPES 8 INCH</li> <li>■ CORRUGATED PIPES 36 INCH</li> <li>■ CLAY LINER</li> <li>■ GCL</li> <li>■ GEOMEMBRANE PIPE 1 INCH</li> <li>■ HYDROSEEDING</li> <li>■ SWPPP</li> <li>■ SITE GENERATOR</li> <li>■ SURVEYOR</li> <li>■ EROSION CONTROL MATT</li> <li>■ EROSION CONTROL PINS</li> <li>■ AS BUILT DRAWINGS</li> </ul>																																			
<b>REVIEW</b>						<b>REVIEW</b>																																			
<ul style="list-style-type: none"> <li>■ 40 LLDP</li> <li>■ MANAGEMENT TEAM</li> <li>■ CORRUGATED PIPE 6 INCH</li> <li>■ CORRUGATED PIPES 8 INCH</li> <li>■ CORRUGATED PIPES 36 INCH</li> <li>■ CLAY LINER</li> <li>■ GCL</li> <li>■ GEOMEMBRANE PIPE 1 INCH</li> <li>■ HYDROSEEDING</li> <li>■ SWPPP</li> <li>■ SITE GENERATOR</li> <li>■ SURVEYOR</li> <li>■ EROSION CONTROL MATT</li> <li>■ EROSION CONTROL PINS</li> <li>■ AS BUILT DRAWINGS</li> </ul>						<ul style="list-style-type: none"> <li>■ 40 LLDP</li> <li>■ MANAGEMENT TEAM</li> <li>■ CORRUGATED PIPE 6 INCH</li> <li>■ CORRUGATED PIPES 8 INCH</li> <li>■ CORRUGATED PIPES 36 INCH</li> <li>■ CLAY LINER</li> <li>■ GCL</li> <li>■ GEOMEMBRANE PIPE 1 INCH</li> <li>■ HYDROSEEDING</li> <li>■ SWPPP</li> <li>■ SITE GENERATOR</li> <li>■ SURVEYOR</li> <li>■ EROSION CONTROL MATT</li> <li>■ EROSION CONTROL PINS</li> <li>■ AS BUILT DRAWINGS</li> </ul>																																			

█ Actual Work   
 █ Critical Remaining Work   


█ Remaining Work   
 ◆ Milestone

Date	Revision	Checked	Approved
Mar-06-23	00		

# SCHOLL CANYON LANDFILL GEOSYNTHETIC CLAY LINER FINAL COVER PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Expense Cost	2023												2024												2025					
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		
<b>APPROVAL</b>						APPROVAL																													
APP-100	40 LLDPE	4	Mar-15-23	Jul-01-24	\$357,000.00	[Gantt bar for APP-100]																													
APP-130	CORRUGATED PIPES 8 INCH	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-130]																													
APP-140	CORRUGATED PIPES 36 INCH	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-140]																													
APP-150	CLAY LINER	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-150]																													
APP-160	GCL	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-160]																													
APP-170	GEOMEMBRANE PIPE 1 INCH	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-170]																													
APP-180	HYDROSEEDING	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-180]																													
APP-210	SWPPP	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-210]																													
APP-260	EROSION CONTROL MATT	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-260]																													
APP-270	EROSION CONTROL PINS	4	Mar-15-23	Mar-20-23	\$17,000.00	[Gantt bar for APP-270]																													
<b>EXECUTION</b>						EXECUTION																													
EA-PH1-100	SUBGRADE	3	Mar-21-23	Jun-13-24	\$4,712,000.00	[Gantt bar for EA-PH1-100]																													
EA-PH1-110	PLACING FOUNDATION LAYER 1 & COMPACTION	4	Mar-24-23	Mar-29-23	\$18,000.00	[Gantt bar for EA-PH1-110]																													
EA-PH1-120	PLACING FOUNDATION LAYER 2 & COMPACTION	4	Mar-30-23	Apr-04-23	\$19,000.00	[Gantt bar for EA-PH1-120]																													
EA-PH1-130	STORMWATER DIVERSION BERM	4	Apr-05-23	Apr-10-23	\$20,000.00	[Gantt bar for EA-PH1-130]																													
EA-PH1-140	PIPE BEDDING	3	Apr-11-23	Apr-13-23	\$15,000.00	[Gantt bar for EA-PH1-140]																													
EA-PH1-200	BACKFILLING/ DRAINAGE GRAVEL	4	May-11-23	May-16-23	\$20,000.00	[Gantt bar for EA-PH1-200]																													
EA-PH1-230	PLACING EROSION CONTROL MATS	5	May-30-23	Jun-05-23	\$20,000.00	[Gantt bar for EA-PH1-230]																													
EA-PH1-240	HYDROSEEDING	4	Jun-06-23	Jun-09-23	\$20,000.00	[Gantt bar for EA-PH1-240]																													
EA-PH2-100	SUBGRADE	3	Apr-05-23	Apr-07-23	\$20,000.00	[Gantt bar for EA-PH2-100]																													
EA-PH2-160	PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE	4	May-05-23	May-10-23	\$20,000.00	[Gantt bar for EA-PH2-160]																													

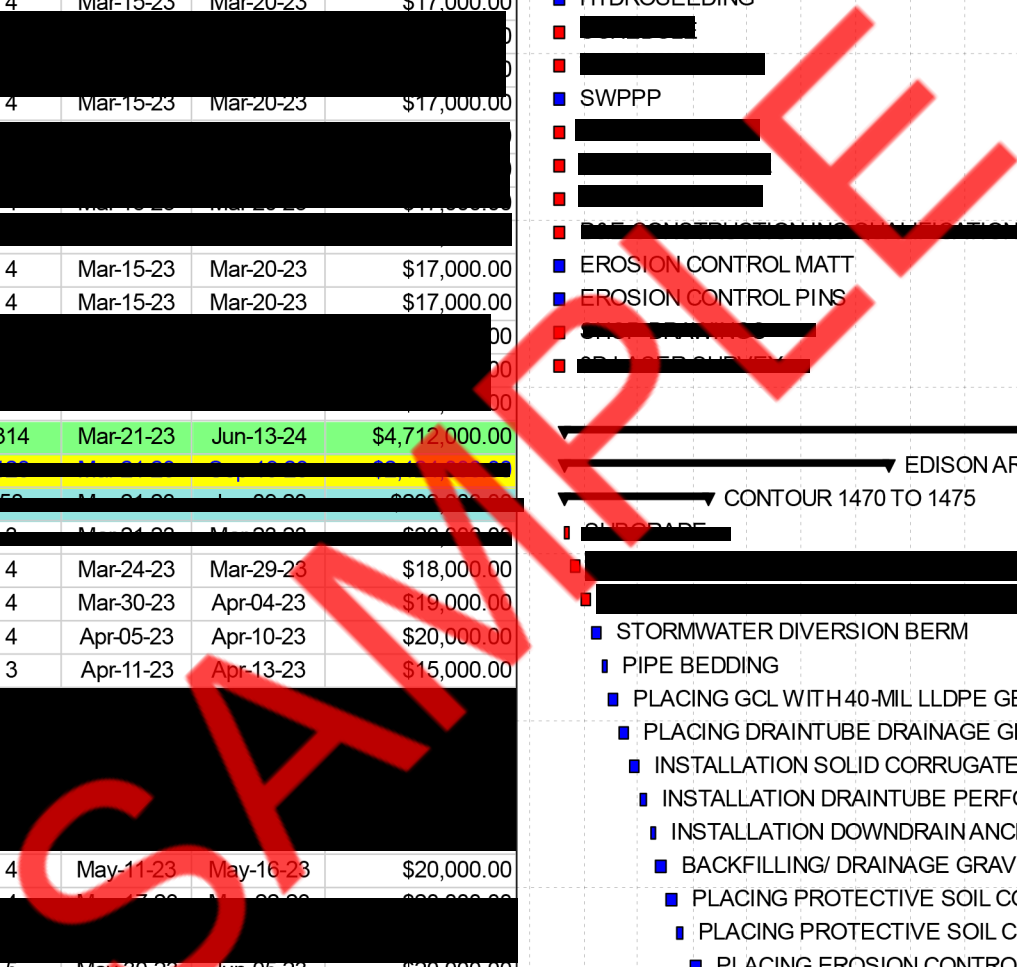

█ Actual Work   
 █ Critical Remaining Work   
 █ Remaining Work   
 ◆ Milestone

Date	Revision	Checked	Approved
Mar-06-23	00		







# SCHOLL CANYON LANDFILL GEOSYNTHETIC CLAY LINER FINAL COVER PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Expense Cost	2023												2024												2025					
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		
						[Redacted]																													
EA-PH6-160	PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE	4	Jul-10-23	Jul-13-23	\$20,000.00	[Redacted]																													
EA-PH6-170	INSTALLATION SOLID CORRUGATED HDPE PIPE	4	Jul-14-23	Jul-19-23	\$20,000.00	[Redacted]																													
EA-PH6-180	INSTALLATION DRAINTUBE PERFORATED PIPE	4	Jul-20-23	Jul-25-23	\$20,000.00	[Redacted]																													
EA-PH6-190	INSTALLATION DOWNDRAIN ANCHORS	3	Jul-26-23	Jul-28-23	\$20,000.00	[Redacted]																													
EA-PH6-200	BACKFILLING/ DRAINAGE GRAVEL	4	Jul-31-23	Aug-03-23	\$20,000.00	[Redacted]																													
						[Redacted]																													
<b>CONTOUR 1499 TO 1503</b>		<b>62</b>	<b>Jun-22-23</b>	<b>Sep-19-23</b>	<b>\$332,000.00</b>	<ul style="list-style-type: none"> <li>■ STORMWATER DIVERSION BERM</li> <li>■ PIPE BEDDING</li> <li>■ PLACING GCL WITH 40-MIL LLDPE GEOMEMBRANE MOISTURE BARRIER</li> <li>■ PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE</li> <li>■ INSTALLATION SOLID CORRUGATED HDPE PIPE</li> <li>■ INSTALLATION DRAINTUBE PERFORATED PIPE</li> <li>■ INSTALLATION DOWNDRAIN ANCHORS</li> <li>■ BACKFILLING/ DRAINAGE GRAVEL</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 1 &amp; COMPACTION</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 2 &amp; COMPACTION</li> <li>■ PLACING EROSION CONTROL MATS</li> <li>■ HYDROSEEDING</li> </ul>																													
						[Redacted]																													
EA-PH7-170	INSTALLATION SOLID CORRUGATED HDPE PIPE	4	Jul-31-23	Aug-03-23	\$20,000.00	[Redacted]																													
EA-PH7-180	INSTALLATION DRAINTUBE PERFORATED PIPE	4	Aug-04-23	Aug-09-23	\$20,000.00	[Redacted]																													
EA-PH7-190	INSTALLATION DOWNDRAIN ANCHORS	3	Aug-10-23	Aug-14-23	\$20,000.00	[Redacted]																													
EA-PH7-200	BACKFILLING/ DRAINAGE GRAVEL	4	Aug-15-23	Aug-18-23	\$20,000.00	[Redacted]																													
						[Redacted]																													
<b>KIDNEY</b>		<b>62</b>	<b>Sep-20-23</b>	<b>Dec-19-23</b>	<b>\$556,000.00</b>	[Redacted]																													
<b>CONTOUR 1428 TO 1432</b>		<b>45</b>	<b>Sep-20-23</b>	<b>Nov-22-23</b>	<b>\$272,000.00</b>	<ul style="list-style-type: none"> <li>■ SUBGRADE</li> <li>■ PIPE BEDDING</li> <li>■ PLACING GCL WITH 40-MIL LLDPE GEOMEMBRANE MOISTURE BARRIER</li> <li>■ PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE</li> <li>■ INSTALLATION SOLID CORRUGATED HDPE PIPE</li> <li>■ INSTALLATION DRAINTUBE PERFORATED PIPE</li> <li>■ INSTALLATION DOWNDRAIN ANCHORS</li> <li>■ BACKFILLING/ DRAINAGE GRAVEL</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 1 &amp; COMPACTION</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 2 &amp; COMPACTION</li> <li>■ PLACING EROSION CONTROL MATS</li> <li>■ HYDROSEEDING</li> </ul>																													
						[Redacted]																													
KD-PH1-160	INSTALLATION SOLID CORRUGATED HDPE PIPE	4	Oct-18-23	Oct-23-23	\$20,000.00	[Redacted]																													
KD-PH1-170	INSTALLATION DRAINTUBE PERFORATED PIPE	3	Oct-24-23	Oct-26-23	\$20,000.00	[Redacted]																													
KD-PH1-180	INSTALLATION DOWNDRAIN ANCHORS	3	Oct-27-23	Oct-31-23	\$20,000.00	[Redacted]																													
KD-PH1-190	BACKFILLING/ DRAINAGE GRAVEL	3	Nov-01-23	Nov-03-23	\$20,000.00	[Redacted]																													
						[Redacted]																													
<b>CONTOUR 1432 TO 1436</b>		<b>50</b>	<b>Oct-03-23</b>	<b>Dec-14-23</b>	<b>\$312,000.00</b>	<ul style="list-style-type: none"> <li>■ SUBGRADE</li> <li>■ PIPE BEDDING</li> <li>■ PLACING GCL WITH 40-MIL LLDPE GEOMEMBRANE MOISTURE BARRIER</li> </ul>																													




<span style="color: green;">█</span> Actual Work	<span style="color: red;">█</span> Critical Remaining Work	<span style="font-size: 2em;">▶</span>
<span style="color: blue;">█</span> Remaining Work	◆ Milestone	

Date	Revision	Checked	Approved
Mar-06-23	00		

# SCHOLL CANYON LANDFILL GEOSYNTHETIC CLAY LINER FINAL COVER PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Expense Cost	2023												2024												2025					
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		
<b>CONTOUR 1436 TO 1440</b> 44 Oct-16-23 Dec-19-23 \$272,000.00						<ul style="list-style-type: none"> <li>■ PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE</li> <li>■ INSTALLATION SOLID CORRUGATED HDPE PIPE</li> <li>■ INSTALLATION DRAINTUBE PERFORATED PIPE</li> <li>■ INSTALLATION DOWNDRAIN ANCHORS</li> <li>■ BACKFILLING/ DRAINAGE GRAVEL</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 1 &amp; COMPACTION</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 2 &amp; COMPACTION</li> <li>■ PLACING EROSION CONTROL MATS</li> <li>■ CONSTRUCTION OF SETTLEMENT MONUMENT</li> <li>■ PLACING PROTECTIVE CONCRETE BLOCKS</li> <li>■ HYDROSEEDING</li> </ul>																													
<b>CONTOUR 1439 TO 1442</b> 54 Dec-20-23 Mar-06-24 \$292,000.00						<ul style="list-style-type: none"> <li>■ SUBGRADE</li> <li>■ PLACING EROSION CONTROL MATS</li> <li>■ WINDY CANYON</li> <li>■ CONTOUR 1439 TO 1442</li> <li>■ SUBGRADE</li> <li>■ STORMWATER DIVERSION BERM</li> <li>■ PIPE BEDDING</li> <li>■ PLACING GCL WITH 40-MIL LLDPE GEOMEMBRANE MOISTURE BARRIER</li> <li>■ PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE</li> <li>■ INSTALLATION SOLID CORRUGATED HDPE PIPE</li> <li>■ INSTALLATION DRAINTUBE PERFORATED PIPE</li> <li>■ INSTALLATION DOWNDRAIN ANCHORS</li> <li>■ BACKFILLING/ DRAINAGE GRAVEL</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 1 &amp; COMPACTION</li> <li>■ PLACING PROTECTIVE SOIL COVER LAYER 2 &amp; COMPACTION</li> <li>■ PLACING EROSION CONTROL MATS</li> <li>■ HYDROSEEDING</li> </ul>																													
<b>CONTOUR 1442 TO 1446</b> 55 Jan-04-24 Mar-20-24 \$312,000.00						<ul style="list-style-type: none"> <li>■ SUBGRADE</li> <li>■ PIPE BEDDING</li> <li>■ PLACING GCL WITH 40-MIL LLDPE GEOMEMBRANE MOISTURE BARRIER</li> <li>■ PLACING DRAINTUBE DRAINAGE GEOCOMPOSITE</li> <li>■ INSTALLATION SOLID CORRUGATED HDPE PIPE</li> <li>■ INSTALLATION DRAINTUBE PERFORATED PIPE</li> <li>■ INSTALLATION DOWNDRAIN ANCHORS</li> <li>■ BACKFILLING/ DRAINAGE GRAVEL</li> </ul>																													

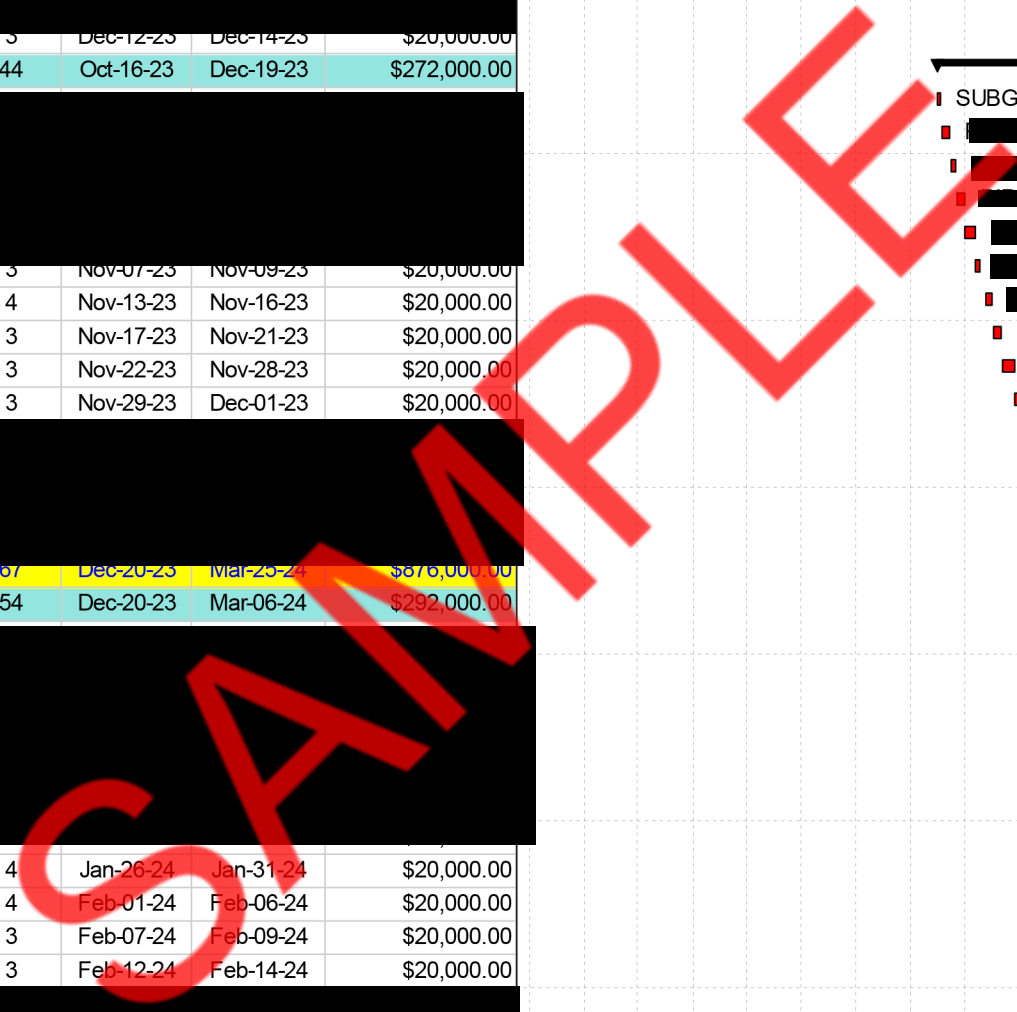

■ Actual Work   
 ■ Critical Remaining Work   
 ■ Remaining Work   
 ◆ Milestone

Date	Revision	Checked	Approved
Mar-06-23	00		

© Primavera Systems, Inc.






**SCHOLL CANYON LANDFILL  
GEOSYNTHETIC CLAY LINER FINAL COVER  
PROJECT SCHEDULE**



Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Expense Cost	2023												2024												2025											
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun								
						[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]
BF-PH3-160	INSTALLATION SOLID CORRUGATED HDPE PIPE	2	May-13-24	May-14-24	\$20,000.00																																				
BF-PH3-170	INSTALLATION DRAINTUBE PERFORATED PIPE	2	May-15-24	May-16-24	\$20,000.00																																				
BF-PH3-180	INSTALLATION DOWNDRAIN ANCHORS	2	May-17-24	May-20-24	\$20,000.00																																				
BF-PH3-190	BACKFILLING/ DRAINAGE GRAVEL	3	May-21-24	May-23-24	\$20,000.00																																				
[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	
<b>PROJECT CLOSEOUT</b>		<b>12</b>	<b>Jun-13-24</b>	<b>Jul-01-24</b>	<b>\$100,000.00</b>																																				
PC-100	SUBSTANTIAL COMPLETION	0		Jun-13-24	\$20,000.00																																				
[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	
PC-140	FINAL COMPLETION	0		Jul-01-24	\$20,000.00																																				

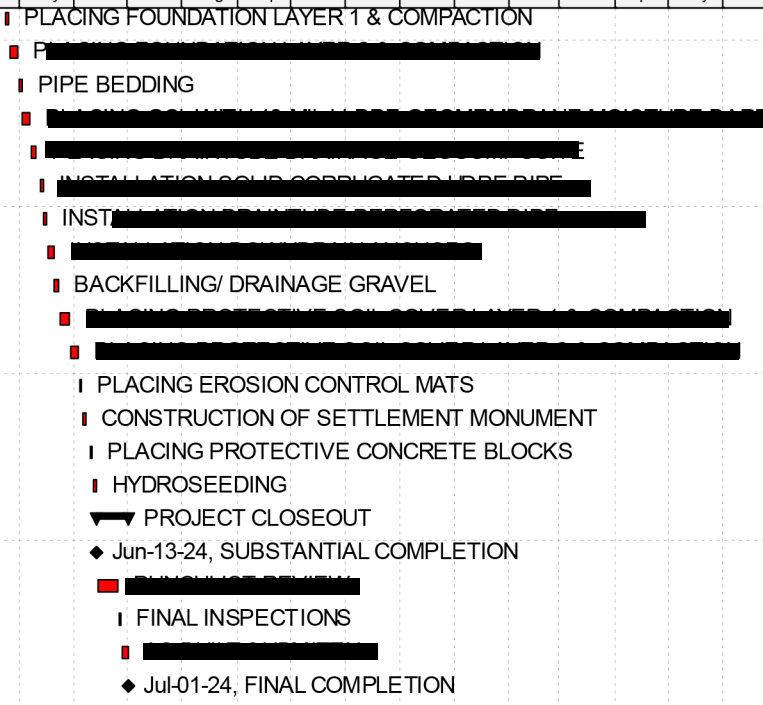

SAMPLE

Date	Revision	Checked	Approved
Mar-06-23	00		

