

Village of Mount Kisco-Mutual Fire Station-Addition and Alterations Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 3, 2023		Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024						
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun				
<b>Village of Mount Kisco-Mutual Fire Station-Addition and Alteration</b>					218	17-Jul-23	31-May-24	31-May-24											
<b>MILESTONES</b>					218	17-Jul-23	31-May-24	31-May-24											
MS-0010	Notice to Proceed (NTP)	0	17-Jul-23*		Notice to Proceed (NTP), 17-Jul-23*														
MS-0020	Project Substantial Completion	0		15-May-24*	◆ Project Substan														
MS-0030	Project Final Completion	0		31-May-24*	◆ Project F														
<b>ENGINEERING</b>					57	17-Jul-23	12-Sep-23	12-Sep-23, ENGINEERING											
<b>SUBMISSION</b>					43	17-Jul-23	28-Aug-23	28-Aug-23, SUBMISSION											
SUB-0010	Submission of all submittals except finishes	29	17-Jul-23	14-Aug-23	Submission of all submittals except finishes														
SUB-0020	Submission of Finishes Submittals	43	17-Jul-23	28-Aug-23	Submission of Finishes Submittals														
<b>REVIEW &amp; APPROVAL</b>					28	15-Aug-23	12-Sep-23	12-Sep-23, REVIEW & APPROVAL											
RA-0010	Review & Approval of all submittals except finishes	14	15-Aug-23	28-Aug-23	Review & Approval of all submittals except finishes														
RA-0020	Review & Approval of Finishes Submittals	14	29-Aug-23	12-Sep-23	Review & Approval of Finishes Submittals														
<b>PROCUREMENT</b>					222	29-Aug-23	17-Apr-24	17-Apr-24, PROCUREMENT											
PROC-0030	Fabrication and Delivery of RTU	193	29-Aug-23	18-Mar-24	Fabrication and Delivery of RTU														
<b>CONSTRUCTION</b>					197	17-Jul-23	01-May-24	01-May-24, CONSTRU											
<b>EARLY SITE WORKS</b>					20	17-Jul-23	11-Aug-23	11-Aug-23, EARLY SITE WORKS											
ESW-0010	Installation of Temporary Fence	5	17-Jul-23	21-Jul-23	Installation of Temporary Fence														
ESW-0020	Installation of Silt Fence	5	24-Jul-23	28-Jul-23	Installation of Silt Fence														
ESW-0030	Installation of Erosion Control Measures	5	31-Jul-23	04-Aug-23	Installation of Erosion Control Measures														
ESW-0040	Clear & Grub	5	07-Aug-23	11-Aug-23	Clear & Grub														
<b>DEMOLITIONS</b>					73	07-Aug-23	20-Nov-23	20-Nov-23, DEMOLITIONS											
<b>ELECTRICAL DEMOLITIONS</b>					34	05-Sep-23	23-Oct-23	23-Oct-23, ELECTRICAL DEMOLITIONS											
DEM-0010	Remove Existing Service Riser	1	05-Sep-23	05-Sep-23	Remove Existing Service Riser														
DEM-0020	Remove Existing Service Conductor	1	06-Sep-23	06-Sep-23	Remove Existing Service Conductor														
DEM-0030	Remove Existing Pole Mounted Transformers	5	07-Sep-23	13-Sep-23	Remove Existing Pole Mounted Transformers														
DEM-0080	Remove Existing Exhaust Fans	2	05-Sep-23	06-Sep-23	Remove Existing Exhaust Fans														
DEM-0090	Remove Existing Lighting Fixtures	3	07-Sep-23	11-Sep-23	Remove Existing Lighting Fixtures														
DEM-0100	Remove Existing Hot Water Unit	2	12-Sep-23	13-Sep-23	Remove Existing Hot Water Unit														
DEM-0110	Remove Existing Utility Meter	1	14-Sep-23	14-Sep-23	Remove Existing Utility Meter														
DEM-0120	Remove Existing Distribution Panel	4	15-Sep-23	20-Sep-23	Remove Existing Distribution Panel														
DEM-0130	Remove Main server Dsconnect Switch	3	21-Sep-23	25-Sep-23	Remove Main server Dsconnect Switch														
DEM-0140	Remove Automatic Transfer Switch	2	26-Sep-23	27-Sep-23	Remove Automatic Transfer Switch														
DEM-0150	Remove Existing Bay door motor	2	28-Sep-23	29-Sep-23	Remove Existing Bay door motor														
DEM-0160	Remove Wiring Devices	5	02-Oct-23	06-Oct-23	Remove Wiring Devices														
DEM-0170	Remove Fire Alarm Devices	5	10-Oct-23	16-Oct-23	Remove Fire Alarm Devices														
DEM-0180	Remove Telephone/Data inlets and outlets	3	17-Oct-23	19-Oct-23	Remove Telephone/Data inlets and outlets														
DEM-0190	Remove Projector	1	20-Oct-23	20-Oct-23	Remove Projector														
DEM-0200	Remove Exit Sign	1	23-Oct-23	23-Oct-23	Remove Exit Sign														
<b>MECHANICAL DEMOLITIONS</b>					13	24-Oct-23	09-Nov-23	09-Nov-23, MECHANICAL DEMOLITIONS											
DEM-0210	Remove Plumbing Fixtures	2	24-Oct-23	25-Oct-23	Remove Plumbing Fixtures														
DEM-0220	Cut, Cap Cold water line to be reconnected	2	26-Oct-23	27-Oct-23	Cut, Cap Cold water line to be reconnected														


SAMPLE

█ Actual Level of Effort   
 █ Remaining Work   
 ◆ Milestone  
█ Actual Work   
 █ Critical Remaining Work   
 ▾ summary

Village of Mount Kisco-Mutual Fire Station-Addition and Alterations Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 3, 2023		Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024		
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
DEM-0221	Remove Gas Meter, piping	1	26-Oct-23	26-Oct-23											
DEM-0222	Remove 6" Tile Catch Basin Connection	1	27-Oct-23	27-Oct-23											
DEM-0223	Remove Existing 12" CMP Catch Basin Connection	1	30-Oct-23	30-Oct-23											
DEM-0230	Cut, Cap existing HHSW/R Piping	2	30-Oct-23	31-Oct-23											
DEM-0240	Remove GE Window A/C	2	01-Nov-23	02-Nov-23											
DEM-0250	Remove FTR	1	03-Nov-23	03-Nov-23											
DEM-0260	Remove 24x12 EA Riser up to EF	1	06-Nov-23	06-Nov-23											
DEM-0270	Remove 24x24 EA Grille	1	07-Nov-23	07-Nov-23											
DEM-0280	Remove Roof Top supply/return duct work	1	08-Nov-23	08-Nov-23											
DEM-0290	Remove Roof Top Unit	1	09-Nov-23	09-Nov-23											
<b>ARCHITECTURAL DEMOLITIONS</b>		<b>73</b>	<b>07-Aug-23</b>	<b>20-Nov-23</b>	20-Nov-23, ARCHITECTURAL DEMOLITIONS										
<b>EXTERIOR DEMOLITIONS</b>		<b>16</b>	<b>07-Aug-23</b>	<b>28-Aug-23</b>	28-Aug-23, EXTERIOR DEMOLITIONS										
DEM-0300	Remove Existing Oil tank concrete pad	1	07-Aug-23	07-Aug-23											
DEM-0310	Remove Generator concrete pad	1	08-Aug-23	08-Aug-23											
DEM-0320	Remove Chain Link Fence	1	09-Aug-23	09-Aug-23											
DEM-0330	Remove Catch Basin	1	10-Aug-23	10-Aug-23											
DEM-0340	Remove Concrete Curb	1	11-Aug-23	11-Aug-23											
DEM-0350	Remove Bell, Pedestal	1	14-Aug-23	14-Aug-23											
DEM-0390	Remove Retaining Wall & Concr. Pad	3	21-Aug-23	23-Aug-23											
DEM-0400	Remove existing swale and rip-rap	2	24-Aug-23	25-Aug-23											
DEM-0410	Remove Tree and Roots	1	28-Aug-23	28-Aug-23											
<b>INTERIOR DEMOLITIONS</b>		<b>53</b>	<b>05-Sep-23</b>	<b>20-Nov-23</b>	20-Nov-23, INTERIOR DEMOLITIONS										
DEM-0420	Abestos Abatement	10	05-Sep-23	18-Sep-23											
DEM-0430	Remove Existing Wall Systems	8	19-Sep-23	28-Sep-23											
DEM-0440	Remove Existing Doors, Frames, Hardware	3	29-Sep-23	03-Oct-23											
DEM-0450	Remove Toilet Accessories	2	04-Oct-23	05-Oct-23											
DEM-0460	Sawcut New opening in existing masonry wall	2	06-Oct-23	10-Oct-23											
DEM-0470	Remove overhead door, frame and hardware	3	11-Oct-23	13-Oct-23											
DEM-0480	Remove suspended accoustical ceiling system	5	16-Oct-23	20-Oct-23											
DEM-0490	Remove Windows and portion of wall below	3	23-Oct-23	25-Oct-23											
DEM-0500	Remove portion of wall to create passageway	2	26-Oct-23	27-Oct-23											
DEM-0510	Remove Utility Sink	1	30-Oct-23	30-Oct-23											
DEM-0520	Remove Existing Flooring and Existing Wall base	8	31-Oct-23	09-Nov-23											
DEM-0530	Remove existing interior roof access ladder	1	13-Nov-23	13-Nov-23											
DEM-0540	Salvage Existing Cast iron wheel for new overhead door	1	14-Nov-23	14-Nov-23											
DEM-0550	Remove existing roof membrane	1	15-Nov-23	15-Nov-23											
<b>EXECUTION</b>		<b>162</b>	<b>05-Sep-23</b>	<b>01-May-24</b>	01-May-24, EXECUTION										
<b>CIVIL WORKS</b>		<b>118</b>	<b>05-Sep-23</b>	<b>28-Feb-24</b>	28-Feb-24, CIVIL WORKS										
EXE-0010	Excavation Works to Foundations Level	8	05-Sep-23	14-Sep-23											

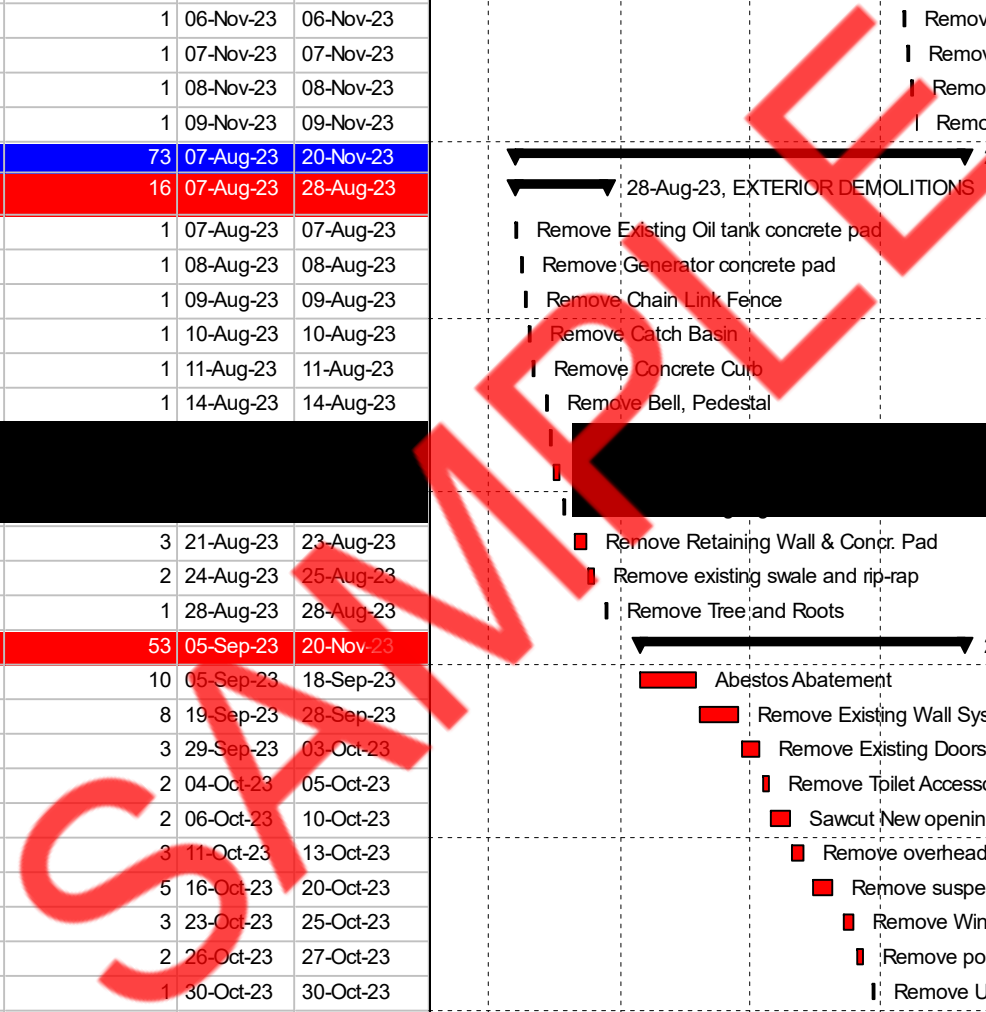

█ Actual Level of Effort   
 █ Remaining Work   
 ◆ Milestone  
█ Actual Work   
 █ Critical Remaining Work   
 ▬ summary

Village of Mount Kisco-Mutual Fire Station-Addition and Alterations Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 3, 2023		Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024		
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
EXE-0020	Grading Works	5	15-Sep-23	21-Sep-23			■								
EXE-0030	Installation of New Retaining Wall	10	22-Sep-23	05-Oct-23			■								
EXE-0040	Installation of Drainage System	3	06-Oct-23	11-Oct-23			■								
EXE-0050	Installation of Raft Formwork	3	12-Oct-23	16-Oct-23				■							
EXE-0060	Installation of Raft Steel Reinforcement rebar works	5	17-Oct-23	23-Oct-23				■							
EXE-0070	Pouring Raft Concrete	1	24-Oct-23	24-Oct-23					■						
EXE-0080	Insulation of Raft Concrete	1	25-Oct-23	25-Oct-23					■						
EXE-0130	Backfilling & Grading to ground level	8	22-Nov-23	05-Dec-23											
EXE-0140	Installation of Slab on Grade formwork	5	06-Dec-23	12-Dec-23											
EXE-0150	Installation of Slab on Grade Steel Reinforcement rebar works	8	13-Dec-23	22-Dec-23											
EXE-0160	Pouring Slab on Grade Concrete	1	26-Dec-23	26-Dec-23											
EXE-0170	Installation of CMU Wall	5	27-Dec-23	03-Jan-24											
EXE-0180	Installation of Elevator Shaft CMU Walls	5	27-Dec-23	03-Jan-24											
EXE-0190	Installation of 1st Floor Slab Formwork	5	04-Jan-24	10-Jan-24											
EXE-0200	Installation of 1st Floor Slab Steel Reinforcement Rebar work	8	11-Jan-24	23-Jan-24											
EXE-0210	Pouring 1st Floor Slab Concrete	1	24-Jan-24	24-Jan-24											
EXE-0220	Installation of Exterior CMU wall	8	25-Jan-24	05-Feb-24											
EXE-0230	Installation of Steel Metal Decking	5	06-Feb-24	13-Feb-24											
EXE-0240	Installation of Steel Roof Truss Framing and Bracing	8	14-Feb-24	26-Feb-24											
EXE-0250	Installation of Purlins	2	27-Feb-24	28-Feb-24											
EXE-0560	Installation of Elevators Steel Frames and Supports	10	14-Feb-24	28-Feb-24											
EXE-0820	Installation of Generator Concrete Pad	8	06-Feb-24	16-Feb-24											
<b>FINISHING WORKS</b>					40	29-Feb-24	25-Apr-24								
EXE-0260	Installation of Cast Stone Veneer	5	29-Feb-24	06-Mar-24											
EXE-0270	Installation of Cast Stones	8	07-Mar-24	18-Mar-24											
EXE-0280	Installation of Brick Veneer	8	07-Mar-24	18-Mar-24											
EXE-0290	Installation of Windows	8	19-Mar-24	28-Mar-24											
EXE-0300	Installation of External Paint	8	19-Mar-24	28-Mar-24											
EXE-0350	Installation of Overflow Scupper	1	02-Apr-24	02-Apr-24											
EXE-0360	Installation of In-Swing Training Door	1	02-Apr-24	02-Apr-24											
EXE-0370	Installation of wall mounted D-ring	1	03-Apr-24	03-Apr-24											
EXE-0380	Installation of Internal CMU Wall	5	29-Feb-24	06-Mar-24											
EXE-0390	Installation of Dry wall studs	5	29-Feb-24	06-Mar-24											
EXE-0400	Installation of Dry Wall Gypsum Board	9	07-Mar-24	19-Mar-24											
EXE-0410	Installation of Dry Wall Gypsum Board paint	10	20-Mar-24	03-Apr-24											
EXE-0420	Installation of Fiber Glass Reinforced Panels	10	29-Feb-24	13-Mar-24											
EXE-0430	Installation of Ceiling Suspended Accoustic panels Frames	10	20-Mar-24	03-Apr-24											
EXE-0440	Installation of Ceiling Suspended Accoustic Panels Tiles	4	04-Apr-24	09-Apr-24											
EXE-0450	Installation of Exposed Ceiling paint	8	20-Mar-24	29-Mar-24											
EXE-0460	Installation of Floor rubber base	2	10-Apr-24	11-Apr-24											

SAMPLE

■ Actual Level of Effort   
 ■ Remaining Work   
 ■ Critical Remaining Work   
 ◆ Milestone   
 ─ summary

Village of Mount Kisco-Mutual Fire Station-Addition and Alterations Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 3, 2023		Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
EXE-0470	Installation of Floor Luxury Vinyl Tiles	8	12-Apr-24	23-Apr-24											Installation of Floor Luxury	
EXE-0480	Installation of Floor Sealed Concrete	5	10-Apr-24	16-Apr-24											Installation of Floor Sealed Cc	
EXE-0490	Installation of Wall Ceramic Tiles in Bathrooms	8	19-Mar-24	28-Mar-24											Installation of Wall Ceramic Tiles in Bat	
EXE-0500	Installation of Floor Cermaic Tiles in Bathrooms	8	29-Mar-24	10-Apr-24											Installation of Floor Cermaic Tiles	
EXE-0510	Installation of Gypsum Ceiling	6	04-Apr-24	11-Apr-24											Installation of Gypsum Ceiling	
EXE-0520	Installation of Ceiling paint	3	12-Apr-24	16-Apr-24											Installation of Ceiling paint	
[REDACTED]																
EXE-0580	Installation of new plastic laminated Counter	2	24-Apr-24	25-Apr-24											Installation of new plastic	
EXE-0590	Installation of 5/8" Coverboard and EPDM Membrane	10	29-Feb-24	13-Mar-24											Installation of 5/8" Coverboard and EPDM Mem	
EXE-0600	Installation of new P.T Blocking at Existing parapet	3	14-Mar-24	18-Mar-24											Installation of new P.T Blocking at Existing p	
EXE-0610	Installation of Wall mounted TV	1	24-Apr-24	24-Apr-24											Installation of Wall mounte	
EXE-0620	Installation of Self Contained Eye Wash Station	2	24-Apr-24	25-Apr-24											Installation of Self Contain	
<b>MECHANICAL WORKS</b>		<b>37</b>	<b>29-Feb-24</b>	<b>22-Apr-24</b>												<b>22-Apr-24, MECHANICAL V</b>
EXE-0630	Installation of Cold Water Supply Pipes	5	07-Mar-24	13-Mar-24											Installation of Cold Water Supply Pipes	
EXE-0640	Installation of Hot Water Supply Pipes	5	07-Mar-24	13-Mar-24											Installation of Hot Water Supply Pipes	
EXE-0650	Installation of Vent Pipes	5	07-Mar-24	13-Mar-24											Installation of Vent Pipes	
EXE-0660	Installation of Drainage Pipes	5	07-Mar-24	13-Mar-24											Installation of Drainage Pipes	
EXE-0670	Insulation of Hot Water Pipes	3	14-Mar-24	18-Mar-24											Insulation of Hot Water Pipes	
EXE-0680	Installation of Duct Work	8	07-Mar-24	18-Mar-24											Installation of Duct Work	
EXE-0690	Installation of refrigerent Pipes	4	19-Mar-24	22-Mar-24											Installation of refrigerent Pipes	
EXE-0700	Insulation of Ducts and Pipes	3	25-Mar-24	27-Mar-24											Insulation of Ducts and Pipes	
EXE-0701	Installation of Fire Stop around penetration	4	28-Mar-24	03-Apr-24											Installation of Fire Stop around pene	
EXE-0710	Installation of HVAC Heaters	8	19-Mar-24	28-Mar-24											Installation of HVAC Heaters	
EXE-0720	Installation of Dampers	8	19-Mar-24	28-Mar-24											Installation of Dampers	
[REDACTED]																
<b>ELECTRICAL WORKS</b>		<b>11</b>	<b>17-Apr-24</b>	<b>01-May-24</b>												<b>01-May-24, ELECTRIC</b>
EXE-0770	Installation of Generator & Accessories	10	18-Apr-24	01-May-24											Installation of Generat	
EXE-0780	Installation of Switchgear	10	18-Apr-24	01-May-24											Installation of Switchge	
EXE-0790	Installation of Lighting Fixtures	6	24-Apr-24	01-May-24											Installation of Lighting	
EXE-0800	Installation of Wiring Devices	5	17-Apr-24	23-Apr-24											Installation of Wiring Devi	
EXE-0810	Installation of Fire Alarm System and Devices	10	18-Apr-24	01-May-24											Installation of Fire Alar	
<b>LANDSCAPE WORKS</b>		<b>39</b>	<b>29-Feb-24</b>	<b>24-Apr-24</b>												<b>24-Apr-24, LANDSCAPE V</b>
EXE-0830	Installation of Final Grading & Concrete Curbs	10	29-Feb-24	13-Mar-24											Installation of Final Grading & Concrete Curbs	
EXE-0840	Installatoin of new aggregate course	6	04-Apr-24	11-Apr-24											Installatoin of new aggregate co	
EXE-0850	Installation of Asphalt Pavement	4	12-Apr-24	17-Apr-24											Installation of Asphalt Pavem	
EXE-0860	Installation of Pemenant Seeding Plantation	5	18-Apr-24	24-Apr-24											Installation of Pemenant	
<b>PROJECT CLOSE-OUT</b>		<b>20</b>	<b>18-Apr-24</b>	<b>15-May-24</b>												<b>15-May-24, PRO</b>
PCO-0001	Removal of Temp. Fence & Silt Fence	10	18-Apr-24	01-May-24											Removal of Temp. Fer	
PCO-0002	Removal of Erosion Control Measures, Debris	10	18-Apr-24	01-May-24											Removal of Erosion Cc	
PCO-0010	Testing & Commissioning	10	02-May-24	15-May-24											Testing & Comm	
PCO-0020	Snagging and Punch List	10	02-May-24	15-May-24											Snagging and F	

SAMPLE

█ Actual Level of Effort   
 █ Remaining Work   
 █ Critical Remaining Work   
 ◆ Milestone   
 ─ summary
