


North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	3	Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025				
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr				
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr				
N. Maple Street (S-131) Extension Project Update 6-1-2023					06-Mar-23 A	06-Mar-25																												
Milestones					06-Mar-23 A	06-Mar-25																												
Contractual Dates					06-Mar-23 A	06-Mar-25																												
MS.CD.	Project Commencement	100%	06-Mar-23 A		Project Commencement, 06-Mar-23 A																													
MS.CD.	Project Duration	11.89%	06-Mar-23 A	06-Mar-25	Project D																													
MS.CD.	Project Completion	0%		06-Mar-25*	Project C																													
Key Milestones					30-Oct-24	06-Mar-25																												
MS.KM.	Completion of Storm Drain	0%		06-Nov-24	Completion of Storm Drain,																													
MS.KM.	Completion of Pavement	0%		30-Oct-24	Completion of Pavement,																													
MS.KM.	Completion of Road Marking & Signs	0%		06-Mar-25	Complet																													
Preliminaries					06-Mar-23 A	22-May-23																												
Important Contract Deliverables					06-Mar-23 A	31-Mar-23																												
PR.CD.(Submission of Performance Bond & Insurance	100%	06-Mar-23 A	17-Mar-23	Submission of Performance Bond & Insurance,																													
PR.CD.(Prepare & Submit CPM Progress Schedule	100%	06-Mar-23 A	31-Mar-23	Prepare & Submit CPM Progress Schedule,																													
Mobilization					06-Mar-23 A	22-May-23																												
PR.MO.	Mobilization Site Office & Other Facilities Roadway Works Zone 01	100%	06-Mar-23 A	29-Mar-23	Mobilization Site Office & Other Facilities Roadway Works Zone 01																													
PR.MO.	Mobilization Site Office & Other Facilities Roadway Works Zone 02	100%	30-Mar-23 A	25-Apr-23 A	Mobilization Site Office & Other Facilities Roadway Works Zone 02																													
PR.MO.	Mobilization Site Office & Other Facilities Roadway Works Zone 03	100%	26-Apr-23 A	22-May-23	Mobilization Site Office & Other Facilities Roadway Works Zone 03																													
NOCs & Permits					06-Mar-23 A	06-Mar-23																												
PR.NO.(Receipt of All Construction NOCs & Permits Zone 01 (by Others)	100%		06-Mar-23	Receipt of All Construction NOCs & Permits Zone 01 (by Others),																													
Possession of Site					06-Mar-23 A	06-Mar-23																												
PR.PS.(Possession of Site - Complete ROW Zone 01 (by Others)	100%	06-Mar-23 A	06-Mar-23	Possession of Site - Complete ROW Zone 01 (by Others)																													
PR.PS.(Possession of Site - Complete ROW Zone 02 (by Others)	100%	06-Mar-23 A	06-Mar-23	Possession of Site - Complete ROW Zone 02 (by Others)																													
PR.PS.(Possession of Site - Complete ROW Zone 03 (by Others)	100%	06-Mar-23 A	06-Mar-23	Possession of Site - Complete ROW Zone 03 (by Others)																													
Initial Survey Works					06-Mar-23 A	31-Mar-23																												
PR.IS.C	Receipt of Survey Control Points	100%	06-Mar-23 A	06-Mar-23	Receipt of Survey Control Points																													
PR.IS.C	Initial Survey/Layout/Calculations	100%	07-Mar-23 A	31-Mar-23	Initial Survey/Layout/Calculations																													
Initial Traffic Diversion Works					06-Mar-23 A	31-Mar-23																												
PR.TD.(Detours/Closures for Clearing of Roadway	100%	06-Mar-23 A	31-Mar-23	Detours/Closures for Clearing of Roadway																													
Bat Moratorium					01-Apr-23 A	15-May-23																												
A1000	Bat Moratorium	100%	01-Apr-23 A	15-May-23	Bat Moratorium																													
Construction					03-Apr-23 A	03-Mar-25																												
Utilities by Others					01-May-23 A	27-Nov-23																												
GN.UT.(AT&T Communication Relocation	0%	01-Jun-23	27-Nov-23	AT&T Communication Relocation																													
GN.UT.(Spectrum Communication Relocation	0%	01-Jun-23	27-Nov-23	Spectrum Communication Relocation																													
GN.UT.(Segra Communication Relocation	100%	01-May-23 A	31-May-23	Segra Communication Relocation																													
GN.UT.(Dominion Energy Natural Gas Relocation	0%	01-Jun-23	27-Nov-23	Dominion Energy Natural Gas Relocation																													
Zone 01					03-Apr-23 A	29-Nov-24																												
Detailed Surveying Works					03-Apr-23 A	11-Apr-23 A																												

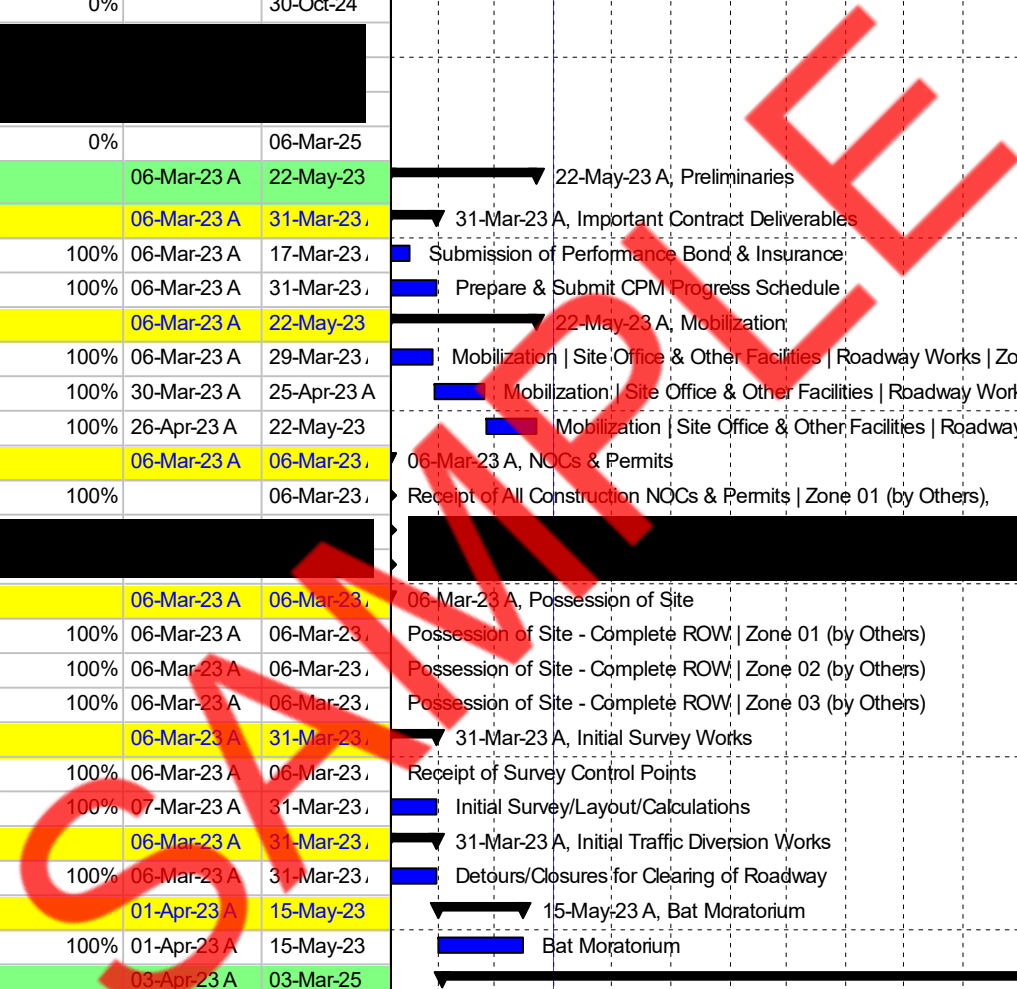


█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ▾ summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	3	Qtr 2, 2023		Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025				
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr		
Z1.GN	Detailed Survey Works (Stakes, Lines, & Grades) Zone 01	100%	03-Apr-23 A	11-Apr-23 A		Detailed Survey Works (Stakes, Lines, & Grades) Zone 01																											
SECTION 5 (Secondary/Parsons) [1,500 LF]						30-Oct-24, SECTION 5 (Secondary/Parsons) [1,500 LF]																											
Traffic Diversion/Management Works						24-Apr-23 A, Traffic Diversion/Management Works																											
Z1.S5	Traffic Diversion Works Zone 01 Section 5	100%	12-Apr-23 A	18-Apr-23 A		Traffic Diversion Works Zone 01 Section 5																											
Z1.S5	Install Construction Signs for Road Closure Zone 01 Section 5	100%	19-Apr-23 A	24-Apr-23 A		Install Construction Signs for Road Closure Zone 01 Section 5																											
Demolitions & Site Clearance						01-May-23 A, Demolitions & Site Clearance																											
Z1.S5	General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 5	100%	25-Apr-23 A	01-May-23		General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 5																											
Earthworks						05-Jul-23, Earthworks																											
Z1.S5	Earthworks to Formation Zone 01 Section 5	50%	02-May-23 A	05-Jul-23		Earthworks to Formation Zone 01 Section 5																											
Storm Drain Works						01-Sep-23, Storm Drain Works																											
Z1.S5	Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Sec	0%	27-Jul-23	02-Aug-23		Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Section 5																											
Z1.S5	Laying of Storm Drains Pipes Zone 01 Section 5	0%	03-Aug-23	10-Aug-23		Laying of Storm Drains Pipes Zone 01 Section 5																											
Z1.S5	Piping Accessories for Storm Drains Zone 01 Section 5	0%	11-Aug-23	22-Aug-23		Piping Accessories for Storm Drains Zone 01 Section 5																											
Pavement Construction						18-Sep-23, Pavement Construction																											
Z1.S5	HMA Formation Preparation Zone 01 Section 5	0%	18-Sep-23	27-Sep-23		HMA Formation Preparation Zone 01 Section 5																											
Z1.S5	Furnish Hot Mix Asphalt Base Course Zone 01 Section 5	0%	21-Sep-23	04-Oct-23		Furnish Hot Mix Asphalt Base Course Zone 01 Section 5																											
Z1.S5	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 01 Section 5	0%	29-Sep-23	10-Oct-23		Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 01 Section 5																											
Z1.S5	Furnish Hot Mix Asphalt Intermediate Course Zone 01 Section 5	0%	05-Oct-23	23-Oct-23		Furnish Hot Mix Asphalt Intermediate Course Zone 01 Section 5																											
Z1.S5	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	16-Oct-24	21-Oct-24		Furnish Liquid Binder (between Intern																											
Z1.S5	Furnish Hot Mix Asphalt Surface Course Zone 01 Section 5	0%	24-Oct-24	30-Oct-24		Furnish Hot Mix Asphalt Surface Co																											
SECTION 1 (New Parsons) [800 LF]						01-Dec-23, SECTION 1 (New Parsons) [800 LF]																											
Traffic Diversion/Management Works						01-May-23 A, Traffic Diversion/Management Works																											
Z1.S1	Traffic Diversion Works Zone 01 Section 1	100%	19-Apr-23 A	25-Apr-23 A		Traffic Diversion Works Zone 01 Section 1																											
Z1.S1	Install Construction Signs for Road Closure Zone 01 Section 1	100%	26-Apr-23 A	01-May-23		Install Construction Signs for Road Closure Zone 01 Section 1																											
Demolitions & Site Clearance						11-May-23 A, Demolitions & Site Clearance																											
Z1.S1	General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 1	100%	02-May-23 A	11-May-23		General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 1																											
Earthworks						14-Jul-23, Earthworks																											
Z1.S1	Earthworks to Formation Zone 01 Section 1	0%	09-Jun-23	14-Jul-23		Earthworks to Formation Zone 01 Section 1																											
Storm Drain Works						04-Oct-23, Storm Drain Works																											
Z1.S1	Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Sec	0%	05-Sep-23	11-Sep-23		Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Section 1																											
Z1.S1	Laying of Storm Drains Pipes Zone 01 Section 1	0%	12-Sep-23	20-Sep-23		Laying of Storm Drains Pipes Zone 01 Section 1																											
Z1.S1	Piping Accessories for Storm Drains Zone 01 Section 1	0%	21-Sep-23	27-Sep-23		Piping Accessories for Storm Drains Zone 01 Section 1																											
Z1.S1	Installation of Catch Basins & Manholes Zone 01 Section 1	0%	21-Sep-23	29-Sep-23		Installation of Catch Basins & Manholes Zone 01 Section 1																											
Z1.S1	Filling over Pipes Zone 01 Section 1	0%	28-Sep-23	04-Oct-23		Filling over Pipes Zone 01 Section 1																											
Pavement Construction						01-Dec-23, Pavement Construction																											
Z1.S1	HMA Formation Preparation Zone 01 Section 1	0%	18-Sep-23	27-Sep-23		HMA Formation Preparation Zone 01 Section 1																											
Z1.S1	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	28-Nov-23	29-Nov-23		Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Milling Zone 01 Section 1																											
Z1.S1	Furnish Hot Mix Asphalt Surface Course Zone 01 Section 1	0%	30-Nov-23	01-Dec-23		Furnish Hot Mix Asphalt Surface Course Zone 01 Section 1																											
SECTION 7 (Richardson Road) [1,400 LF]						14-Feb-24, SECTION 7 (Richardson Road) [1,400 LF]																											
Traffic Diversion/Management Works						08-May-23 A, Traffic Diversion/Management Works																											
Z1.S7	Traffic Diversion Works Zone 01 Section 7	100%	26-Apr-23 A	02-May-23		Traffic Diversion Works Zone 01 Section 7																											
Z1.S7	Install Construction Signs for Road Closure Zone 01 Section 7	100%	03-May-23 A	08-May-23		Install Construction Signs for Road Closure Zone 01 Section 7																											
Demolitions & Site Clearance						31-May-23 A, Demolitions & Site Clearance																											
Z1.S7	General Site Clearance Cleaning & Grubbing within Roadway Zone 01 Section 7	100%	09-May-23 A	18-May-23		General Site Clearance Cleaning & Grubbing within Roadway Zone 01 Section 7																											
Z1.S7	General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 7	100%	12-May-23 A	31-May-23		General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 7																											

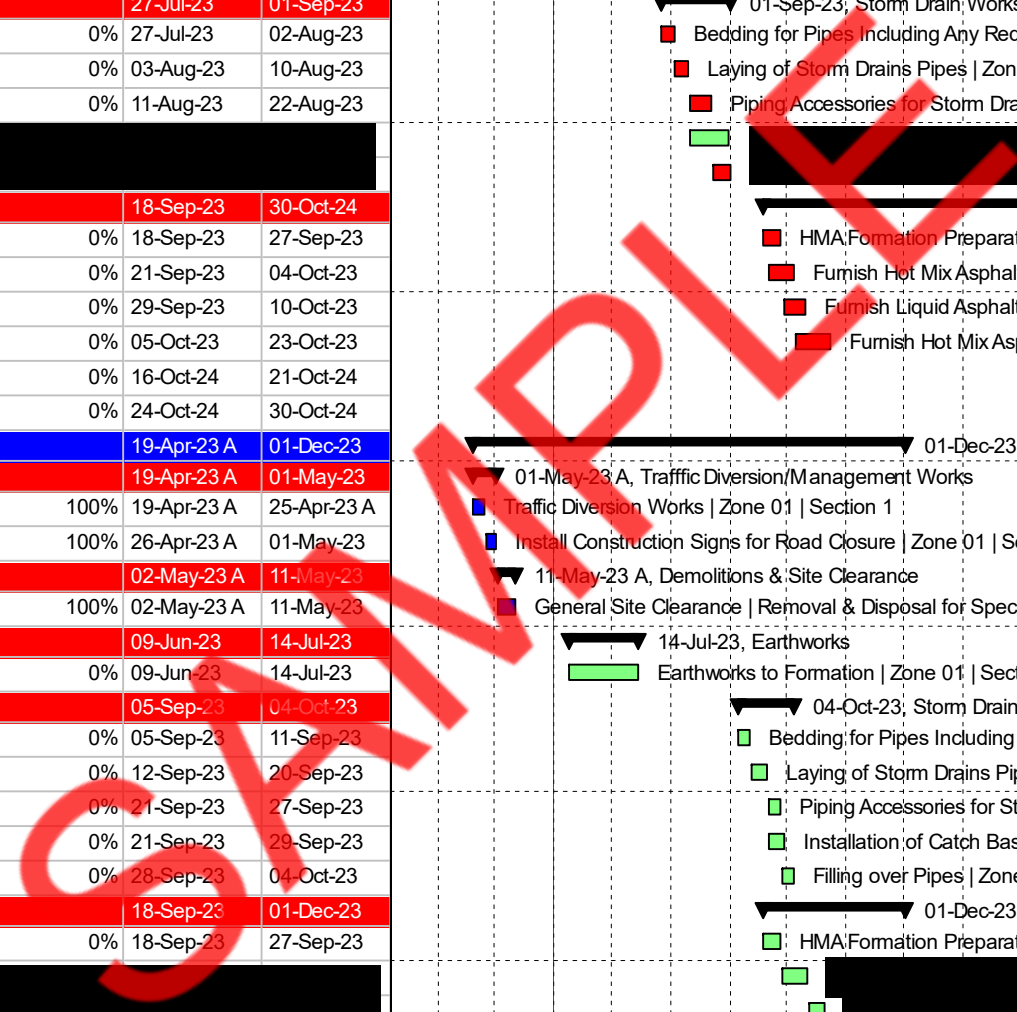

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ── summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	3	Qtr 2, 2023		Qtr 3, 2023		Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025						
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr			
Earthworks																																		
Z1.S7	Earthworks to Formation Zone 01 Section 7	0%	05-Oct-23	15-Nov-23																														
Storm Drain Works																																		
Z1.S7	Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Sec	0%	16-Nov-23	18-Dec-23																														
Z1.S7	Filling over Pipes Zone 01 Section 7	0%	12-Dec-23	18-Dec-23																														
Pavement Construction																																		
Z1.S7	HMA Formation Preparation Zone 01 Section 7	0%	19-Dec-23	29-Dec-23																														
Z1.S7	Furnish Hot Mix Asphalt Base Course Zone 01 Section 7	0%	22-Dec-23	16-Jan-24																														
Z1.S7	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 01 Section 7	0%	10-Jan-24	19-Jan-24																														
Z1.S7	Furnish Hot Mix Asphalt Intermediate Course Zone 01 Section 7	0%	17-Jan-24	01-Feb-24																														
Z1.S7	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	31-Jan-24	05-Feb-24																														
Z1.S7	Furnish Hot Mix Asphalt Surface Course Zone 01 Section 7	0%	08-Feb-24	14-Feb-24																														
SECTION 6 (Railroad Tie-In) [600 LF]																																		
Traffic Diversion/Management Works																																		
Z1.S6	Traffic Diversion Works Zone 01 Section 6	100%	08-May-24 A	20-May-24																														
Z1.S6	Install Construction Signs for Road Closure Zone 01 Section 6	100%	15-May-24 A	20-May-24																														
Demolitions & Site Clearance																																		
Z1.S6	General Site Clearance Removal & Disposal for Specific Items Zone 01 Section 6	100%	21-May-24 A	31-May-24																														
Earthworks																																		
Z1.S6	Earthworks to Formation Zone 01 Section 6	0%	08-Jun-23	29-Jun-23																														
Storm Drain Works																																		
Z1.S6	Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Sec	0%	12-Sep-23	18-Sep-23																														
Z1.S6	Filling over Pipes Zone 01 Section 6	0%	21-Dec-23	28-Dec-23																														
Pavement Construction																																		
Z1.S6	HMA Formation Preparation Zone 01 Section 6	0%	29-Dec-23	10-Jan-24																														
Z1.S6	Furnish Hot Mix Asphalt Base Course Zone 01 Section 6	0%	17-Jan-24	26-Jan-24																														
Z1.S6	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 01 Section 6	0%	23-Jan-24	31-Jan-24																														
Z1.S6	Furnish Hot Mix Asphalt Intermediate Course Zone 01 Section 6	0%	02-Feb-24	13-Feb-24																														
Z1.S6	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	14-Feb-24	15-Feb-24																														
Z1.S6	Furnish Hot Mix Asphalt Surface Course Zone 01 Section 6	0%	21-Feb-24	22-Feb-24																														
Tie-Ins with Existing Roads																																		
Traffic Diversion/Management Works																																		
Z1.TI	Traffic Diversion Works Zone 01 Tie-In	100%	12-Apr-23 A	18-Apr-23 A																														
Z1.TI	Install Construction Signs for Road Closure Zone 01 Tie-In	100%	19-Apr-23 A	24-Apr-23 A																														
Demolitions & Site Clearance																																		
Z1.TI	General Site Clearance Removal & Disposal for Specific Items Zone 01 Tie-In	100%	25-Apr-23 A	04-May-23																														
Earthworks																																		
Z1.TI	Earthworks to Formation Zone 01 Tie-In	0%	01-Jun-23	22-Jun-23																														
Storm Drain Works																																		
Z1.TI	Bedding for Pipes Including Any Required Additional Foundation Works Zone 01 Tie-	0%	24-Nov-23	30-Nov-23																														
Z1.TI	Laying of Storm Drains Pipes Zone 01 Tie-In	0%	01-Dec-23	11-Dec-23																														


SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ▼ summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	2023												2024			2025								
					Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025		
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
Z1.TI	Filling over Pipes Zone 01 Tie-In	0%	19-Dec-23	26-Dec-23																								
Pavement Construction					27-Dec-23	26-Feb-24																						
Z1.TI	HMA Formation Preparation Zone 01 Tie-In	0%	27-Dec-23	03-Jan-24																								
Z1.TI	Furnish Hot Mix Asphalt Base Course Zone 01 Tie-In	0%	02-Jan-24	08-Jan-24																								
Z1.TI	Furnish Hot Mix Asphalt Surface Course Zone 01 Tie-In	0%	23-Feb-24	26-Feb-24																								
Erosion Maintenance					16-Nov-23	03-May-24																						
Z1.GN	Erosion Maintenance Activities Zone 01	0%	16-Nov-23	03-May-24																								
Sidewalk Works					06-May-24	24-May-24																						
Z1.GN	Pouring Concrete for Curb & Gutter Zone 01	0%	06-May-24	10-May-24																								
Z1.GN	Pouring Concrete for Sidewalk Zone 01	0%	13-May-24	17-May-24																								
Z1.GN	Pouring Concrete for Pedestrian Ramp Zone 01	0%	20-May-24	24-May-24																								
Final Concrete					31-Oct-24	21-Nov-24																						
Z1.GN	Pouring Concrete for Driveway Zone 01	0%	31-Oct-24	06-Nov-24																								
Z1.GN	Pouring Concrete for Median Zone 01	0%	07-Nov-24	14-Nov-24																								
Z1.GN	Installation of Roadway Detectable Wearing Material Zone 01	0%	15-Nov-24	21-Nov-24																								
Traffic Signals Works					22-Nov-24	29-Nov-24																						
Z1.GN	Furnish & Install Final Traffic Signals Items (Poles & Cameras) Zone 01	0%	22-Nov-24	29-Nov-24																								
Zone 02					26-Apr-23 A	20-Dec-24																						
Detailed Surveying Works					26-Apr-23 A	15-May-23																						
Z2.GN	Detailed Survey Works (Stakes, Lines, & Grades) Zone 02	100%	26-Apr-23 A	15-May-23																								
SECTION 2 (South of US-78) [1,800 LF]					16-May-23 A	20-Mar-24																						
Traffic Diversion/Management Works					16-May-23 A	26-May-23																						
Z2.S2	Traffic Diversion Works Zone 02 Section 2	100%	16-May-23 A	22-May-23																								
Z2.S2	Install Construction Signs for Road Closure Zone 02 Section 2	100%	23-May-23 A	26-May-23																								
Earthworks					23-Jun-23	14-Jul-23																						
Z2.S2	Earthworks to Formation Zone 02 Section 2	0%	23-Jun-23	14-Jul-23																								
Storm Drain Works					27-Dec-23	14-Mar-24																						
Z2.S2	Removal & Disposal of Existing Pavement Zone 02 Section 2	0%	27-Dec-23	11-Jan-24																								
Z2.S2	Installation of Catch Basins & Manholes Zone 02 Section 2	0%	16-Feb-24	12-Mar-24																								
Z2.S2	Filling over Pipes Zone 02 Section 2	0%	04-Mar-24	14-Mar-24																								
Pavement Construction					24-Jan-24	20-Mar-24																						
Z2.S2	HMA Formation Preparation Zone 02 Section 2	0%	24-Jan-24	02-Feb-24																								
Z2.S2	Furnish Hot Mix Asphalt Base Course Zone 02 Section 2	0%	29-Jan-24	16-Feb-24																								
Z2.S2	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 02 Section 2	0%	13-Feb-24	22-Feb-24																								
Z2.S2	Furnish Hot Mix Asphalt Intermediate Course Zone 02 Section 2	0%	20-Feb-24	06-Mar-24																								
SECTION 4 (Secondary/US-78) [2,200 LF]					23-May-23 A	05-Jun-24																						
Traffic Diversion/Management Works					23-May-23 A	31-May-23																						
Z2.S4	Traffic Diversion Works Zone 02 Section 4	100%	23-May-23 A	29-May-23																								
Z2.S4	Install Construction Signs for Road Closure Zone 02 Section 4	100%	30-May-23 A	31-May-23																								
Demolitions & Site Clearance					01-Jun-23	12-Jun-23																						
Z2.S4	General Site Clearance Cleaning & Grubbing within Roadway Zone 02 Section 4	0%	01-Jun-23	12-Jun-23																								
Earthworks					17-Jul-23	04-Aug-23																						

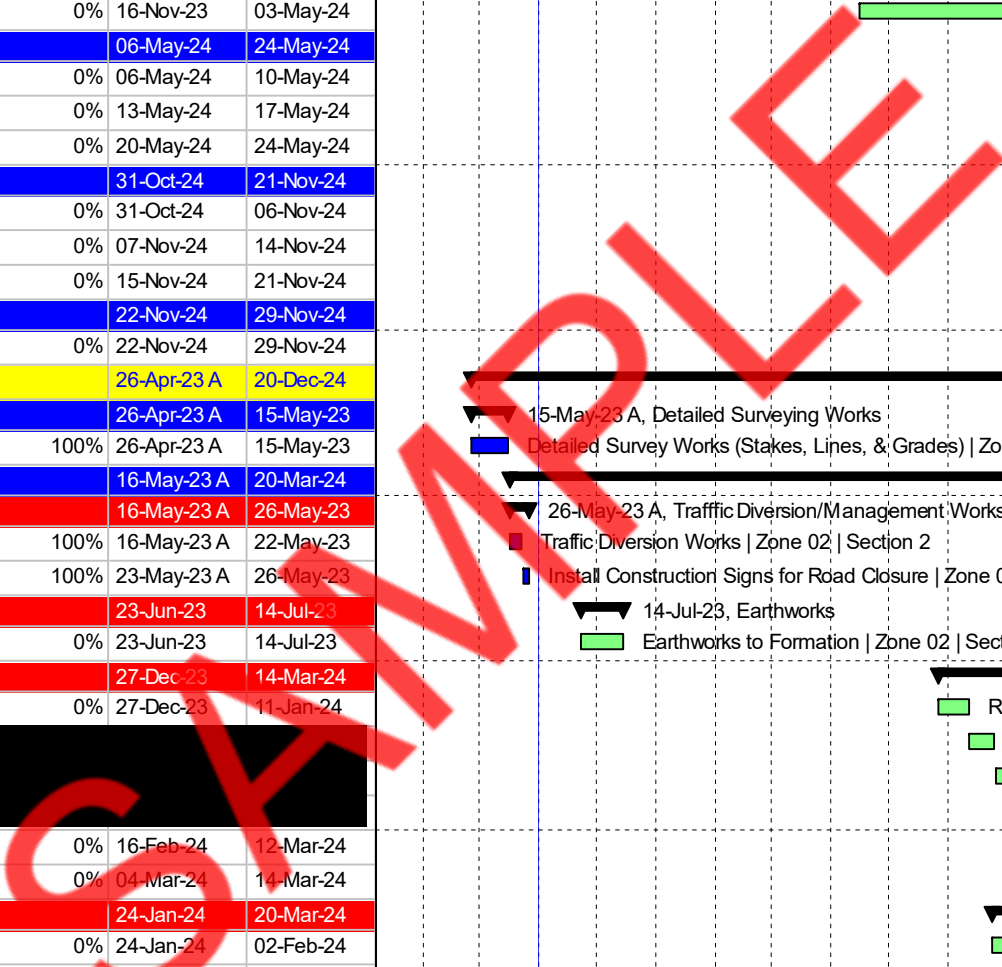


■ Actual Level of Effort ■ Remaining Work ◆ Milestone
■ Actual Work ■ Critical Remaining Work ▶ summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	2023																									
					Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025	
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
Z2.S4	Earthworks to Formation Zone 02 Section 4	0%	17-Jul-23	04-Aug-23																										
Storm Drain Works					15-Mar-24	05-Jun-24																								
Z2.S4	Removal & Disposal of Existing Pavement Zone 02 Section 4	0%	15-Mar-24	01-Apr-24																										
Z2.S4	Bedding for Pipes Including Any Required Additional Foundation Works Zone 02 Sec	0%	02-Apr-24	16-Apr-24																										
Z2.S4	Filling over Pipes Zone 02 Section 4	0%	23-May-24	05-Jun-24																										
Pavement Construction					07-Mar-24	16-May-24																								
Z2.S4	HMA Formation Preparation Zone 02 Section 4	0%	07-Mar-24	18-Mar-24																										
Z2.S4	Furnish Hot Mix Asphalt Base Course Zone 02 Section 4	0%	12-Mar-24	10-Apr-24																										
Z2.S4	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 02 Section 4	0%	05-Apr-24	15-Apr-24																										
Z2.S4	Furnish Hot Mix Asphalt Intermediate Course Zone 02 Section 4	0%	11-Apr-24	30-Apr-24																										
Z2.S4	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	01-May-24	02-May-24																										
Z2.S4	Furnish Hot Mix Asphalt Surface Course Zone 02 Section 4	0%	07-May-24	16-May-24																										
Tie-Ins with Existing Roads					30-May-23 A	08-Jul-24																								
Traffic Diversion/Management Works					30-May-23 A	31-May-23																								
Z2.TI	Traffic Diversion Works Zone 02 Tie-In	100%	30-May-23 A	31-May-23																										
Z2.TI	Install Construction Signs for Road Closure Zone 02 Tie-In	100%	30-May-23 A	31-May-23																										
Earthworks					07-Aug-23	25-Aug-23																								
Z2.TI	Earthworks to Formation Zone 02 Tie-In	0%	07-Aug-23	25-Aug-23																										
Storm Drain Works					06-Jun-24	08-Jul-24																								
Z2.TI	Removal & Disposal of Existing Pavement Zone 02 Tie-In	0%	06-Jun-24	10-Jun-24																										
Z2.TI	Bedding for Pipes Including Any Required Additional Foundation Works Zone 02 Tie-	0%	11-Jun-24	14-Jun-24																										
Z2.TI	Laying of Storm Drains Pipes Zone 02 Tie-In	0%	17-Jun-24	25-Jun-24																										
Pavement Construction					01-May-24	05-Jun-24																								
Z2.TI	HMA Formation Preparation Zone 02 Tie-In	0%	01-May-24	10-May-24																										
Z2.TI	Furnish Hot Mix Asphalt Base Course Zone 02 Tie-In	0%	06-May-24	15-May-24																										
Z2.TI	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 02 Tie-In	0%	10-May-24	20-May-24																										
Z2.TI	Furnish Hot Mix Asphalt Intermediate Course Zone 02 Tie-In	0%	16-May-24	28-May-24																										
Z2.TI	Furnish Liquid Binder (between Intermediate & Surface) & Milling Existing Asphalt Millin	0%	24-May-24	30-May-24																										
Z2.TI	Furnish Hot Mix Asphalt Surface Course Zone 02 Tie-In	0%	04-Jun-24	05-Jun-24																										
Erosion Maintenance					06-May-24	26-Sep-24																								
Z2.GN	Erosion Maintenance Activities Zone 02	0%	06-May-24	26-Sep-24																										
Sidewalk Works					27-Sep-24	18-Oct-24																								
Z2.GN	Pouring Concrete for Curb & Gutter Zone 02	0%	27-Sep-24	03-Oct-24																										
Z2.GN	Pouring Concrete for Sidewalk Zone 02	0%	04-Oct-24	10-Oct-24																										
Z2.GN	Pouring Concrete for Pedestrian Ramp Zone 02	0%	11-Oct-24	18-Oct-24																										
Final Concrete					07-Nov-24	29-Nov-24																								
Z2.GN	Pouring Concrete for Driveway Zone 02	0%	07-Nov-24	14-Nov-24																										
Z2.GN	Pouring Concrete for Median Zone 02	0%	15-Nov-24	21-Nov-24																										
Z2.GN	Installation of Roadway Detectable Wearing Material Zone 02	0%	22-Nov-24	29-Nov-24																										
Traffic Signals Works					02-Dec-24	20-Dec-24																								
Z2.GN	Install Video Detection System Including Lead-In Zone 02	0%	02-Dec-24	06-Dec-24																										

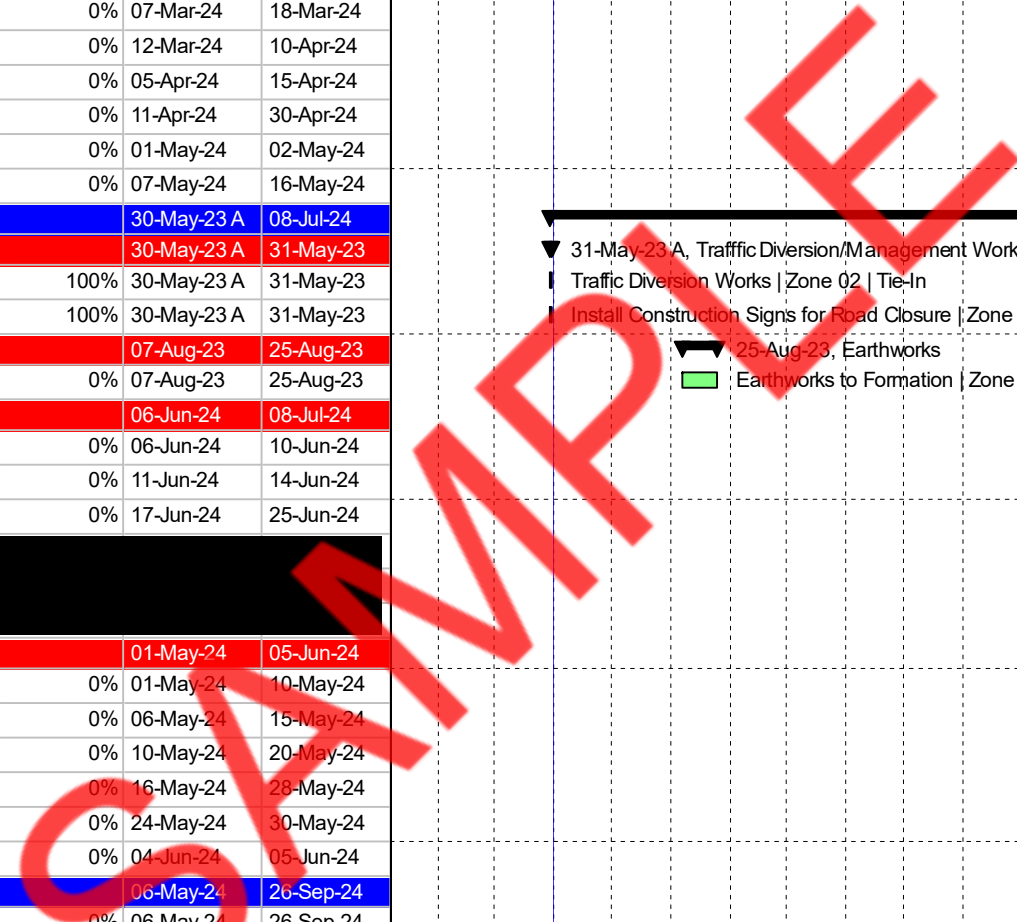

█ Actual Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	2023		Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025			
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr				
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr				
Zone 03					23-May-23 A	24-Feb-25																												
Detailed Surveying Works					23-May-23 A	31-May-23																												
Z3.GN	Detailed Survey Works (Stakes, Lines, & Grades) Zone 03	100%	23-May-23 A	31-May-23																														
SECTION 2 (North of US-78) [2,900 LF]					29-May-23 A	09-Jan-25																												
Traffic Diversion/Management Works					29-May-23 A	31-May-23																												
Z3.S3	Traffic Diversion Works Zone 03 Section 3	100%	29-May-23 A	31-May-23																														
Z3.S3	Install Construction Signs for Road Closure Zone 03 Section 3	100%	30-May-23 A	31-May-23																														
Demolitions & Site Clearance					01-Jun-23	12-Jun-23																												
Z3.S3	General Site Clearance Removal & Disposal for Specific Items Zone 03 Section 3	0%	01-Jun-23	12-Jun-23																														
Earthworks					28-Aug-23	18-Sep-23																												
Z3.S3	Earthworks to Formation Zone 03 Section 3	0%	28-Aug-23	18-Sep-23																														
Storm Drain Works					09-Jul-24	07-Oct-24																												
Z3.S3	Removal & Disposal of Existing Pavement Zone 03 Section 3	0%	09-Jul-24	29-Jul-24																														
Z3.S3	Installation of Catch Basins & Manholes Zone 03 Section 3	0%	11-Sep-24	04-Oct-24																														
Z3.S3	Filling over Pipes Zone 03 Section 3	0%	25-Sep-24	07-Oct-24																														
Force Main Works					08-Oct-24	04-Dec-24																												
Z3.S3	Install Steel Casing for Force Main Pipes Zone 03 Section 3	0%	08-Oct-24	22-Oct-24																														
Z3.S3	Laying of Force Main PVC Pipes Zone 03 Section 3	0%	23-Oct-24	12-Nov-24																														
Z3.S3	Piping Accessories for Force Main Zone 03 Section 3	0%	13-Nov-24	26-Nov-24																														
Z3.S3	Connection to Existing Force Main Network & Manholes Zone 03 Section 3	0%	27-Nov-24	04-Dec-24																														
Gravity Sewer Works					08-Oct-24	09-Jan-25																												
Z3.S3	Laying of Gravity Sewer PVC Pipes Zone 03 Section 3	0%	08-Oct-24	29-Oct-24																														
Z3.S3	Installation of Gravity Sewer Clean Outs Zone 03 Section 3	0%	30-Oct-24	05-Nov-24																														
Z3.S3	Trees Removal Zone 03 Section 3	0%	11-Dec-24	17-Dec-24																														
Z3.S3	SCDOT Road Pavement Cut & Repair Zone 03 Section 3	0%	18-Dec-24	23-Dec-24																														
Z3.S3	Traffic Control Zone 03 Section 3	0%	24-Dec-24	31-Dec-24																														
Z3.S3	Soil Compaction Testing Zone 03 Section 3	0%	02-Jan-25	09-Jan-25																														
Pavement Construction					29-May-24	13-Aug-24																												
Z3.S3	HMA Formation Preparation Zone 03 Section 3	0%	29-May-24	11-Jun-24																														
Z3.S3	Furnish Hot Mix Asphalt Base Course Zone 03 Section 3	0%	03-Jun-24	09-Jul-24																														
Z3.S3	Furnish Liquid Asphalt Binder (between Base & Intermediate) Zone 03 Section 3	0%	01-Jul-24	12-Jul-24																														
Z3.S3	Furnish Hot Mix Asphalt Intermediate Course Zone 03 Section 3	0%	08-Jul-24	25-Jul-24																														
Tie-Ins with Existing Roads					01-Jun-23	14-Jan-25																												
Traffic Diversion/Management Works					01-Jun-23	13-Jun-23																												
Z3.TI	Traffic Diversion Works Zone 03 Tie-In	0%	01-Jun-23	07-Jun-23																														
Z3.TI	Install Construction Signs for Road Closure Zone 03 Tie-In	0%	08-Jun-23	13-Jun-23																														
Demolitions & Site Clearance					14-Jun-23	26-Jun-23																												
Z3.TI	General Site Clearance Removal & Disposal for Specific Items Zone 03 Tie-In	0%	14-Jun-23	26-Jun-23																														
Earthworks					19-Sep-23	10-Oct-23																												
Z3.TI	Earthworks to Formation Zone 03 Tie-In	0%	19-Sep-23	10-Oct-23																														
Storm Drain Works					08-Oct-24	06-Nov-24																												

SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ─── summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	2023												2024			2025											
					Qtr 2, 2023				Qtr 3, 2023				Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025		
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
Z3.GN	Progress Striping Fast Dry Paint for Curbs & Median Zone 03	0%	16-Dec-24	30-Dec-24																											
Z3.GN	Final Striping Pavement Marking & Signs for Roadway Zone 03	0%	31-Dec-24	13-Jan-25																											
Final Touches					16-Dec-24	03-Mar-25																									
Zone 1					16-Dec-24	18-Feb-25																									
Z1.GN	Furnish Geotextile For Erosion Control Under Rip-rap Zone 01	0%	16-Dec-24	26-Dec-24																											
Z1.GN	Furnish Rip-Rap Zone 01	0%	27-Dec-24	03-Jan-25																											
Z1.GN	Install Mailboxes Zone 01	0%	04-Feb-25	18-Feb-25																											
Zone 2					30-Dec-24	25-Feb-25																									
Z2.GN	Moving Items Zone 02	0%	30-Dec-24	06-Jan-25																											
Z2.GN	Furnish Geotextile For Erosion Control Under Rip-rap Zone 02	0%	07-Jan-25	13-Jan-25																											
Z2.GN	Furnish Rip-Rap Zone 02	0%	14-Jan-25	21-Jan-25																											
Z2.GN	Install Chain Link Fence Zone 02	0%	22-Jan-25	28-Jan-25																											
Z2.GN	Right of Way Marker, Plat & Permenent Cover Zone 02	0%	04-Feb-25	10-Feb-25																											
Z2.GN	Install Mailboxes Zone 02	0%	19-Feb-25	25-Feb-25																											
Zone 3					14-Jan-25	03-Mar-25																									
Z3.GN	Furnish Geotextile For Erosion Control Under Rip-rap Zone 03	0%	14-Jan-25	22-Jan-25																											
Z3.GN	Furnish Rip-Rap Zone 03	0%	23-Jan-25	30-Jan-25																											
Z3.GN	Install Chain Link Fence Zone 03	0%	31-Jan-25	07-Feb-25																											
Project Close-out					28-Aug-23	03-Mar-25																									
As-built Drawings					28-Aug-23	24-Feb-25																									
Zone 1					16-Nov-23	27-Jan-25																									
Road Profile					16-Nov-23	27-Dec-23																									
Z1.RD	Prepare/Submit As-built Drawings Road Profile Zone 01	0%	16-Nov-23	15-Dec-23																											
Z1.RD	Review/Approval of As-built Drawings Road Profile Zone 01	0%	18-Dec-23	27-Dec-23																											
Road Pavement					27-Feb-24	04-Apr-24																									
Z1.AE	Prepare/Submit As-built Drawings Road Pavement Zone 01	0%	27-Feb-24	26-Mar-24																											
Z1.AE	Review/Approval of As-built Drawings Road Pavement Zone 01	0%	27-Mar-24	04-Apr-24																											
Road Marking					16-Dec-24	27-Jan-25																									
Z1.AE	Prepare/Submit As-built Drawings Road Marking Zone 01	0%	16-Dec-24	15-Jan-25																											
Z1.AE	Review/Approval of As-built Drawings Road Marking Zone 01	0%	16-Jan-25	27-Jan-25																											
Road Signs					16-Dec-24	27-Jan-25																									
Z1.AE	Prepare/Submit As-built Drawings Road Signs Zone 01	0%	16-Dec-24	15-Jan-25																											
Z1.AE	Review/Approval of As-built Drawings Road Signs Zone 01	0%	16-Jan-25	27-Jan-25																											
Storm Drain					29-Dec-23	08-Feb-24																									
Z1.AE	Prepare/Submit As-built Drawings Storm Drain Network Zone 01	0%	29-Dec-23	30-Jan-24																											
Z1.AE	Review/Approval of As-built Drawings Storm Drain Network Zone 01	0%	31-Jan-24	08-Feb-24																											
Zone 2					28-Aug-23	07-Feb-25																									
Road Profile					28-Aug-23	05-Oct-23																									
Z2.RD	Prepare/Submit As-built Drawings Road Profile Zone 02	0%	28-Aug-23	26-Sep-23																											
Z2.RD	Review/Approval of As-built Drawings Road Profile Zone 02	0%	27-Sep-23	05-Oct-23																											
Road Pavement					06-Jun-24	17-Jul-24																									
Z2.AE	Prepare/Submit As-built Drawings Road Marking Zone 02	0%	30-Dec-24	29-Jan-25																											

SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ─── summary

North Maple Street Extension Project - Progress Schedule Update 6-1-2023



Activity ID	Activity Name	Activity % Complete	Start	Finish	3	Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			2025
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
Z2.AE	Review/Approval of As-built Drawings Road Marking Zone 02	0%	30-Jan-25	07-Feb-25																										
Road Signs																														
Z2.AE	Prepare/Submit As-built Drawings Road Signs Zone 02	0%	30-Dec-24	29-Jan-25																										
Z2.AE	Review/Approval of As-built Drawings Road Signs Zone 02	0%	30-Jan-25	07-Feb-25																										
Storm Drain																														
			09-Jul-24	15-Aug-24																										
Zone 3																														
Road Profile																														
Z3RD	Prepare/Submit As-built Drawings Road Profile Zone 03	0%	11-Oct-23	20-Nov-23																										
Z3RD	Review/Approval of As-built Drawings Road Profile Zone 03	0%	09-Nov-23	20-Nov-23																										
Road Pavement																														
Z3.AE	Prepare/Submit As-built Drawings Road Pavement Zone 03	0%	30-Aug-24	09-Oct-24																										
Z3.AE	Review/Approval of As-built Drawings Road Pavement Zone 03	0%	01-Oct-24	09-Oct-24																										
Road Marking																														
Z3.AE	Prepare/Submit As-built Drawings Road Marking Zone 03	0%	14-Jan-25	24-Feb-25																										
Z3.AE	Review/Approval of As-built Drawings Road Marking Zone 03	0%	13-Feb-25	24-Feb-25																										
Road Signs																														
Z3.AE	Prepare/Submit As-built Drawings Road Signs Zone 03	0%	14-Jan-25	12-Feb-25																										
Z3.AE	Review/Approval of As-built Drawings Road Signs Zone 03	0%	13-Feb-25	24-Feb-25																										
Storm Drain																														
			07-Nov-24	18-Dec-24																										
Force Main																														
Z3.AE	Prepare/Submit As-built Drawings Force Main Network Zone 03	0%	12-Dec-24	20-Dec-24																										
Z3.AE	Review/Approval of As-built Drawings Force Main Network Zone 03	0%	23-Dec-24	02-Jan-25																										
Gravity Sewer																														
Z3.AE	Prepare/Submit As-built Drawings Gravity Sewer Network Zone 03	0%	15-Jan-25	24-Jan-25																										
Z3.AE	Review/Approval of As-built Drawings Gravity Sewer Network Zone 03	0%	27-Jan-25	04-Feb-25																										
Handing Over																														
Z1.PC.C	Final Cleaning & Handing Over Zone 01	0%	28-Jan-25	05-Feb-25																										
Z2.PC.C	Final Cleaning & Handing Over Zone 02	0%	10-Feb-25	19-Feb-25																										
Z3.PC.C	Final Cleaning & Handing Over Zone 03	0%	25-Feb-25	28-Feb-25																										
TOC																														
TOC10	Application for Taking Over Certificate	0%	03-Mar-25	03-Mar-25																										

SAMPLE
