


iLovePDF

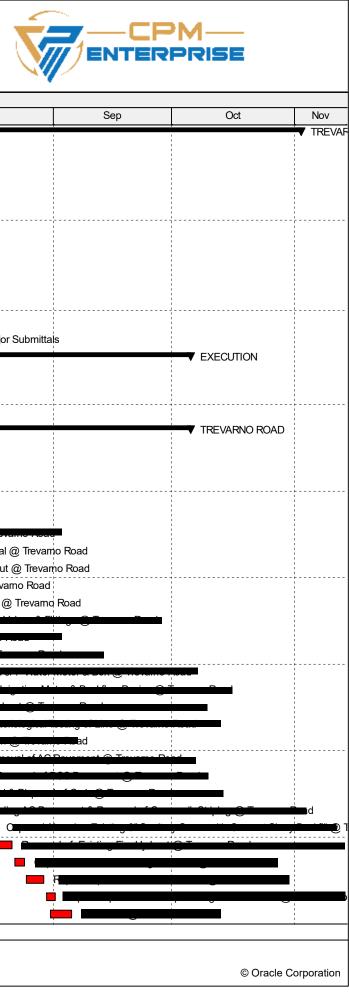

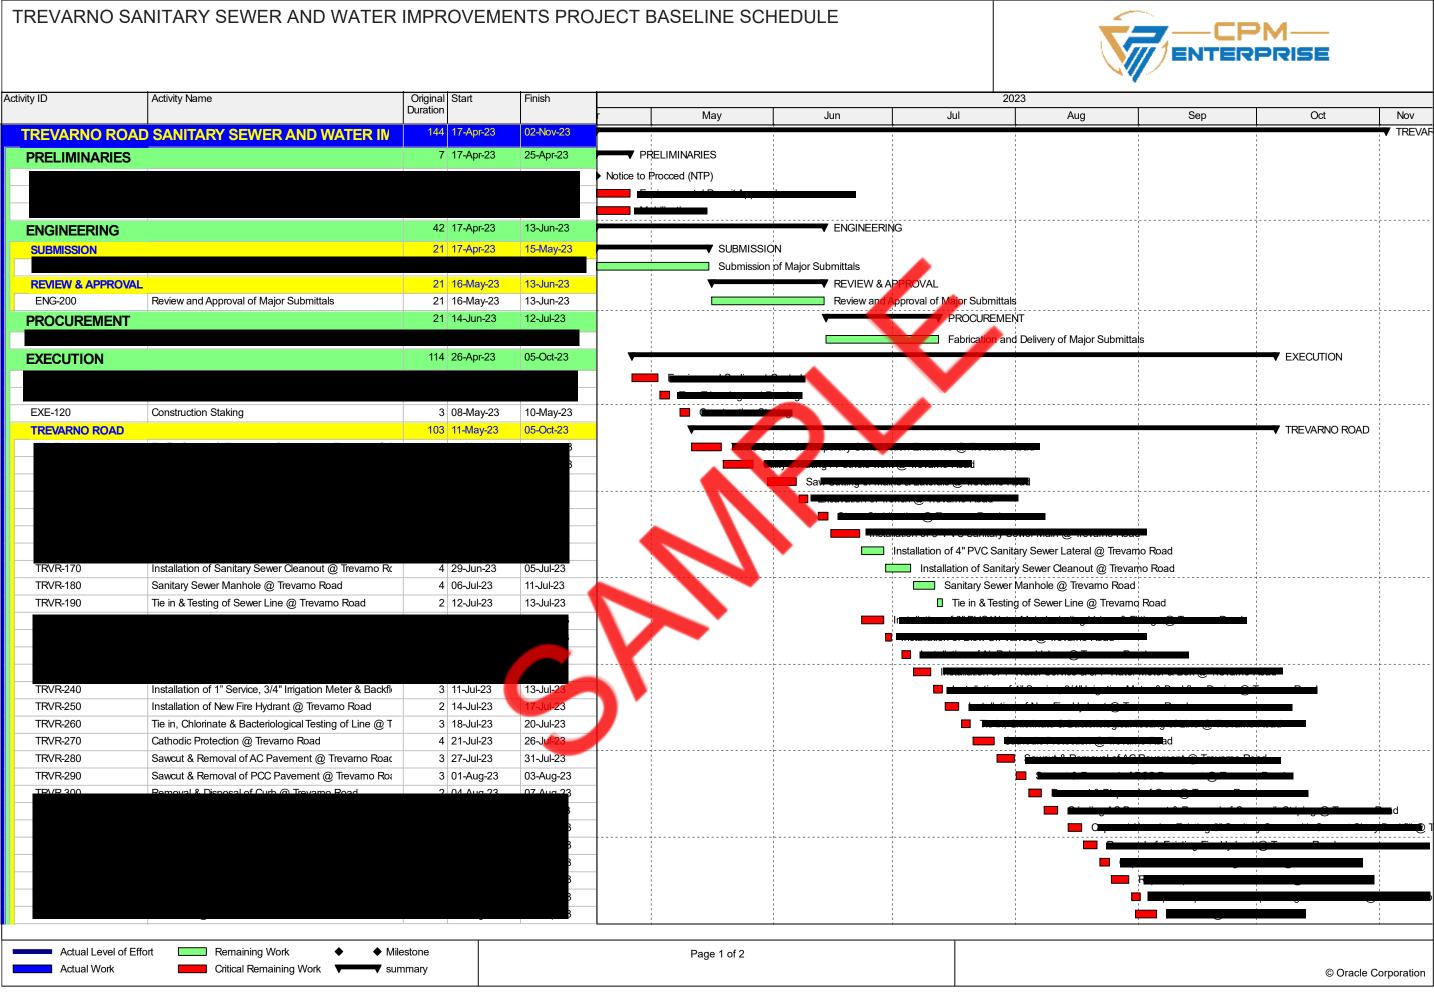

iLovePDF

TREVARNO SANITARY SEWER AND WATER IMPROVEMENTS PROJECT BASELINE SCHEDULE

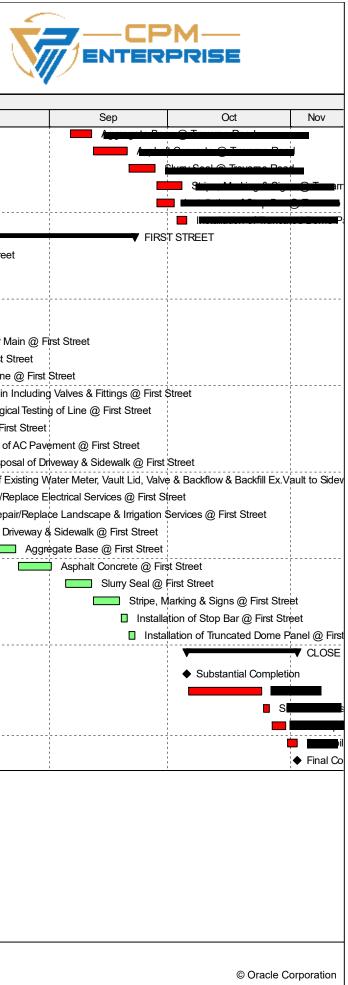

/ ID	Activity Name	Original Start	Finish		2023					
		Duration		r	Мау	Jun	Jul	Aug		
					,					
			8							
			8							
TRVR-410	Stripe, Marking & Signs @ Trevarno Road	5 28-Sep-23	04-Oct-23							
TRVR-420	Installation of Stop Bar @ Trevarno Road	3 28-Sep-23	02-Oct-23							
TRVR-430	Installation of Truncated Dome Panel @ Trevamo Roa	3 03-Oct-23	05-Oct-23							
FIRST STREET		76 07-Jun-23	22-Sep-23			V			_	
FSTR-100	Traffic Control & Temporary Construction Entrance @ I	3 07-Jun-23	09-Jun-23			Traffic Control	& Temporary Construction I	Entrance @ First Street		
ESTD 110	Litility Locating / Patholo work @ First Street	2 12 Jun 22	14 Jun 23			🔲 Utility Loc	ating / Pothole work @ First	t Street		
						🔲 Saw	Cutting of Mains & Laterals	@ First Street		
						📃 🗖	cavation of Trench @ First	Street		
F31K-140		3 23-Jun-23	27-Jun-25				Stone Stablization @ Firs	st Street		
FSTR-150	Installation of 8" PVC Sanitary Sewer Main @ First Str	6 28-Jun-23	06-Jul-23				Installation of 8"	VC Sanitary Sewer Main @	First {	
FSTR-160	Sanitary Sewer Manhole @ First Street	4 07-Jul-23	12-Jul-23					wer Manhole @ First Street		
							Tie in &	Testing of Sewer Line @ Fin	st Stre	
							Installation of	of 8" PVC Water Main Includ	ing Va	
							🥒 🛯 Tie in, Chl	orinate & Bacteriological Test	ting of	
FSTR-200	Cathodic Protection @ First Street	4 18-Jul-23	21-Jul-23				📃 🗖 Cath	nodic Protection @ First Stre	et	
FSTR-210	Sawcut & Removal of AC Pavement @ First Street	3 24-Jul-23	26-Jul-23					Sawcut & Removal of AC Pa	avęme	
FSTR-220	Removal & Disposal of Driveway & Sidewalk @ First Si	3 27-Jul-23	31-Jul-23					Removal & Disposal of	Drivev	
								Removal of Existing	, Wate	
								Repair/Replace	1	
0111200	nopann opiaco Landocapo a migation comoco (a, i m	0 10 10 20	117 49 20					Repair/Rep		
FSTR-260	Driveway & Sidewalk @ First Street	3 15-Aug-23	17-Aug-23	_				Driveway	y & Sir	
FSTR-270	Aggregate Base @ First Street	4 18-Aug-23	23-Aug-23	- (Ag		
FSTR-280	Asphalt Concrete @ First Street	7 24-Aug-23	01-Sep-23						Ξ Α	
FSTR-290	Slurry Seal @ First Street	5 05-Sep-23	11-Sep-23							
FSTR-300	Stripe, Marking & Signs @ First Street	5 12-Sep-23	18-Sep-23							
FSTR-310	Installation of Stop Bar @ First Street	2 19-Sep-23	20-Sep-23							
FSTR-320	Installation of Truncated Dome Panel @ First Street	2 21-Sep-23	22-Sep-23							
LOSE OUT		19 05-Oct-23	02-Nov-23							
~										
								1		

Actual Level of Effort	Remaining Work	•	♦ Milestone	Page 2 of 2	
Actual Work	Critical Remaining Work		summary		
