H.S QUEENS SCIENCE LAB UPGRADE

207-01 116TH AVENUE, QUEENS, NY 11411

PROJECT SCHEDULE



|) | Activity Name | Original Duration | Start | Finish | 2023 2024 |
|-------------|---|----------------------|------------------------|------------------------|--|
| OUEENO OC | NEVOE LAB LIBODADE | | 47.00 | 0 00 00 | Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb ▼ H.S. QUEENS SCIENCE LAB UPGRADE |
| | CIENCE LAB UPGRADE | 278 | Aug-17-22 | Sep-08-23 | |
| | Notice to Proceed (NTP) | 0 | Aug-17-22 | - 12.00 | ◆ Notice to Proceed (NTP) |
| BMITTALS | | 18 | Aug-18-22 | Sep-12-22 | SUBMITTALS Consul Requirements |
| | | | | | General Requirements |
| | | | | | Shop Drawings |
| | | | | | Project Organization Chart |
| | | | | | Safe Work Plans (SWP) |
| | Dust Control Work Plan | 5 | Aug-26-22 | Sep-01-22 | Dust Control Work Plan |
| | Concrete | 6 | Aug-18-22 | Aug-25-22 | ■ Concrete |
| | Paint | 6 | Aug-18-22 | Aug-25-22 | ■ Paint |
| | Ceiling | 6 | Aug-18-22 | Aug-25-22 | ■ Ceiling |
| | Flooring | 6 | Aug-18-22 | Aug-25-22 | ■ Flooring |
| JB-190 | Furniture & Equipment | 6 | Aug-18-22 | Aug-25-22 | ■ Furniture & Equipment |
| JB-200 | Mechanical Duct, Valves, Hangers and Supports | 7 | Aug-26-22 | Sep-05-22 | Mechanical Duct, Valves, Hangers and Supports |
| JB-210 | Cold and Hot Water Piping - Hangers and Supports | 7 | Aug-26-22 | Sep-05-22 | Cold and Hot Water Piping - Hangers and Supports |
| JB-220 | Plumbing Fixtures, Water Heaters, Ice Maker | 7 | Aug-31-22 | Sep-08-22 | ■ Plumbing Fixtures, Water Heaters, Ice Maker |
| JB-230 | Leviton Duplex Receptacle | 7 | Aug-31-22 | Sep-08-22 | Leviton Duplex Receptacle |
| JB-240 | Wiring Systems Affidavit & Schedule | 7 | Aug-31-22 | Sep-08-22 | ■ Wiring Systems Affidavit & Schedule |
| JB-250 | Raceways Affidavit & Schedule | 7 | Aug-31-22 | Sep-08-22 | Raceways Affi <mark>dav</mark> it & Schedule |
| | DOB Electrical Permit | 7 | Aug-31-22 | Sep-08-22 | DOB Electrical Permit |
| | SAF Form | 7 | Aug-31-22 | Sep-08-22 | ■ SAF Form |
| | Louvers, Curb & Flashing | 7 | Aug-24-22 | Sep-01-22 | Louvers, Curb & Flashing |
| | Wall Mounted Boards | 7 | Aug-24-22 | Sep-01-22 | ■ Wall Mounted Boards |
| | Windows | 7 | Sep-02-22 | Sep-12-22 | Windows |
| | Doors | 7 | Sep-02-22 | Sep-12-22 Sep-12-22 | Doors |
| | Lights & Lighting Fixtures | 7 | Sep-02-22 Sep-02-22 | Sep-12-22 Sep-12-22 | Lights & Lighting Fixtures |
| | | , | · | | Alarm Detectors |
| | Alarm Detectors | | Sep-02-22 | Sep-12-22 | Fume Hood & Acid Cabinet |
| | Fume Hood & Acid Cabinet | / | Sep-02-22 | Sep-12-22 | |
| | Signage | 7 | Sep-02-22 | Sep-12-22 | Signage |
| MOLITION WO | | 35 | Sep-02-22 | Oct-20-22 | DEMOLITION WORKS |
| V-100 | Removal of Existing Lab Furniture & Equipment | 2 | Sep-02-22 | Sep-05-22 | Removal of Existing Lab Furniture & Equipment |
| V-110 | Removal of Existing Lab Benches & Fixed Furniture | 2 | Sep-06-22 | Sep-07-22 | Removal of Existing Lab Benches & Fixed Furniture |
| | Removal of Existing Shelves & Cabinets | 3 | Sep-08-22 | Sep-12-22 | ■ Removal of Existing Shelves & Cabinets |
| | Removal of Existing Flooring & Wall Bases | 3 | Sep-13-22 | Sep-15-22 | Removal of Existing Flooring & Wall Bases |
| | Removal of Existing Ceiling, Hanger & Supports | 3 | Sep-16-22 | Sep-20-22 | ■ Removal of Existing Ceiling, Hanger & Supports |
| | Removal of Existing Doors & Windows | 3 | Sep-21-22 | Sep-23-22 | ■ Removal of Existing Doors & Windows |
| V-160 | Removal of Existing Masonry Wall | 3 | Sep-26-22 | Sep-28-22 | Removal of Existing Masonry Wall |
| V-170 | Removal of Existing Sink Cabinet & Countertop | 2 | Sep-29-22 | Sep-30-22 | Removal of Existing Sink Cabinet & Countertop |
| | | | | | Removal of Existing Mechanical Fixtures & Equipments |
| | | | | | Removal of Existing Plumbing Piping & Fixtures |
| | | | | | ■ Removal of Existing Electric. Wiring & Fixtures |
| | | | | | Removal of Existing Roofing |
| CHITECTURA | AL WORKS | 211 | Oct-21-22 | Aug-11-23 | ▼ ARCHITECTURAL WORKS |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | 1 | 1 | | |
| Actual Work | ck Critical Remaining Work | | Page 1 of 2 | | Date Revision Checked Approved Aug-04-22 00 © Primavera |


Remaining Work •

H.S QUEENS SCIENCE LAB UPGRADE

207-01 116TH AVENUE, QUEENS, NY 11411

PROJECT SCHEDULE



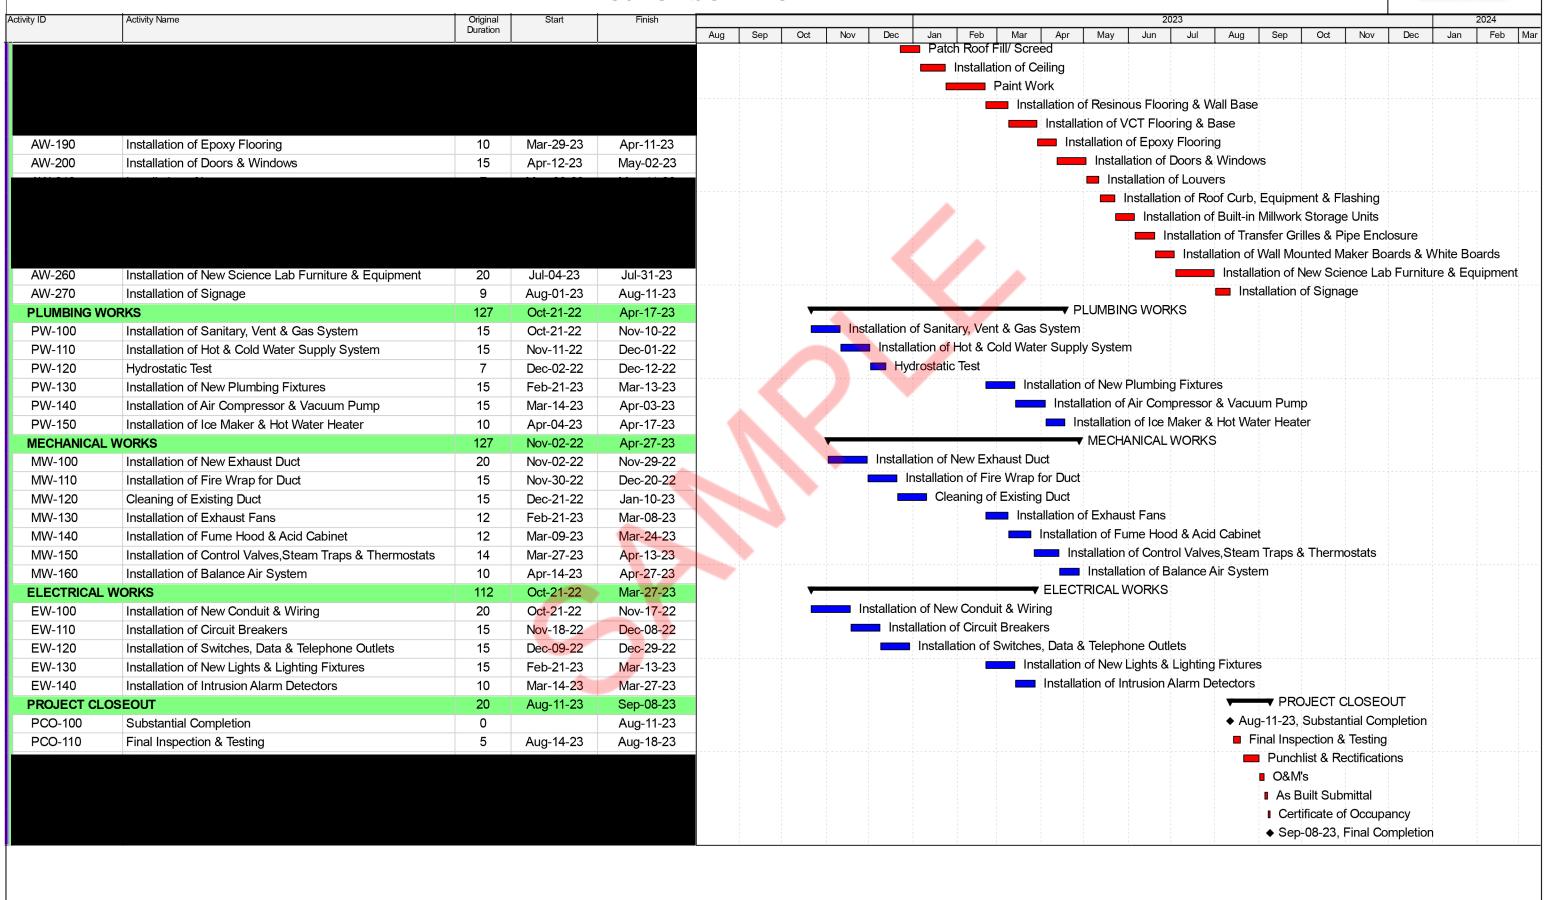

Page 2 of 2

Revision

00

Checked

Approved
