


CSM B36 MECHANICAL ENGINEERING PROJECT

BASELINE SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	2022												2023												2024											
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct							
CSM B36 MECHANICAL ENGINEERING PROJECT					CSM B36 MECHANICAL ENGINEERING PROJECT																																			
PRE-CONSTRUCTION					<ul style="list-style-type: none"> ▼ PRE-CONSTRUCTION █ Notice of Award █ Post Award Deliverables █ Agreement █ Notice to Proceed 																																			
LONG LEAD ITEMS					<ul style="list-style-type: none"> ▶ LONG LEAD ITEMS 																																			
UNDERGROUND PIPING					<ul style="list-style-type: none"> ▶ UNDERGROUND PIPING █ Submit █ Review/Approve █ Fabricate 																																			
REBAR					<ul style="list-style-type: none"> ▶ REBAR █ Detail █ Review/Approve █ Fabricate 																																			
STRUCTURAL STEEL					<ul style="list-style-type: none"> ▶ STRUCTURAL STEEL █ Review/Approve █ Fabricate 																																			
ROOF TOP UNIT					<ul style="list-style-type: none"> ▶ ROOF TOP UNIT █ Detail █ Review/Approve █ Fabricate 																																			
SPECIALTY CONTROL VALVES					<ul style="list-style-type: none"> ▶ SPECIALTY CONTROL VALVES █ Submit █ Approve █ Fabricate 																																			
MAIN PUMPS (3)					<ul style="list-style-type: none"> ▶ MAIN PUMPS (3) █ Submit 																																			
INSPECTIONS					<ul style="list-style-type: none"> ▶ INSPECTIONS █ Underground Piping █ Trenching B/F █ PAD █ Rebar █ Electrical Rough-In █ Electrical Complete █ HVAC 																																			
CONSTRUCTION					<ul style="list-style-type: none"> ▶ CONSTRUCTION ▶ PHASE 1 WORK ▶ MOBILIZE PHASE 1 																																			
PHASE 1 WORK					<ul style="list-style-type: none"> █ Mobilize 																																			
MOBILIZE PHASE 1					<ul style="list-style-type: none"> █ Mobilize 																																			
PH1-MOB-100 Mobilize					<ul style="list-style-type: none"> █ Mobilize 																																			
PH1-MOB-110 Rain Delay					<ul style="list-style-type: none"> █ Rain Delay 																																			
INTERIOR					<ul style="list-style-type: none"> ▶ INTERIOR 																																			

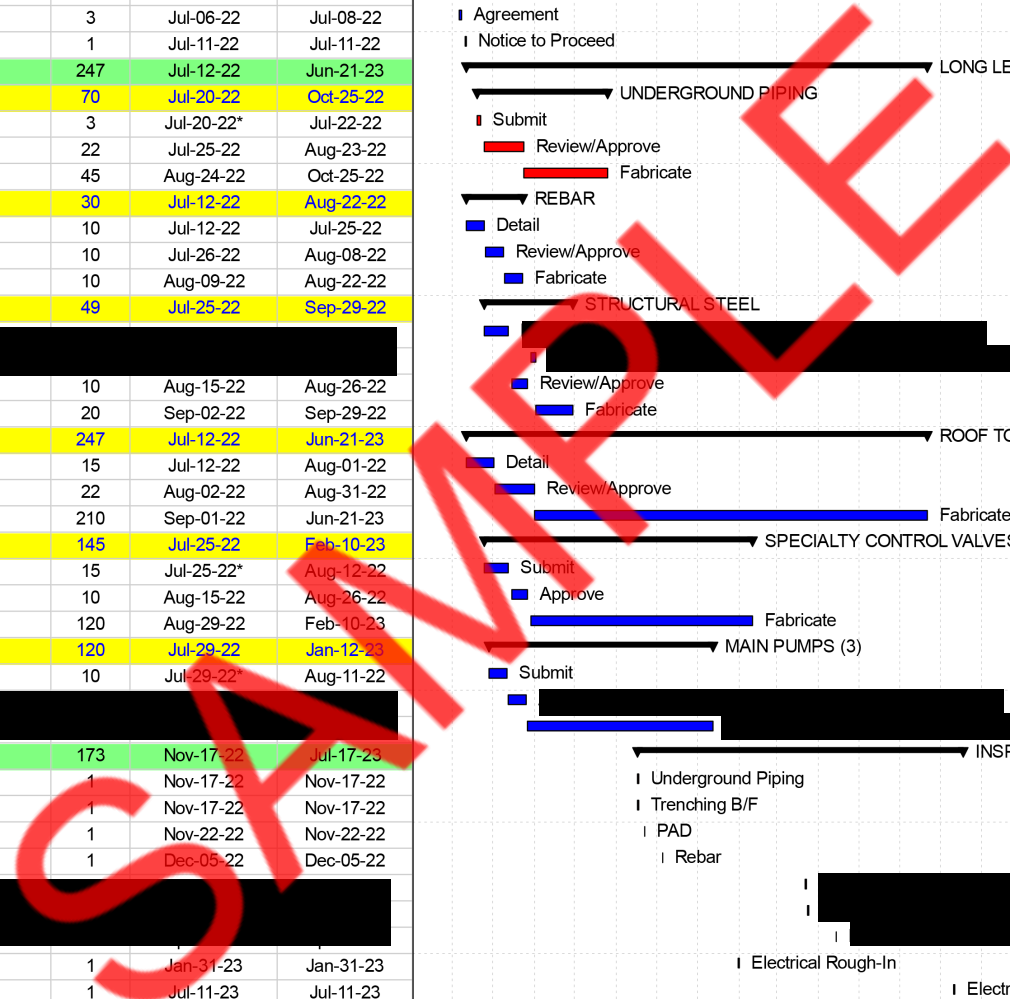


█ Actual Work
 █ Critical Remaining Work
 ▶ Milestone
█ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
Dec-08-22	02		



CSM B36 MECHANICAL ENGINEERING PROJECT

BASELINE SCHEDULE

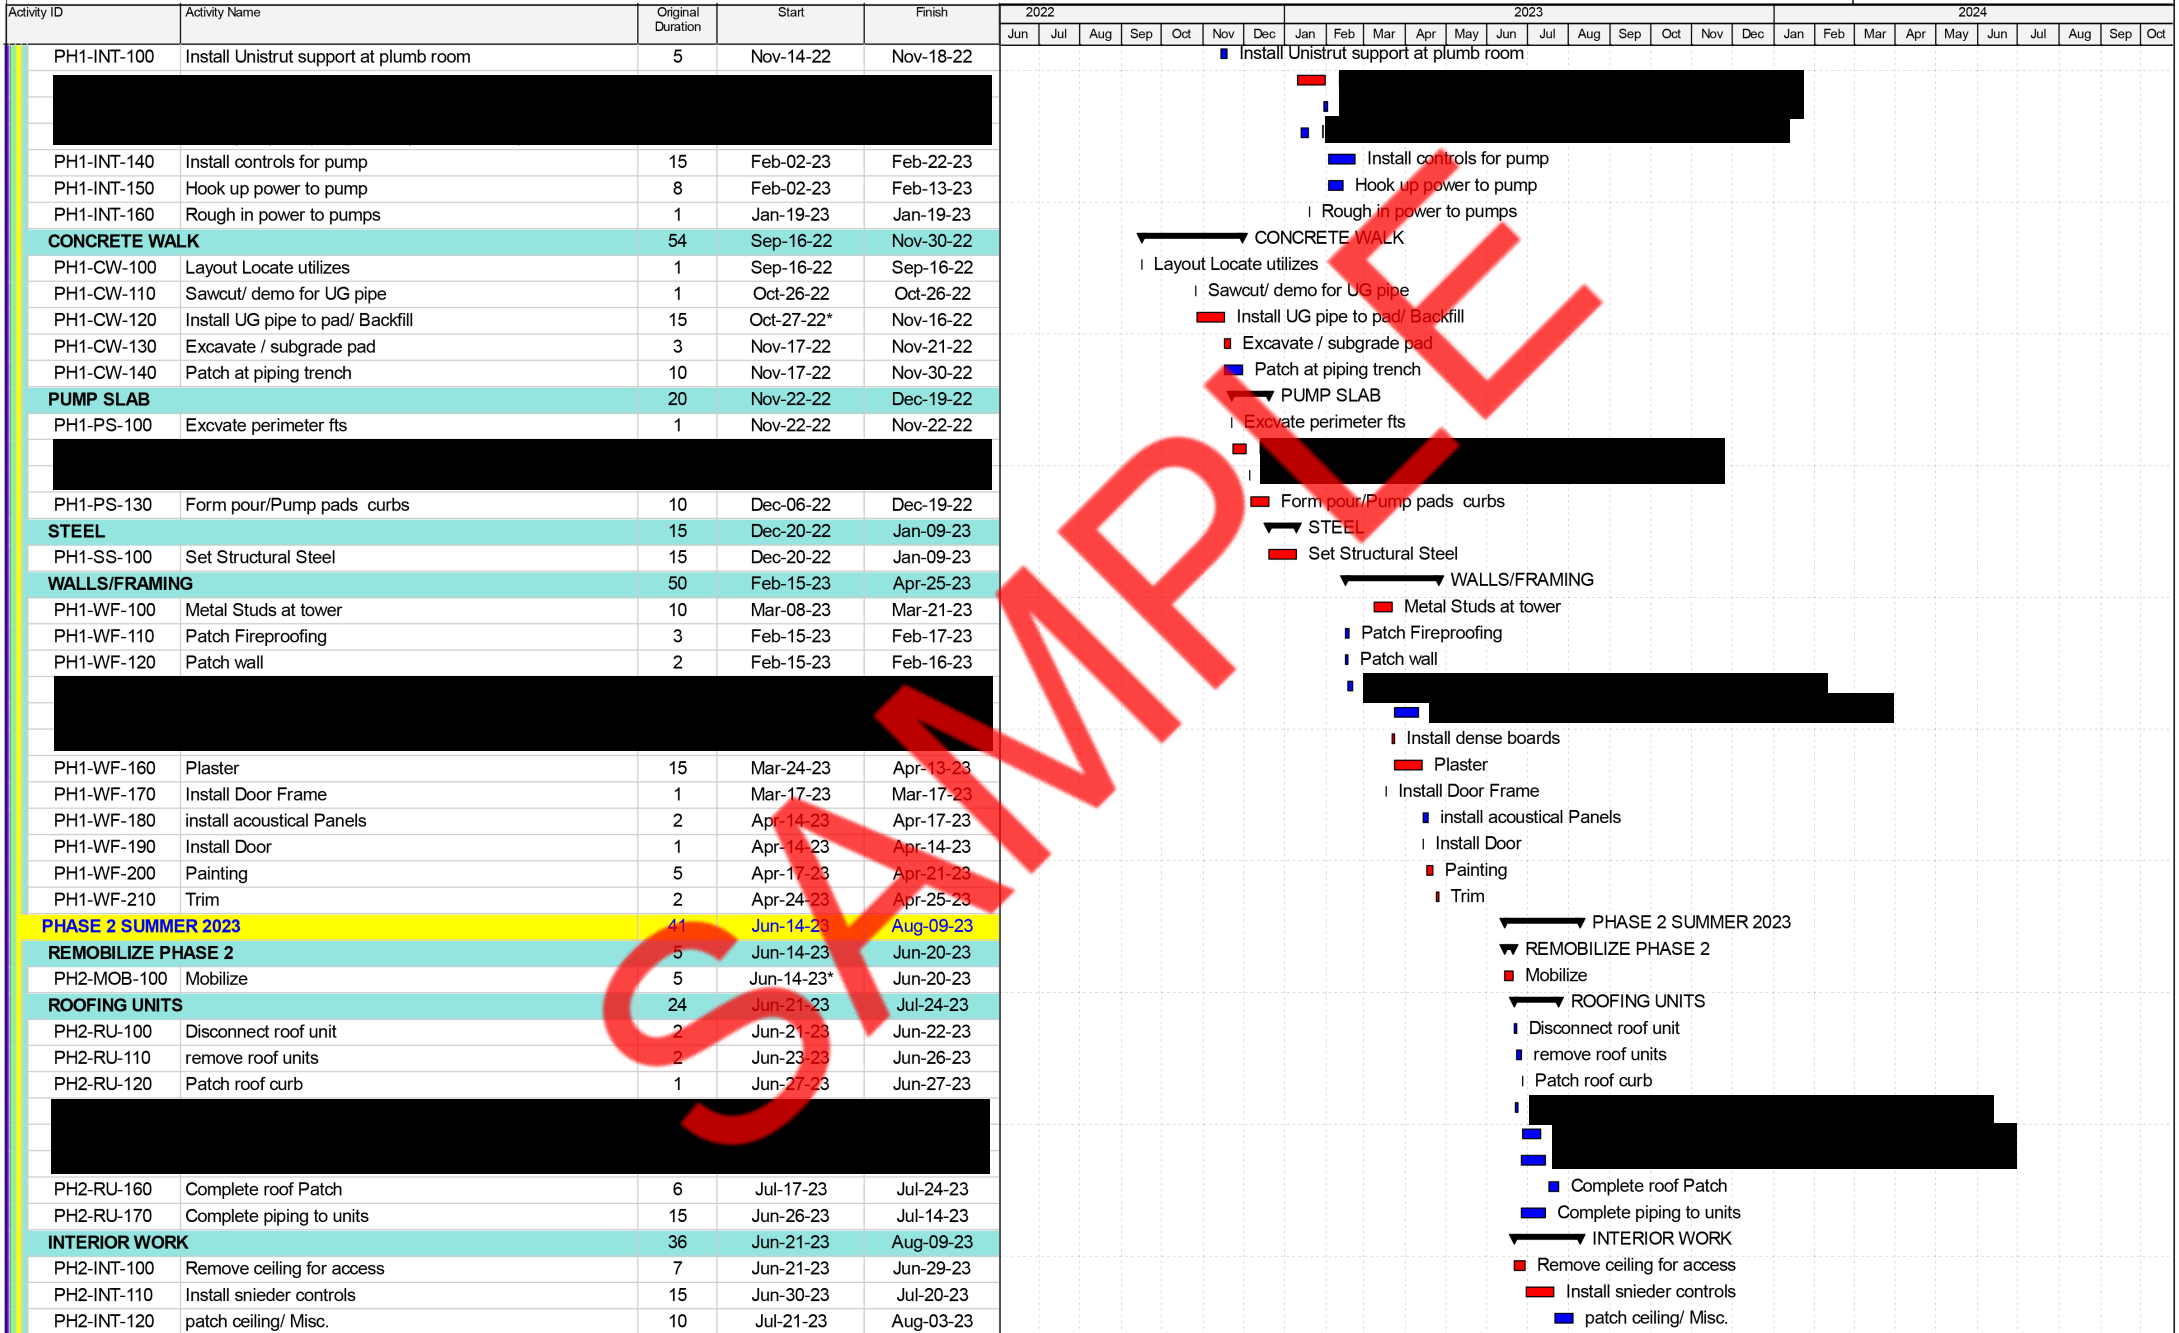


█ Actual Work
 █ Critical Remaining Work
 █ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
Dec-08-22	02		



CSM B36 MECHANICAL ENGINEERING PROJECT BASELINE SCHEDULE

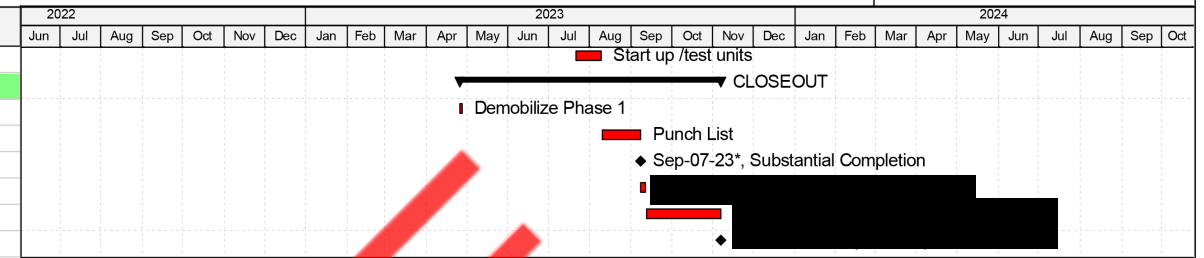Activity ID	Activity Name	Original Duration	Start	Finish	2022												2023												2024											
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct							
PH2-INT-130	Start up /test units	14	Jul-21-23	Aug-09-23																																				
CLOSEOUT		139	Apr-26-23	Nov-06-23																																				
CLO-100	Demobilize Phase 1	2	Apr-26-23	Apr-27-23																																				
CLO-110	Punch List	21	Aug-10-23	Sep-07-23																																				
CLO-115	Substantial Completion	0		Sep-07-23*																																				

SAMPLE
