


PAVEMENT PRESERVATION OF MAIN PARK ROAD EVERGLADES NATIONAL PARK MIAMI FLORIDA PROJECT SCHEDULE



■ Actual Work ■ Critical Remaining Work ▼
■ Remaining Work ◆ Milestone

Date	Revision	Checked	Approved
Sep-20-22	00		

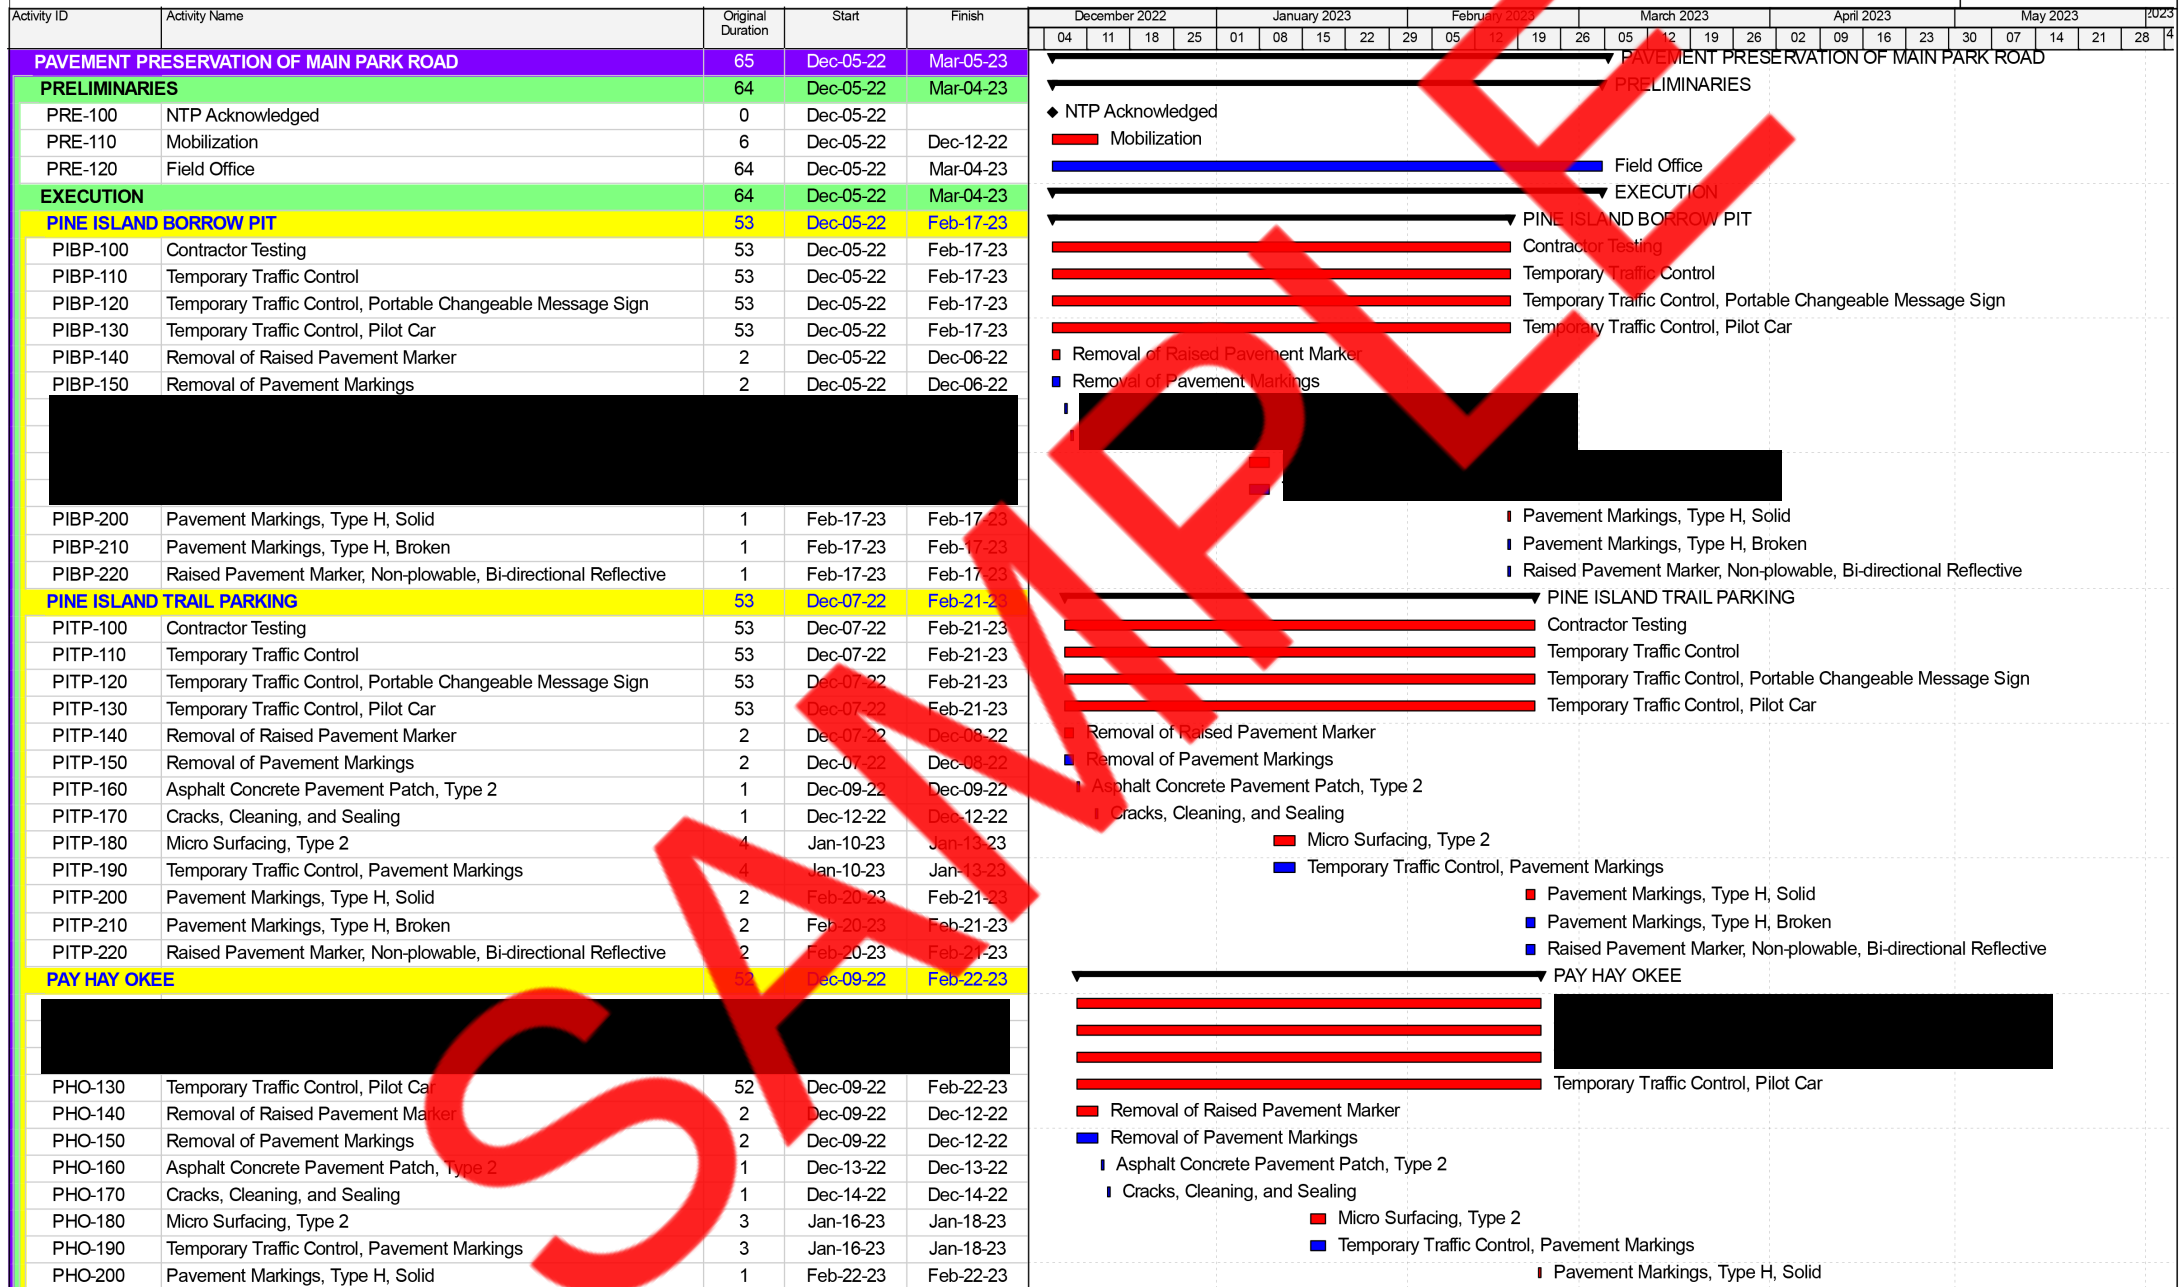


PAVEMENT PRESERVATION OF MAIN PARK ROAD EVERGLADES NATIONAL PARK MIAMI FLORIDA



PROJECT SCHEDULE

Activity ID	Activity Name	Original Duration	Start	Finish	December 2022				January 2023				February 2023				March 2023				April 2023				May 2023							
					04	11	18	25	01	08	15	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	07	14	21	28		
PHO-210	Pavement Markings, Type H, Broken	1	Feb-22-23	Feb-22-23																												
PHO-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	1	Feb-22-23	Feb-22-23																												
SISAL POND																																
SP-130	Temporary Traffic Control, Pilot Car	52	Dec-13-22	Feb-24-23																												
SP-140	Removal of Raised Pavement Marker	2	Dec-13-22	Dec-14-22																												
SP-150	Removal of Pavement Markings	2	Dec-13-22	Dec-14-22																												
SP-160	Asphalt Concrete Pavement Patch, Type 2	2	Dec-15-22	Dec-16-22																												
SP-170	Cracks, Cleaning, and Sealing	1	Dec-19-22	Dec-19-22																												
SP-180	Micro Surfacing, Type 2	4	Jan-19-23	Jan-24-23																												
SP-190	Temporary Traffic Control, Pavement Markings	4	Jan-19-23	Jan-24-23																												
SP-200	Pavement Markings, Type H, Solid	2	Feb-23-23	Feb-24-23																												
SP-210	Pavement Markings, Type H, Broken	2	Feb-23-23	Feb-24-23																												
SP-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	2	Feb-23-23	Feb-24-23																												
MAHOGANY HAMMOCK PARKING																																
MHP-100	Contractor Testing	51	Dec-15-22	Feb-27-23																												
MHP-110	Temporary Traffic Control	51	Dec-15-22	Feb-27-23																												
MHP-120	Temporary Traffic Control, Portable Changeable Message Sign	51	Dec-15-22	Feb-27-23																												
MHP-130	Temporary Traffic Control, Pilot Car	51	Dec-15-22	Feb-27-23																												
MHP-140	Removal of Raised Pavement Marker	2	Dec-15-22	Dec-16-22																												
MHP-150	Removal of Pavement Markings	2	Dec-15-22	Dec-16-22																												
MHP-160	Asphalt Concrete Pavement Patch, Type 2	1	Dec-19-22	Dec-19-22																												
MHP-170	Cracks, Cleaning, and Sealing	1	Dec-20-22	Dec-20-22																												
MHP-180	Micro Surfacing, Type 2	3	Jan-25-23	Jan-27-23																												
MHP-190	Temporary Traffic Control, Pavement Markings	3	Jan-25-23	Jan-27-23																												
PAUROTIS POND																																
PP-100	Contractor Testing	50	Dec-19-22	Feb-28-23																												
PP-110	Temporary Traffic Control	50	Dec-19-22	Feb-28-23																												
PP-120	Temporary Traffic Control, Portable Changeable Message Sign	50	Dec-19-22	Feb-28-23																												
PP-130	Temporary Traffic Control, Pilot Car	50	Dec-19-22	Feb-28-23																												
PP-140	Removal of Raised Pavement Marker	2	Dec-19-22	Dec-20-22																												
PP-150	Removal of Pavement Markings	2	Dec-19-22	Dec-20-22																												
PP-160	Asphalt Concrete Pavement Patch, Type 2	1	Dec-21-22	Dec-21-22																												
PP-170	Cracks, Cleaning, and Sealing	1	Dec-22-22	Dec-22-22																												
PP-180	Micro Surfacing, Type 2	3	Jan-30-23	Feb-01-23																												
PP-190	Temporary Traffic Control, Pavement Markings	3	Jan-30-23	Feb-01-23																												
PP-200	Pavement Markings, Type H, Solid	1	Feb-28-23	Feb-28-23																												
9 MILE POND																																
9MP-100	Contractor Testing	49	Dec-21-22	Mar-01-23																												

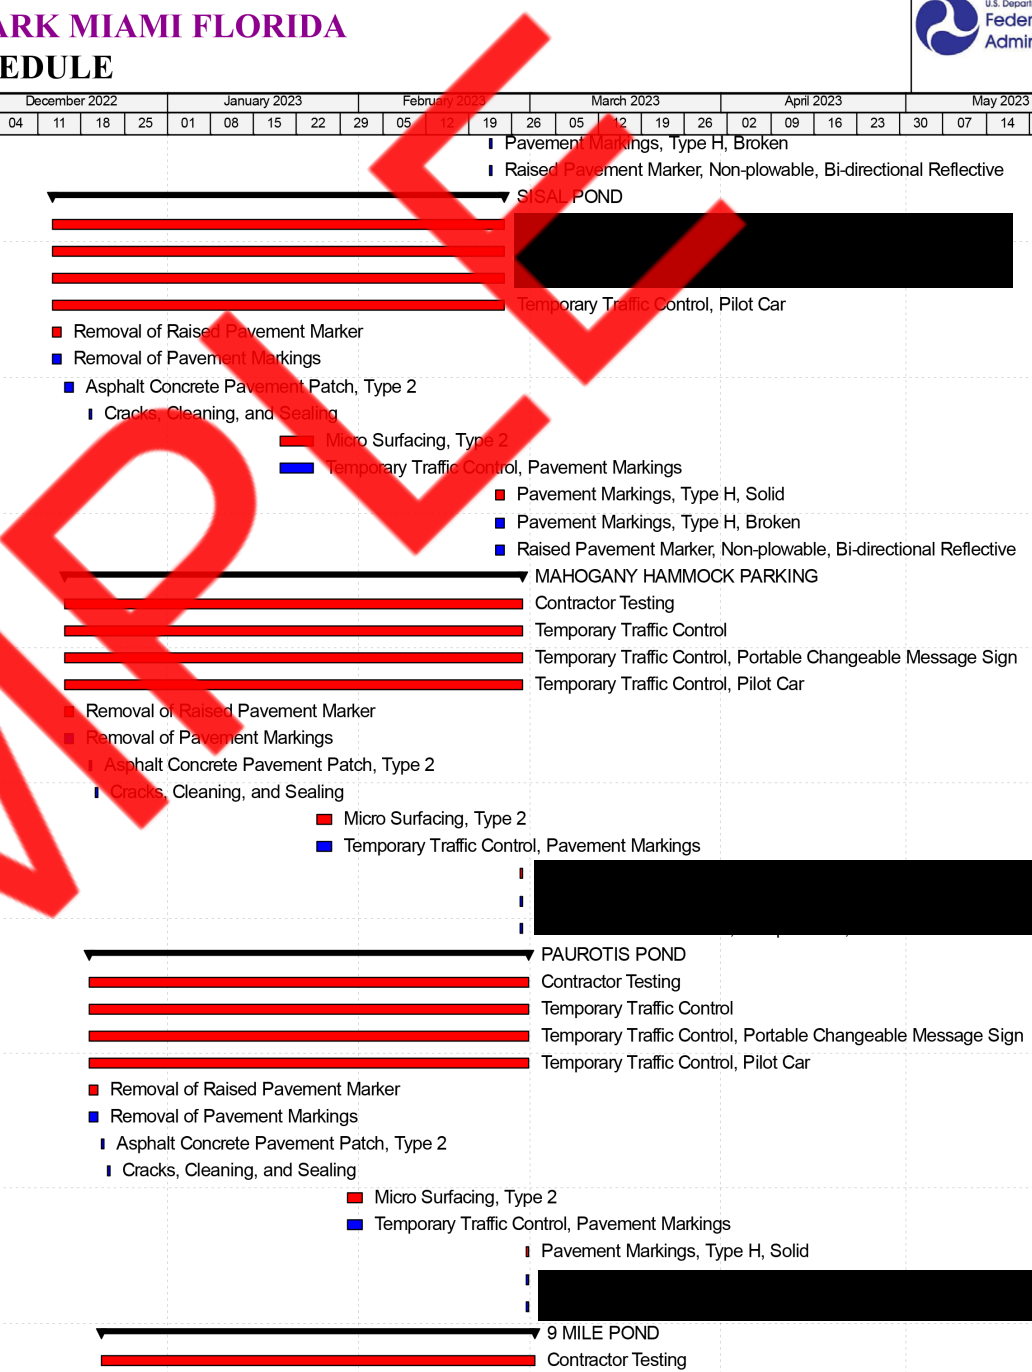

■ Actual Work ■ Critical Remaining Work ■ Remaining Work
◆ Milestone

Date	Revision	Checked	Approved
Sep-20-22	00		



PAVEMENT PRESERVATION OF MAIN PARK ROAD EVERGLADES NATIONAL PARK MIAMI FLORIDA PROJECT SCHEDULE



Activity ID	Activity Name	Original Duration	Start	Finish	December 2022				January 2023				February 2023				March 2023				April 2023				May 2023							
					04	11	18	25	01	08	15	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	07	14	21	28		
9MP-110	Temporary Traffic Control	49	Dec-21-22	Mar-01-23	[Gantt bar: Dec 21 to Mar 1, 2023]																											
9MP-120	Temporary Traffic Control, Portable Changeable Message Sign	49	Dec-21-22	Mar-01-23	[Gantt bar: Dec 21 to Mar 1, 2023]																											
[Redacted]																																
9MP-160	Asphalt Concrete Pavement Patch, Type 2	1	Dec-23-22	Dec-23-22	[Gantt bar: Dec 23, 2022]																											
9MP-170	Cracks, Cleaning, and Sealing	1	Dec-27-22	Dec-27-22	[Gantt bar: Dec 27, 2022]																											
9MP-180	Micro Surfacing, Type 2	3	Feb-02-23	Feb-06-23	[Gantt bar: Feb 2 to Feb 6, 2023]																											
9MP-190	Temporary Traffic Control, Pavement Markings	3	Feb-02-23	Feb-06-23	[Gantt bar: Feb 2 to Feb 6, 2023]																											
9MP-200	Pavement Markings, Type H, Solid	1	Mar-01-23	Mar-01-23	[Gantt bar: Mar 1, 2023]																											
9MP-210	Pavement Markings, Type H, Broken	1	Mar-01-23	Mar-01-23	[Gantt bar: Mar 1, 2023]																											
9MP-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	1	Mar-01-23	Mar-01-23	[Gantt bar: Mar 1, 2023]																											
WEST LAKE																																
WL-100	Contractor Testing	48	Dec-23-22	Mar-02-23	[Gantt bar: Dec 23 to Mar 2, 2023]																											
WL-110	Temporary Traffic Control	48	Dec-23-22	Mar-02-23	[Gantt bar: Dec 23 to Mar 2, 2023]																											
WL-120	Temporary Traffic Control, Portable Changeable Message Sign	48	Dec-23-22	Mar-02-23	[Gantt bar: Dec 23 to Mar 2, 2023]																											
WL-130	Temporary Traffic Control, Pilot Car	48	Dec-23-22	Mar-02-23	[Gantt bar: Dec 23 to Mar 2, 2023]																											
WL-140	Removal of Raised Pavement Marker	2	Dec-23-22	Dec-27-22	[Gantt bar: Dec 23 to Dec 27, 2022]																											
WL-150	Removal of Pavement Markings	2	Dec-23-22	Dec-27-22	[Gantt bar: Dec 23 to Dec 27, 2022]																											
WL-160	Asphalt Concrete Pavement Patch, Type 2	1	Dec-28-22	Dec-28-22	[Gantt bar: Dec 28, 2022]																											
WL-170	Cracks, Cleaning, and Sealing	1	Dec-29-22	Dec-29-22	[Gantt bar: Dec 29, 2022]																											
WL-180	Micro Surfacing, Type 2	3	Feb-07-23	Feb-09-23	[Gantt bar: Feb 7 to Feb 9, 2023]																											
WL-190	Temporary Traffic Control, Pavement Markings	3	Feb-07-23	Feb-09-23	[Gantt bar: Feb 7 to Feb 9, 2023]																											
WL-200	Pavement Markings, Type H, Solid	1	Mar-02-23	Mar-02-23	[Gantt bar: Mar 2, 2023]																											
WL-210	Pavement Markings, Type H, Broken	1	Mar-02-23	Mar-02-23	[Gantt bar: Mar 2, 2023]																											
WL-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	1	Mar-02-23	Mar-02-23	[Gantt bar: Mar 2, 2023]																											
ROWDY BEND																																
RB-100	Contractor Testing	47	Dec-28-22	Mar-03-23	[Gantt bar: Dec 28 to Mar 3, 2023]																											
[Redacted]																																
RB-140	Removal of Raised Pavement Marker	2	Dec-28-22	Dec-29-22	[Gantt bar: Dec 28 to Dec 29, 2022]																											
RB-150	Removal of Pavement Markings	2	Dec-28-22	Dec-29-22	[Gantt bar: Dec 28 to Dec 29, 2022]																											
RB-160	Asphalt Concrete Pavement Patch, Type 2	1	Dec-30-22	Dec-30-22	[Gantt bar: Dec 30, 2022]																											
RB-170	Cracks, Cleaning, and Sealing	1	Jan-03-23	Jan-03-23	[Gantt bar: Jan 3, 2023]																											
RB-180	Micro Surfacing, Type 2	3	Feb-10-23	Feb-14-23	[Gantt bar: Feb 10 to Feb 14, 2023]																											
RB-190	Temporary Traffic Control, Pavement Markings	3	Feb-10-23	Feb-14-23	[Gantt bar: Feb 10 to Feb 14, 2023]																											
RB-200	Pavement Markings, Type H, Solid	1	Mar-03-23	Mar-03-23	[Gantt bar: Mar 3, 2023]																											
RB-210	Pavement Markings, Type H, Broken	1	Mar-03-23	Mar-03-23	[Gantt bar: Mar 3, 2023]																											
RB-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	1	Mar-03-23	Mar-03-23	[Gantt bar: Mar 3, 2023]																											
FLAMINGO GAS STATION/ MAINTENANCE YARD																																
FGS-MY-100	Contractor Testing	46	Dec-30-22	Mar-04-23	[Gantt bar: Dec 30 to Mar 4, 2023]																											
FGS-MY-110	Temporary Traffic Control	46	Dec-30-22	Mar-04-23	[Gantt bar: Dec 30 to Mar 4, 2023]																											
FGS-MY-120	Temporary Traffic Control, Portable Changeable Message Sign	46	Dec-30-22	Mar-04-23	[Gantt bar: Dec 30 to Mar 4, 2023]																											
FGS-MY-130	Temporary Traffic Control, Pilot Car	46	Dec-30-22	Mar-04-23	[Gantt bar: Dec 30 to Mar 4, 2023]																											
FGS-MY-140	Removal of Raised Pavement Marker	2	Dec-30-22	Jan-03-23	[Gantt bar: Dec 30 to Jan 3, 2023]																											

■ Actual Work ■ Critical Remaining Work ▼
■ Remaining Work ◆ Milestone

Date	Revision	Checked	Approved
Sep-20-22	00		



**PAVEMENT PRESERVATION OF MAIN PARK ROAD
EVERGLADES NATIONAL PARK MIAMI FLORIDA
PROJECT SCHEDULE**



Activity ID	Activity Name	Original Duration	Start	Finish	December 2022				January 2023				February 2023				March 2023				April 2023				May 2023			
					04	11	18	25	01	08	15	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	07	14
FGS-MY-150	Removal of Pavement Markings	2	Dec-30-22	Jan-03-23																								
FGS-MY-160	Asphalt Concrete Pavement Patch, Type 2	1	Jan-04-23	Jan-04-23																								
FGS-MY-170	Cracks, Cleaning, and Sealing	1	Jan-05-23	Jan-05-23																								
FGS-MY-210	Pavement Markings, Type H, Broken	1	Mar-04-23	Mar-04-23																								
FGS-MY-220	Raised Pavement Marker, Non-plowable, Bi-directional Reflective	1	Mar-04-23	Mar-04-23																								
CLOSE OUT		0	Mar-05-23	Mar-05-23																								
CO-100	Final Inspection	0	Mar-05-23	Mar-05-23																								

SAMPLE

■ Actual Work ■ Critical Remaining Work ▼
■ Remaining Work ◆ Milestone

Date	Revision	Checked	Approved
Sep-20-22	00		

