

SAMPLE


■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ ◆ Milestone



Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Timeline			
						Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023
A1050	Fab/Deliver Misc Metals	40	18-Jan-23	17-Mar-23	Standard 5 Day Workweek	[Gantt bar: 18-Jan-23 to 17-Mar-23]			
A1051	Fab/Deliver Fencing	40	18-Jan-23	17-Mar-23	Standard 5 Day Workweek	[Gantt bar: 18-Jan-23 to 17-Mar-23]			
A1052	Fab/Deliver Fiberglass Grates	40	18-Jan-23	17-Mar-23	Standard 5 Day Workweek	[Gantt bar: 18-Jan-23 to 17-Mar-23]			
A1053	Fab/Deliver Pumping Equipment & Controls	30	18-Jan-23	03-Mar-23	Standard 5 Day Workweek	[Gantt bar: 18-Jan-23 to 03-Mar-23]			
A1054	Fab/Deliver Construction Project Funding Sign	9	06-Mar-23	17-Mar-23	Standard 5 Day Workweek	[Gantt bar: 06-Mar-23 to 17-Mar-23]			
A1055	Fab/Deliver Electrical	45	09-Jan-23	15-Mar-23	Standard 5 Day Workweek	[Gantt bar: 09-Jan-23 to 15-Mar-23]			
[Redacted]						[Gantt bar: 09-Jan-23 to 15-Mar-23]			
A1060	Install Drain Inlet Protection(Loc.3 & 4)	1	03-Apr-23	03-Apr-23	Standard 5 Day Workweek	[Milestone: 03-Apr-23]			
Location 1_Mossdale Up Rte 120-5_Pump 29-0030W						[Gantt bar: 03-Jul-23 to 20-May-23]			
A1061	Install Conduit & Concrete for Electric Service(Loc.1)	55	17-Apr-23	03-Jul-23	Standard 5 Day Workweek	[Gantt bar: 17-Apr-23 to 03-Jul-23]			
A1062	Perform Tree Trimming(Loc.1)	4	17-Apr-23	20-Apr-23	Standard 5 Day Workweek	[Gantt bar: 17-Apr-23 to 20-Apr-23]			
A1063	Install Power Pole(Loc.1)	1	21-Apr-23	21-Apr-23	Standard 5 Day Workweek	[Milestone: 21-Apr-23]			
A1064	Install Electric Equip Service Enclosure(Loc.1)	1	01-May-23	02-May-23	Standard 5 Day Workweek	[Milestone: 01-May-23]			
[Redacted]						[Gantt bar: 01-May-23 to 02-May-23]			
A1070	Install Grating, Ladders, Grab Bars(Loc.1)	4	06-Jun-23	09-Jun-23	Standard 5 Day Workweek	[Gantt bar: 06-Jun-23 to 09-Jun-23]			
A1071	Install Electrical(Loc.1)	10	12-Jun-23	23-Jun-23	Standard 5 Day Workweek	[Gantt bar: 12-Jun-23 to 23-Jun-23]			
A1072	Start Up and Testing(Loc.1)	5	26-Jun-23	30-Jun-23	Standard 5 Day Workweek	[Gantt bar: 26-Jun-23 to 30-Jun-23]			
A1073	Performance Testing(Loc.1)	1	03-Jul-23	03-Jul-23	Standard 5 Day Workweek	[Milestone: 03-Jul-23]			
Location 2_Route 5-4 Sep_Pump 29-0232W						[Gantt bar: 28-Jul-23 to 28-Jul-23]			
A1120	Install HDD Conduit under waterway(Loc.2)	69	21-Apr-23	28-Jul-23	Standard 5 Day Workweek	[Gantt bar: 21-Apr-23 to 28-Jul-23]			
A1130	Install Conduit & Concrete for Electric Service(Loc.2)	4	21-Apr-23	26-Apr-23	Standard 5 Day Workweek	[Gantt bar: 21-Apr-23 to 26-Apr-23]			
A1140	Install Service Meter Enclosure(Loc.2)	1	04-May-23	04-May-23	Standard 5 Day Workweek	[Milestone: 04-May-23]			
[Redacted]						[Gantt bar: 04-May-23 to 04-May-23]			
A1150	Install Mechanical(Loc.2)	6	20-Jun-23	06-Jul-23	Standard 5 Day Workweek	[Gantt bar: 20-Jun-23 to 06-Jul-23]			
A1200	Install Grating and Grab Bar(Loc.2)	4	30-Jun-23	06-Jul-23	Standard 5 Day Workweek	[Gantt bar: 30-Jun-23 to 06-Jul-23]			
A1210	Install Electrical(Loc.2)	10	07-Jul-23	20-Jul-23	Standard 5 Day Workweek	[Gantt bar: 07-Jul-23 to 20-Jul-23]			
A1220	Start Up and Testing(Loc.2)	5	21-Jul-23	27-Jul-23	Standard 5 Day Workweek	[Gantt bar: 21-Jul-23 to 27-Jul-23]			
A1230	Performance Testing	1	28-Jul-23	28-Jul-23	Standard 5 Day Workweek	[Milestone: 28-Jul-23]			
A1250	Concrete Curing	5	27-Apr-23	03-May-23	Standard 5 Day Workweek	[Gantt bar: 27-Apr-23 to 03-May-23]			
Location 3_Rte 99 Eastside Up_Pump 29-0065W						[Gantt bar: 23-Aug-23 to 23-Aug-23]			
A1074	De-energize PGE Lines(10-1.02F)	82	28-Apr-23	23-Aug-23	Standard 5 Day Workweek	[Gantt bar: 28-Apr-23 to 23-Aug-23]			
A1075	Install Conduit & Concrete for Electric Service(Loc.3)	1	28-Apr-23	03-May-23	Standard 5 Day Workweek	[Gantt bar: 28-Apr-23 to 03-May-23]			
A1076	Install Electric Equip Service Enclosure(Loc.3)	4	16-May-23	17-May-23	Standard 5 Day Workweek	[Gantt bar: 16-May-23 to 17-May-23]			
[Redacted]						[Gantt bar: 16-May-23 to 17-May-23]			
A1082	Install Grates(Loc.3)	1	31-Jul-23	01-Aug-23	Standard 5 Day Workweek	[Milestone: 31-Jul-23]			
A1083	Install Electrical(Loc.3)	2	02-Aug-23	15-Aug-23	Standard 5 Day Workweek	[Gantt bar: 02-Aug-23 to 15-Aug-23]			
A1084	Install Iron Fencing & Gates(Loc.3)	10	02-Aug-23	15-Aug-23	Standard 5 Day Workweek	[Gantt bar: 02-Aug-23 to 15-Aug-23]			
A1085	Start Up and Testing(Loc.3)	5	16-Aug-23	22-Aug-23	Standard 5 Day Workweek	[Gantt bar: 16-Aug-23 to 22-Aug-23]			
A1086	Performance Testing	1	23-Aug-23	23-Aug-23	Standard 5 Day Workweek	[Milestone: 23-Aug-23]			
A1116	Concrete curing	9	03-May-23	16-May-23	Standard 5 Day Workweek	[Gantt bar: 03-May-23 to 16-May-23]			
Location 4_Rte 99 Wilson Way_Pump 29-0118W						[Gantt bar: 26-Sep-23 to 26-Sep-23]			
[Redacted]						[Gantt bar: 26-Sep-23 to 26-Sep-23]			
[Redacted]						[Gantt bar: 26-Sep-23 to 26-Sep-23]			

SAMPLE

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ ◆ Milestone

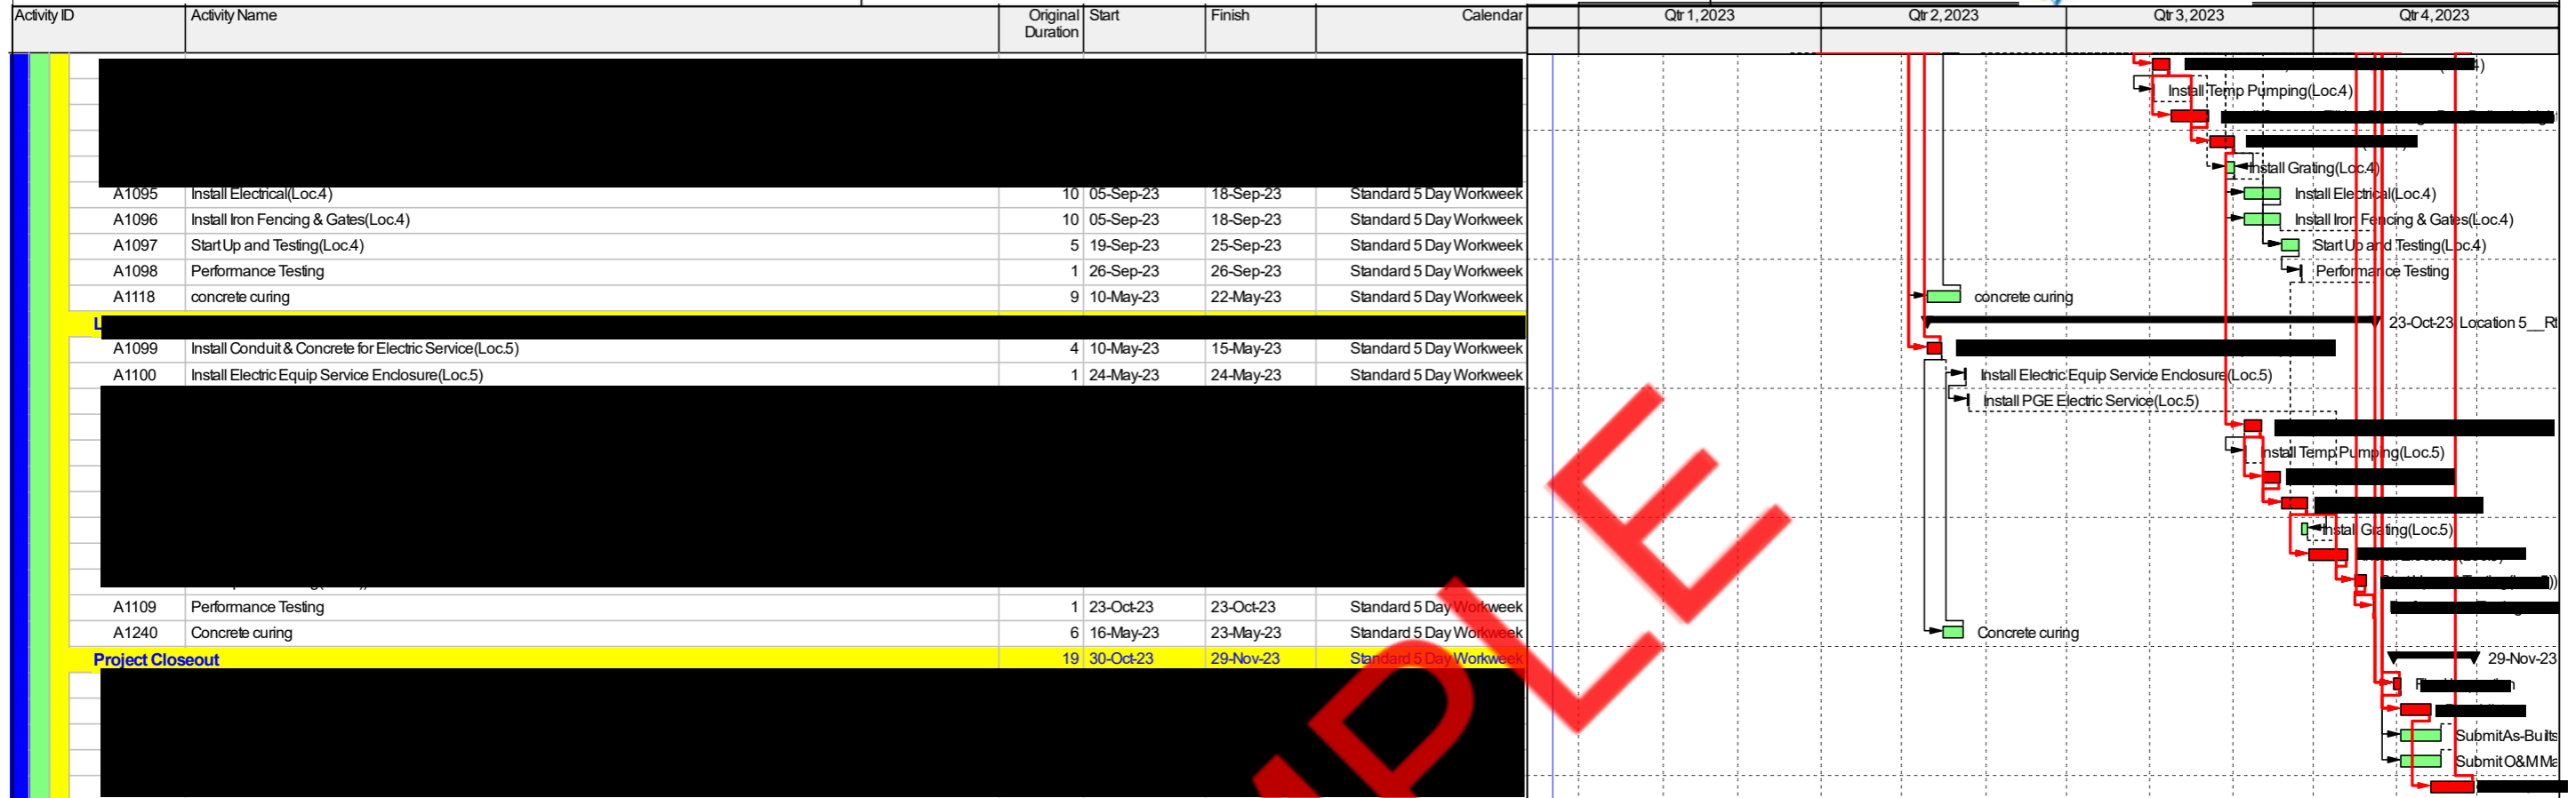

SAMPLE

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ ◆ Milestone
