

D020604-B001



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024		
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
D020604-B001		271	05-Sep-23	03-Oct-24	[Summary bar]															
MILESTONES		383	05-Sep-23	03-Oct-24	[Summary bar]															
MS-0010	Notice to Proceed (NTP)	0	05-Sep-23*		Notice to Proceed (NTP), 05-Sep-23*															
MS-0040	End of Demolition Basement Floor	0		02-Feb-24	◆ End of Demolition Basement Floor,															
					◆ End of Demolition First Floor,															
MS-0110	End of Execution Third Floor	0		08-Jul-24	[Redacted]															
MS-0130	End of Execution Fourth Floor	0		19-Jul-24	◆ End of Execution Fourth Floor,															
MS-0140	End of Demolition Fifth Floor	0		01-Aug-24	◆ End of Demolition Fifth Floor,															
					[Redacted]															
MS-0030	Project Final Completion	0		03-Oct-24*	◆ Project F															
ENGINEERING		70	05-Sep-23	15-Nov-23	15-Nov-23, ENGINEERING															
SUBMITTALS		70	05-Sep-23	15-Nov-23	15-Nov-23, SUBMITTALS															
SUBMISSION		40	05-Sep-23	15-Oct-23	15-Oct-23, SUBMISSION															
SUB-S-030	Submission of Site Safety Plan	30	05-Sep-23	04-Oct-23	Submission of Site Safety Plan															
SUB-S-001	Submission of DOB General Construction Permit	37	05-Sep-23	12-Oct-23	Submission of DOB General Construction Permit															
					[Redacted]															
SUB-S-008	Submission of Ornamental Metal Submittal	40	05-Sep-23	15-Oct-23	Submission of Ornamental Metal Submittal															
SUB-S-009	Submission of Firestopping /Smoke Seal & Assembly St	40	05-Sep-23	15-Oct-23	Submission of Firestopping /Smoke Seal & Assembly Submittal															
SUB-S-010	Submission of Joint Sealers Submittal	40	05-Sep-23	15-Oct-23	Submission of Joint Sealers Submittal															
					[Redacted]															
SUB-S-016	Submission of Louvers Submittal	40	05-Sep-23	15-Oct-23	Submission of Louvers Submittal															
SUB-S-017	Submission of HVAC Identification Submittal	40	05-Sep-23	15-Oct-23	Submission of HVAC Identification Submittal															
SUB-S-018	Submission of Vibration Isolation - HVAC Submittal	40	05-Sep-23	15-Oct-23	Submission of Vibration Isolation - HVAC Submittal															
					[Redacted]															
SUB-S-026	Submission of Enclosed Switches Submittal	40	05-Sep-23	15-Oct-23	Submission of Enclosed Switches Submittal															

SAMPLE


█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ── summary



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024		
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
■ SUB-S-027	Submission of Panelboards Submittal	40	05-Sep-23	15-Oct-23	Submission of Panelboards Submittal															
■ SUB-S-028	Submission of Fire Alarm System Equipment Submittal	40	05-Sep-23	15-Oct-23	Submission of Fire Alarm System Equipment Submittal															
■ SUB-S-029	Submission of Heat Trace System Submittal	40	05-Sep-23	15-Oct-23	Submission of Heat Trace System Submittal															
REVIEW AND APPROVAL					15-Nov-23, REVIEW AND APPROVAL															
■ RA-S-0070	Review and Approval of Site Safety Plan	21	05-Oct-23	26-Oct-23	Review and Approval of Site Safety Plan															
[REDACTED]					[REDACTED]															
■ RA-S-0120	Review and Approval of Finish Hardware Submittal	21	16-Oct-23	05-Nov-23	Review and Approval of Finish Hardware Submittal															
■ RA-S-0130	Review and Approval of Gypsum Board assemblies and	21	16-Oct-23	05-Nov-23	Review and Approval of Gypsum Board assemblies and Accessories Submittal															
[REDACTED]					[REDACTED]															
■ RA-S-0250	Review and Approval of Wiring Devices Submittal	21	16-Oct-23	05-Nov-23	Review and Approval of Wiring Devices Submittal															
■ RA-S-0260	Review and Approval of Enclosed Switches Submittal	21	16-Oct-23	05-Nov-23	Review and Approval of Enclosed Switches Submittal															
■ RA-S-0270	Review and Approval of Panelboards Submittal	21	16-Oct-23	05-Nov-23	Review and Approval of Panelboards Submittal															
[REDACTED]					[REDACTED]															
■ RA-S-0150	Review and Approval of Plumbing Permit	30	16-Oct-23	15-Nov-23	Review and Approval of Plumbing Permit															
WORKSHOP DRAWINGS					05-Nov-23, WORKSHOP DRAWINGS															
SUBMISSION					15-Oct-23, SUBMISSION															
■ SUB-W-00	Submission of Concrete Pad Layouts Shop Drawing	40	05-Sep-23	15-Oct-23	Submission of Concrete Pad Layouts Shop Drawing															
[REDACTED]					[REDACTED]															
■ SUB-W-01	Submission of Ductwork Shop Standards Shop Drawing	40	05-Sep-23	15-Oct-23	Submission of Ductwork Shop Standards Shop Drawing															
■ SUB-W-01	Submission of Ductwork Shop Drawing	40	05-Sep-23	15-Oct-23	Submission of Ductwork Shop Drawing															

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ▸ summary

Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024		Qtr 4, 2024			
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
■ SUB-W-01	Submission of Wiring Diagrams and Layout Shop Drawi	40	05-Sep-23	15-Oct-23	Submission of Wiring Diagrams and Layout Shop Drawing															
■ REVIEW AND APPROVAL					05-Nov-23, REVIEW AND APPROVAL															
■ RA-W-0010	Review and Approval of Concrete Pad Layouts Shop Dr:	21	16-Oct-23	05-Nov-23	Review and Approval of Concrete Pad Layouts Shop Drawing															
■ RA-W-0120					Review and Approval of Ductwork Shop Standards Shop Drawing															
■ RA-W-0130					Review and Approval of Ductwork Shop Drawing															
■ RA-W-0140					Review and Approval of Wiring Diagrams and Layout Shop Drawing															
■ MOCKUPS					05-Nov-23, MOCKUPS															
■ SUBMISSION					15-Oct-23, SUBMISSION															
■ SUB-M-00	Submission of Joint Sealers Mockup	40	05-Sep-23	15-Oct-23	Submission of Joint Sealers Mockup															
■ SUB-M-00i					Submission of Wiring Devices Mockup															
■ REVIEW AND APPROVAL					05-Nov-23, REVIEW AND APPROVAL															
■ RA-M-0010	Review and Approval of Joint Sealers Mockup	21	16-Oct-23	05-Nov-23	Review and Approval of Joint Sealers Mockup															
■ RA-M-0080					Review and Approval of Wiring Devices Mockup															
■ PROCUREMENT					25-Jul-24, PROCUREMENT															
■ PROC-0040	Fabrtication and Delivery of Remaining Long Lead Items	100	06-Nov-23	21-Feb-24	Fabrtication and Delivery of Remaining Long Lead Items															
■ PROC-0010					Fabrtication and Delivery of Fans															
■ CONSTRUCTION					03-Sep-24, CONSTRU															
■ EARLY SITE WORKS					08-Dec-23, EARLY SITE WORKS															
■ ESW-0010	Mobilization	10	13-Nov-23	28-Nov-23	Mobilization															
■ BASEMENT FLOOR					22-Apr-24, BASEMENT FLOOR															
■ DEMOLITION WORKS					02-Feb-24, DEMOLITION WORKS															
■ ELECTRICAL DEMOLITIONS					02-Jan-24, ELECTRICAL DEMOLITIONS															
■ C.DEM.E.	BF: Disconnect Wiring and Conduits to F-2 and Ass. VFI	3	11-Dec-23	13-Dec-23	BF: Disconnect Wiring and Conduits to F-2 and Ass. VFD															

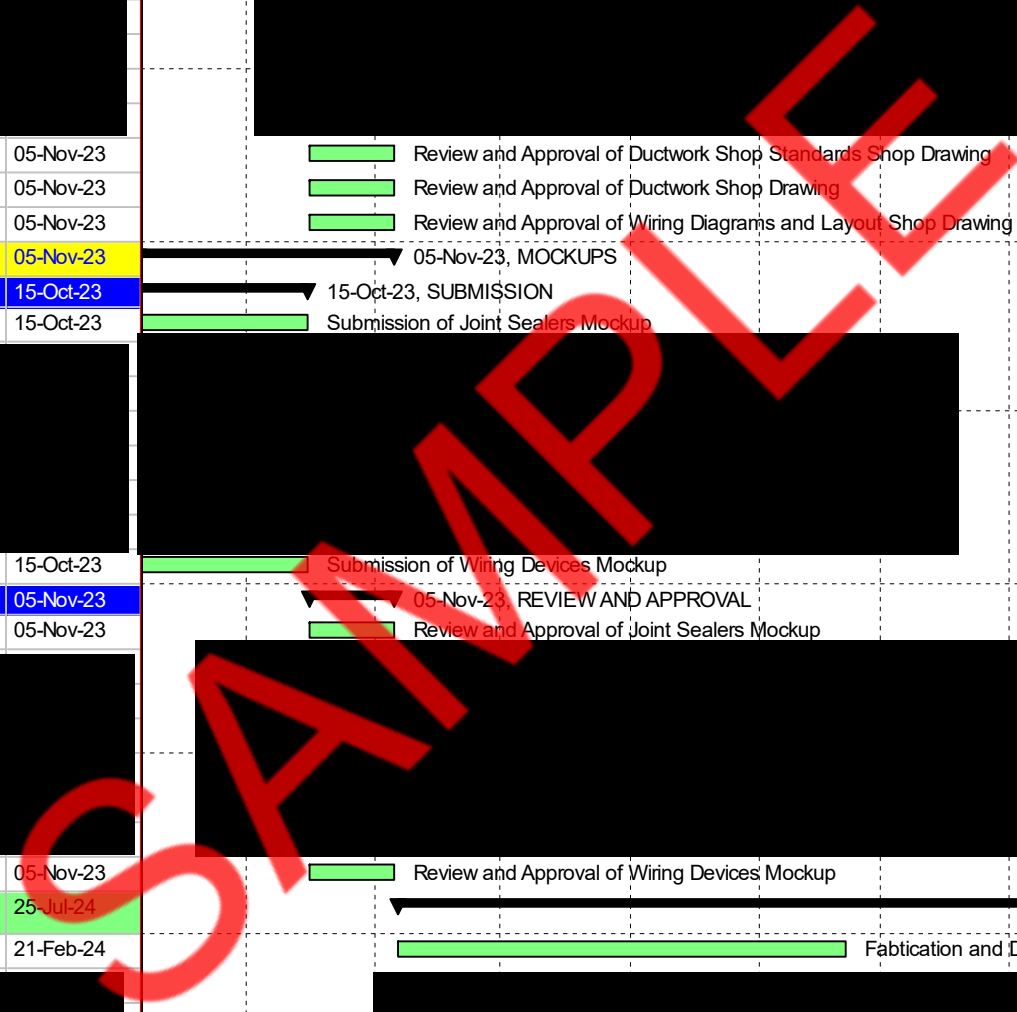

■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone
■ Actual Work
 ■ Critical Remaining Work
 ▼ summary



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024	
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
C.DEM.E	BF: Relocate Existing Conduits Under Shaft	2	14-Dec-23	15-Dec-23															
C.DEM.E	BF: Remove Fire Alarm Devices from Specified Areas	10	18-Dec-23	02-Jan-24															
MECHANICAL DEMOLITIONS					25	11-Dec-23	17-Jan-24												
C.DEM.M	BF: Cutback Existing outside air duct riser	1	11-Dec-23	11-Dec-23															
C.DEM.M	BF: Disconnect Existing outside air duct from HV-3	1	12-Dec-23	12-Dec-23															
[Redacted]																			
C.DEM.M	BF: Remove ass. LPS and LPC piping	1	10-Jan-24	10-Jan-24															
C.DEM.M	BF: Remove Existing Supply Air duct for HV-2	1	11-Jan-24	11-Jan-24															
[Redacted]																			
FINISHING DEMOLITIONS					12	18-Jan-24	02-Feb-24												
C.DEM.F	BF: Remove Concrete Pad	1	18-Jan-24	18-Jan-24															
[Redacted]																			
EXECUTION WORKS					61	24-Jan-24	22-Apr-24												
FINISHING WORKS					51	24-Jan-24	08-Apr-24												
C.EXE.FI	BF: Install new concrete pad	8	24-Jan-24	02-Feb-24															
[Redacted]																			
C.EXE.FI	BF: Finishing CID Inspection/Approval	1	08-Apr-24	08-Apr-24															
MECHANICAL WORKS					45	24-Jan-24	28-Mar-24												
C.EXE.M	BF: Install Duct Work Ph1	10	24-Jan-24	06-Feb-24															
[Redacted]																			
C.EXE.M	BF: Install Sound Attenuator	1	12-Mar-24	12-Mar-24															
C.EXE.M	BF: Install Sensor	1	13-Mar-24	13-Mar-24															
[Redacted]																			
C.EXE.M	BF: Mechanical CID Inspection/Approval	1	28-Mar-24	28-Mar-24															
ELECTRICAL WORKS					11	08-Apr-24	22-Apr-24												
C.EXE.E	BF: Re-Feed Power to Fan F-2	1	08-Apr-24	08-Apr-24															
[Redacted]																			
C.EXE.E	BF: Electrical CID Inspection/Approval	1	22-Apr-24	22-Apr-24															
FIRST FLOOR					22	16-Apr-24	15-May-24												
DEMOLITION WORKS					2	16-Apr-24	17-Apr-24												
ELECTRICAL DEMOLITIONS					1	16-Apr-24	16-Apr-24												
C.DEM.E	1F: Disconnect Power to KEF-1	1	16-Apr-24	16-Apr-24															

SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ▼ summary



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024		Qtr 4, 2024
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
MECHANICAL DEMOLITIONS																	
		2	16-Apr-24	17-Apr-24													
EXECUTION WORKS																	
		20	18-Apr-24	15-May-24													
FINISHING WORKS																	
		7	29-Apr-24	07-May-24													
	C.EXE.F. 1F: Finishing CID Inspection/Approval	1	07-May-24	07-May-24													
MECHANICAL WORKS																	
		7	18-Apr-24	26-Apr-24													
	C.EXE.M. 1F: Connect Sound Attenuator to Riser Shafts	1	18-Apr-24	18-Apr-24													
	C.EXE.M. 1F: Install signge on each cleanout door	1	25-Apr-24	25-Apr-24													
	C.EXE.M. 1F: Install new glucol pipes from Cellar to Fan RM-2	7	18-Apr-24	26-Apr-24													
	C.EXE.M. 1F: Mechanical CID Inspection/Approval	1	26-Apr-24	26-Apr-24													
ELECTRICAL WORKS																	
		7	07-May-24	15-May-24													
	C.EXE.E. 1F: Reuse Existing Feeder and Motor Starter for kitchen	1	07-May-24	07-May-24													
SECOND FLOOR																	
		29	16-May-24	26-Jun-24													
DEMOLITION WORKS																	
		4	16-May-24	21-May-24													
MECHANICAL DEMOLITIONS																	
		4	16-May-24	21-May-24													
	C.DEM.M 2F: Remove Existing Grease Exhaust duct	1	16-May-24	16-May-24													
	C.DEM.M 2F: Remove Existing Plenum Box	1	17-May-24	17-May-24													
	C.DEM.M 2F: Remove Louver	1	20-May-24	20-May-24													
	C.DEM.M 2F: Remove Volume Damper	1	21-May-24	21-May-24													
EXECUTION WORKS																	
		25	22-May-24	26-Jun-24													
FINISHING WORKS																	
		9	05-Jun-24	17-Jun-24													
	C.EXE.F. 2F: Finishing CID Inspection/Approval	1	17-Jun-24	17-Jun-24													
MECHANICAL WORKS																	
		14	22-May-24	11-Jun-24													
	C.EXE.M. 2F: Install new plenum box	2	22-May-24	23-May-24													
	C.EXE.M. 2F: Mechanical CID Inspection/Approval	1	11-Jun-24	11-Jun-24													
ELECTRICAL WORKS																	
		11	12-Jun-24	26-Jun-24													
	C.EXE.E. 2F: Install Fire Alarm Work	10	12-Jun-24	25-Jun-24													
THIRD FLOOR																	
		19	11-Jun-24	08-Jul-24													


SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ─── summary



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024		Qtr 3, 2024			Qtr 4, 2024	
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
EXECUTION WORKS																		
FINISHING WORKS																		
C.EXE.F.:	3F: Patch and Repair Existing Ceiling	2	18-Jun-24	19-Jun-24														
MECHANICAL WORKS																		
C.EXE.M.	3F: Install Duct Mounted Smoke Detector	2	11-Jun-24	12-Jun-24														
C.EXE.M.	3F: Mechanical CID Inspection/Approval	1	18-Jun-24	18-Jun-24														
ELECTRICAL WORKS																		
C.EXE.E.	3F: Electrical CID Inspection/Approval	1	08-Jul-24	08-Jul-24														
FOURTH FLOOR																		
EXECUTION WORKS																		
FINISHING WORKS																		
C.EXE.F.:	4F: Patch and Repair Existing Ceilings	3	28-Jun-24	02-Jul-24														
C.EXE.F.:	4F: Finishing CID Inspection/Approval	1	18-Jul-24	18-Jul-24														
MECHANICAL WORKS																		
C.EXE.M.	4F: Install new duct mounted smoke detector	2	21-Jun-24	24-Jun-24														
ELECTRICAL WORKS																		
C.EXE.E.	4F: Electrical CID Inspection/Approval	1	19-Jul-24	19-Jul-24														
FIFTH FLOOR																		
DEMOLITION WORKS																		
ELECTRICAL DEMOLITIONS																		
C.DEM.E.	5F: Remove Corridor Lighting Fixtures	1	05-Jul-24	05-Jul-24														
MECHANICAL DEMOLITIONS																		
C.DEM.M	5F: Remove Supply Grilles	5	10-Jul-24	16-Jul-24														
FINISHING DEMOLITIONS																		
C.DEM.F.	5F: Remove Corridor Ceiling	2	08-Jul-24	09-Jul-24														
EXECUTION WORKS																		
FINISHING WORKS																		
C.EXE.F.:	5F: Install Corridor Ceiling	2	24-Jul-24	25-Jul-24														
C.EXE.F.:	5F: Finishing CID Inspection/Approval	1	05-Aug-24	05-Aug-24														
MECHANICAL WORKS																		
		13	10-Jul-24	26-Jul-24														

SAMPLE

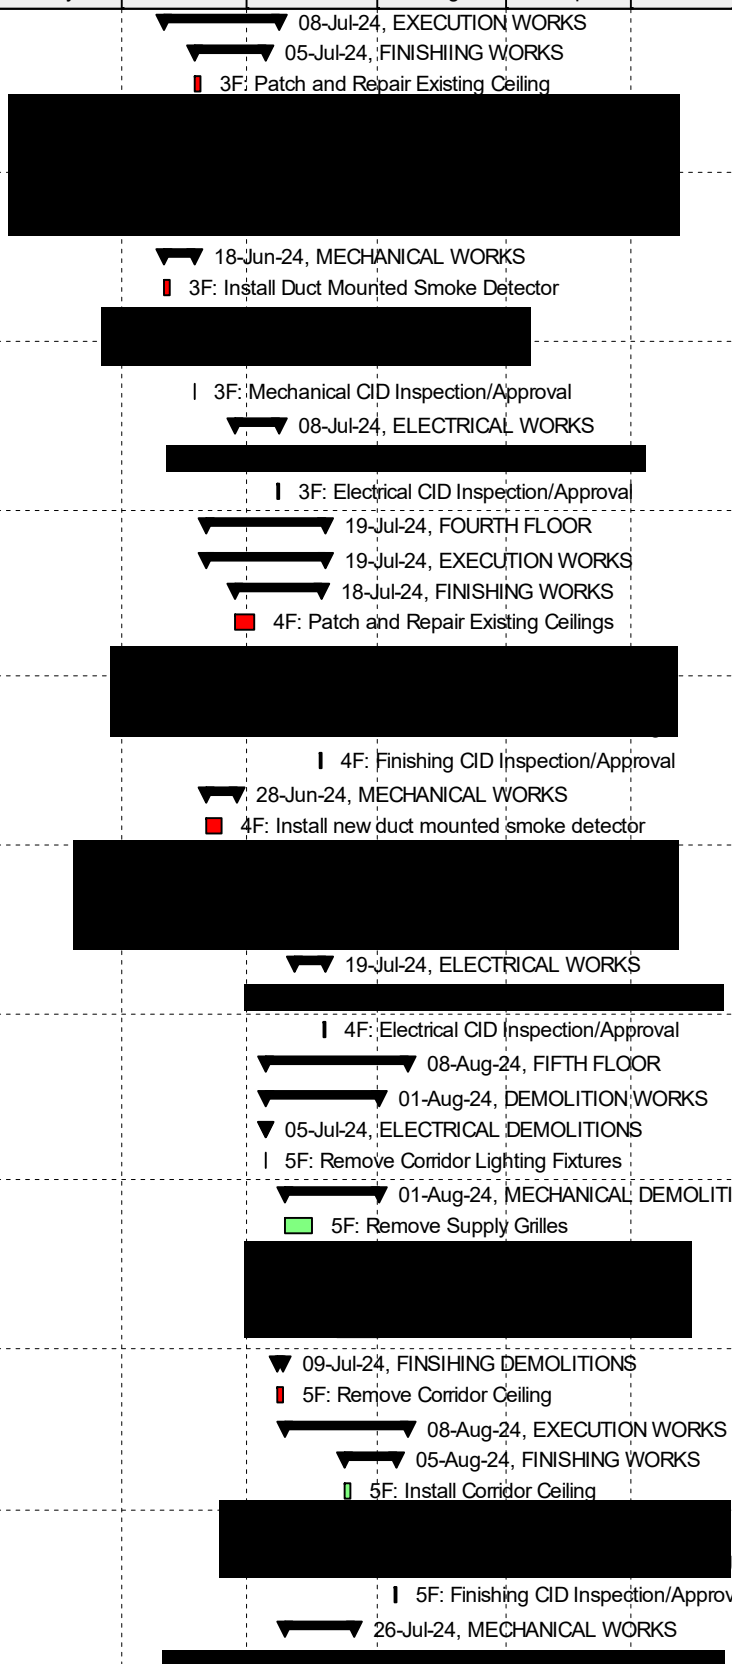

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ─ summary

Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
C.EXE.M.	5F: Install opposed blade Damper	1	17-Jul-24	17-Jul-24														
C.EXE.M.	5F: Mechanical CID Inspection/Approval	1	26-Jul-24	26-Jul-24														
ELECTRICAL WORKS					6	01-Aug-24	08-Aug-24											
C.EXE.E.	5F: Reinstall Ceiling lighting Fixtures	1	05-Aug-24	05-Aug-24														
ROOF FLOOR					21	06-Aug-24	03-Sep-24											
DEMOLITION WORKS					13	06-Aug-24	22-Aug-24											
ELECTRICAL DEMOLITIONS					13	06-Aug-24	22-Aug-24											
C.DEM.E.	RF: Remove wiring and conduits	4	06-Aug-24	09-Aug-24														
C.DEM.E.	RF: Disconnect and remove panel PP-3	3	20-Aug-24	22-Aug-24														
MECHANICAL DEMOLITIONS					4	06-Aug-24	09-Aug-24											
C.DEM.M.	RF: Remove Exhaust Fan	2	06-Aug-24	07-Aug-24														
C.DEM.M.	RF: Remove Motorized Damper	2	06-Aug-24	07-Aug-24														
EXECUTION WORKS					17	12-Aug-24	03-Sep-24											
CIVIL WORKS					6	12-Aug-24	19-Aug-24											
C.EXE.C.	RF: Install Concrete Pad	3	12-Aug-24	14-Aug-24														
C.EXE.C.	RF: Install Steel Dunnage	5	12-Aug-24	16-Aug-24														
C.EXE.C.	RF: Civil CID Inspection/Approval	1	19-Aug-24	19-Aug-24														
MECHANICAL WORKS					17	12-Aug-24	03-Sep-24											
C.EXE.M.	RF: Route new 3'G around mechanical Shaft	1	12-Aug-24	12-Aug-24														
C.EXE.M.	RF: Install new coil for GEF-1 Exhaust	3	26-Aug-24	28-Aug-24														
C.EXE.M.	RF: Install new coil for GEF-2 Exhaust	3	29-Aug-24	02-Sep-24														
ELECTRICAL WORKS					15	12-Aug-24	30-Aug-24											
C.EXE.E.	RF: Install controlling Wiring From Unit Disc. to VFD	1	12-Aug-24	12-Aug-24														
C.EXE.E.	RF: Install labels	3	26-Aug-24	28-Aug-24														
C.EXE.E.	RF: Install heating cables beneath piping	4	26-Aug-24	29-Aug-24														
C.EXE.E.	RF: Electrical CID Inspection/Approval	1	30-Aug-24	30-Aug-24														

SAMPLE

█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ── summary



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2023				Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
PROJECT CLOSEOUT		24	02-Sep-24	03-Oct-24														03-Oct-24
PCO-0020	Testing and Commissioning	22	04-Sep-24	03-Oct-24														Testing &

SAMPLE
