

SAMPLE

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone



Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Predecessors	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024
PH1-DM-110	Safe off Utilities	8	21-Nov-22	30-Nov-22	DCAC 5 Day	PH1-DM-100	Safe off Utilities					
PH1-DM-120	Move Owners Equipment	7	01-Dec-22	09-Dec-22	DCAC 5 Day	PH1-DM-110	Move Owners Equipment					
PH1-DM-130	Demolition of First Floor	15	12-Dec-22	30-Dec-22	DCAC 5 Day	PH1-DM-120	Demolition of First Floor					
PH1-DM-140	Cap Off Fire Sprinklers	3	03-Jan-23	05-Jan-23	DCAC 5 Day	PH1-DM-130	Cap Off Fire Sprinklers					
PHASE 2 BUILDING WORK												
FIRST FLOOR												
PH2-BW-FF-100	Reinforce Steel Connection	15	30-Mar-23	19-Apr-23	DCAC 5 Day	PH1-DM-100, PH1-DM-180, MS-110	Reinforce Steel Connection					
PH2-BW-FF-110	Patch Fireproofing	10	20-Apr-23	03-May-23	DCAC 5 Day	PH2-BW-FF-100	Patch Fireproofing					
PH2-BW-FF-120	Install slab infills	61	20-Jan-23	17-Apr-23	DCAC 5 Day	PH1-DM-150	Install slab infills					
PH2-BW-FF-130	Install Utilities Hangers	15	18-Apr-23	08-May-23	DCAC 5 Day	PH2-BW-FF-120	Install Utilities Hangers					
PH2-BW-FF-180	Install/Relocate data/electrical	15	04-May-23	24-May-23	DCAC 5 Day	PH2-BW-FF-160	Install/Relocate data/electrical					
PH2-BW-FF-189	Install metal Studs - South Side	15	02-Jun-23	22-Jun-23	DCAC 5 Day	PH2-BW-FF-100, PH2-BW-FF-170	Install metal Studs - South Side					
PH2-BW-FF-190	Install metal Studs - North Side	15	23-Jun-23	14-Jul-23	DCAC 5 Day	PH2-BW-FF-189	Install metal Studs - North Side					
PH2-BW-FF-200	Rough Plumbing	15	17-Jul-23	04-Aug-23	DCAC 5 Day	PH2-BW-FF-190, RER-130	Rough Plumbing					
PH2-BW-FF-210	Install metal Ceiling framing	13	17-Jul-23	02-Aug-23	DCAC 5 Day	PH2-BW-FF-190	Install metal Ceiling framing					
PH2-BW-FF-220	Install Acoustic insulation	5	03-Aug-23	09-Aug-23	DCAC 5 Day	PH2-BW-FF-210	Install Acoustic insulation					
PH2-BW-FF-230	Gypboard, Tape and finish	15	10-Aug-23	30-Aug-23	DCAC 5 Day	PH2-BW-FF-140, PH2-BW-FF-150, PH2-BW-FF-200, PH2-BW-FF-220	Gypboard, Tape and finish					
PH2-BW-FF-240	Install Ceramic tile	15	31-Aug-23	21-Sep-23	DCAC 5 Day	PH2-BW-FF-230	Install Ceramic tile					
PH2-BW-FF-250	Interior painting	15	31-Aug-23	21-Sep-23	DCAC 5 Day	PH2-BW-FF-230	Interior painting					
PH2-BW-FF-260	Install Casework	15	22-Sep-23	12-Oct-23	DCAC 5 Day	PH2-BW-FF-250	Install Casework					
PH2-BW-FF-270	Toilet access/partition	10	22-Sep-23	05-Oct-23	DCAC 5 Day	PRF-120, PH2-BW-FF-240	Toilet access/partition					
PH2-BW-FF-320	install Epoxy Floor	8	05-Sep-23	14-Sep-23	DCAC 5 Day	PH2-BW-FF-310	install Epoxy Floor					
PH2-BW-FF-330	Sethook up Kitchen equipment	12	15-Sep-23	02-Oct-23	DCAC 5 Day	PH2-BW-FF-320, PRF-140	Sethook up Kitchen equipment					
PH2-BW-FF-340	Adjust Fire Sprinklers	12	17-Jul-23	01-Aug-23	DCAC 5 Day	PH2-BW-FF-190	Adjust Fire Sprinklers					
PH2-BW-FF-350	Install acoustic ceilings	12	22-Sep-23	09-Oct-23	DCAC 5 Day	PH2-BW-FF-250	Install acoustic ceilings					
PH2-BW-FF-360	Finish HVAC	15	10-Oct-23	30-Oct-23	DCAC 5 Day	PH2-BW-FF-350, PRF-150	Finish HVAC					
PH2-BW-FF-370	Install lights in ceiling	12	10-Oct-23	25-Oct-23	DCAC 5 Day	PH2-BW-FF-350, PRF-130	Install lights in ceiling					
PH2-BW-FF-380	Finish Electrical trim	15	22-Sep-23	12-Oct-23	DCAC 5 Day	PH2-BW-FF-250	Finish Electrical trim					
PH2-BW-FF-390	Finish Fire alarm trim	15	22-Sep-23	12-Oct-23	DCAC 5 Day	PH2-BW-FF-250	Finish Fire alarm trim					
PH2-BW-FF-400	Frame in black box	12	17-Jul-23	01-Aug-23	DCAC 5 Day	PH2-BW-FF-190	Frame in black box					
PH2-BW-FF-410	Ductwork	12	02-Aug-23	17-Aug-23	DCAC 5 Day	PH2-BW-FF-400	Ductwork					
PH2-BW-FF-420	Fire sprinklers	10	02-Aug-23	15-Aug-23	DCAC 5 Day	PH2-BW-FF-400	Fire sprinklers					
PH2-BW-FF-430	Rough electrical	15	18-Aug-23	08-Sep-23	DCAC 5 Day	PH2-BW-FF-410	Rough electrical					
PH2-BW-FF-431	Gyp board wall	10	11-Sep-23	22-Sep-23	DCAC 5 Day	PH2-BW-FF-430	Gyp board wall					
PH2-BW-FF-432	Lighting grid	8	25-Sep-23	04-Oct-23	DCAC 5 Day	PH2-BW-FF-431	Lighting grid					
PH2-BW-FF-433	paintroom	8	05-Oct-23	16-Oct-23	DCAC 5 Day	PH2-BW-FF-432	paintroom					
PH2-BW-FF-434	Finish electrical/mech trim	15	17-Oct-23	06-Nov-23	DCAC 5 Day	PH2-BW-FF-433	Finish electrical/mech trim					
PH2-BW-FF-436	Av work	15	17-Oct-23	06-Nov-23	DCAC 5 Day	PH2-BW-FF-433	Av work					
PH2-BW-FF-437	Polished floor	15	17-Oct-23	06-Nov-23	DCAC 5 Day	PH2-BW-FF-433	Polished floor					
PH2-BW-FF-440	Protect floor	2	07-Nov-23	08-Nov-23	DCAC 5 Day	PH2-BW-FF-437	Protect floor					
PH2-BW-FF-450	Install Casework at polished floor	5	09-Nov-23	16-Nov-23	DCAC 5 Day	PH2-BW-FF-440	Install Casework at polished floor					
PH2-BW-FF-460	Install Sealed Concrete	4	22-Sep-23	27-Sep-23	DCAC 5 Day	PH2-BW-FF-250	Install Sealed Concrete					
PH2-BW-FF-470	Install Flooring	10	31-Oct-23	14-Nov-23	DCAC 5 Day	PH2-BW-FF-360, PH2-BW-FF-380, PH2-BW-FF-390, PH2-BW-FF-420	Install Flooring					


SAMPLE

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone



Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Predecessors	Timeline													
							Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024								
PH2-BW-FF-520	Install Storefront	10	10-Aug-23	23-Aug-23	DCAC 5 Day	PRF-110, PH2-BW-FF-510														
PH2-BW-FF-530	Install CMU walls	10	17-Jul-23	28-Jul-23	DCAC 5 Day	PH2-BW-FF-190														
PH2-BW-FF-540	Install roll up door	5	31-Jul-23	04-Aug-23	DCAC 5 Day	PH2-BW-FF-530														
PH2-BW-FF-550	Complete finishes in Kiln Room	15	07-Aug-23	25-Aug-23	DCAC 5 Day	PH2-BW-FF-540, PH2-BW-FF-530														
PH2-BW-FF-560	Set equipment in Kiln room	5	28-Aug-23	01-Sep-23	DCAC 5 Day	PH2-BW-FF-550														
PH2-BW-FF-570	Clean up	3	01-Dec-23	05-Dec-23	DCAC 5 Day	PH2-BW-FF-260, PH2-BW-FF-270, PH2-BW-FF-300, PH2-BW-FF-330, PH2-BW-FF-340														
SECOND FLOOR		121	18-Apr-23	06-Oct-23	DCAC 5 Day															
PH2-BW-SF-160	Install metal Studs	10	02-May-23	15-May-23	DCAC 5 Day	PH2-BW-SF-100														
PH2-BW-SF-170	Rough Plumbing	10	16-May-23	30-May-23	DCAC 5 Day	PH2-BW-SF-160														
PH2-BW-SF-180	Install metal Ceiling framing	13	16-May-23	02-Jun-23	DCAC 5 Day	PH2-BW-SF-110, PH2-BW-SF-160														
PH2-BW-SF-190	Install Acoustic insulation	7	05-Jun-23	13-Jun-23	DCAC 5 Day	PH2-BW-SF-180														
PH2-BW-SF-200	Gypboard, Tape and finish	12	27-Jun-23	13-Jul-23	DCAC 5 Day	PH2-BW-SF-140, PH2-BW-SF-150, PH2-BW-SF-170, PH2-BW-SF-190														
PH2-BW-SF-210	Install Ceramic tile	10	14-Jul-23	27-Jul-23	DCAC 5 Day	PH2-BW-SF-200														
PH2-BW-SF-220	Interior painting	13	14-Jul-23	01-Aug-23	DCAC 5 Day	PH2-BW-SF-200														
PH2-BW-SF-230	Install Casework	10	02-Aug-23	15-Aug-23	DCAC 5 Day	PH2-BW-SF-220														
PH2-BW-SF-240	Toilet access/partition	10	28-Jul-23	10-Aug-23	DCAC 5 Day	PRF-120, PH2-BW-SF-210														
PH2-BW-SF-250	Install Door Frames	10	16-May-23	30-May-23	DCAC 5 Day	PH2-BW-SF-160														
PH2-BW-SF-260	Install Doors/Hardware	10	31-May-23	13-Jun-23	DCAC 5 Day	PH2-BW-SF-250														
PH2-BW-SF-270	Finish Doors	10	14-Jun-23	27-Jun-23	DCAC 5 Day	PH2-BW-SF-260														
PH2-BW-SF-280	Adjust Fire Sprinklers	10	16-May-23	30-May-23	DCAC 5 Day	PH2-BW-SF-160, RER-190, RER-110														
PH2-BW-SF-290	Install acoustic ceilings	10	02-Aug-23	15-Aug-23	DCAC 5 Day	PH2-BW-SF-220														
PH2-BW-SF-300	Finish HVAC	12	16-Aug-23	31-Aug-23	DCAC 5 Day	PH2-BW-SF-290														
PH2-BW-SF-310	Finish Electrical trim	12	02-Aug-23	17-Aug-23	DCAC 5 Day	PH2-BW-SF-220														
PH2-BW-SF-320	Finish Fire alarm trim	10	02-Aug-23	15-Aug-23	DCAC 5 Day	PH2-BW-SF-220														
PH2-BW-SF-330	Install Acoustic ceiling panels	10	01-Sep-23	15-Sep-23	DCAC 5 Day	PH2-BW-SF-280, PH2-BW-SF-300														
PH2-BW-SF-340	Install Flooring	8	18-Sep-23	27-Sep-23	DCAC 5 Day	PH2-BW-SF-230, PH2-BW-SF-330														
PH2-BW-SF-350	Protect floor	5	28-Sep-23	04-Oct-23	DCAC 5 Day	PH2-BW-SF-340														
PH2-BW-SF-360	Complete misc. trim/signage Etc.	10	02-Aug-23	15-Aug-23	DCAC 5 Day	PH2-BW-SF-220														
PH2-BW-SF-370	Clean Up	2	05-Oct-23	06-Oct-23	DCAC 5 Day	PH2-BW-SF-240, PH2-BW-SF-310, PH2-BW-SF-320, PH2-BW-SF-350, PH2-BW-SF-360														
ROOF WORK		75	16-Aug-23	04-Dec-23	DCAC 5 Day															
RFW-100	Demo Roofing (Start Spring)	10	16-Aug-23	29-Aug-23	DCAC 5 Day	PH2-BW-SF-360														
RFW-110	Readjust/install Curbs	10	30-Aug-23	13-Sep-23	DCAC 5 Day	RFW-100														
RFW-120	Install Skylights/ Supports	10	30-Aug-23	13-Sep-23	DCAC 5 Day	RFW-100														
RFW-130	High roof forst	15	14-Sep-23	04-Oct-23	DCAC 5 Day	RFW-110, RFW-120														
RFW-131	low roof	15	05-Oct-23	25-Oct-23	DCAC 5 Day	RFW-130														
RFW-140	Install Mechanical Equipment	15	26-Oct-23	16-Nov-23	DCAC 5 Day	RFW-131														
RFW-150	Complete Flashing	7	17-Nov-23	29-Nov-23	DCAC 5 Day	RFW-140														
RFW-160	Hook Up mechanical Equipment	10	17-Nov-23	04-Dec-23	DCAC 5 Day	PRF-160, RFW-140														
SITWORK		79	11-Aug-23	05-Dec-23	DCAC 5 Day															
STW-130	Landscaping	18	24-Oct-23	17-Nov-23	DCAC 5 Day	STW-100, STW-120														
STW-140	Site Furnishings	15	21-Aug-23	11-Sep-23	DCAC 5 Day	STW-100														
STW-150	Pavers	5	12-Sep-23	18-Sep-23	DCAC 5 Day	STW-110														
STW-160	Punch out Sitework	10	20-Nov-23	05-Dec-23	DCAC 5 Day	STW-130, STW-140, STW-150														
CLOSEOUT		33	06-Dec-23	22-Jan-24																
CO-100	Weather Allowance	14	06-Dec-23	19-Dec-23	DCAC 7 Day	PH2-BW-FF-570, PH2-BW-SF-370, RFW-150, RFW-160, STW-160														
CO-110	Substantial Completion	0		19-Dec-23	DCAC 5 Day	CO-100														
CO-120	Start Up /Balance HVAC System	8	20-Dec-23	01-Jan-24	DCAC 5 Day	CO-110														
CO-130	Fire Alarm Testing	5	20-Dec-23	27-Dec-23	DCAC 5 Day	CO-110														
CO-140	Punchlist Review	10	02-Jan-24	15-Jan-24	DCAC 5 Day	CO-120, CO-130														
CO-150	Final Inspections	5	16-Jan-24	22-Jan-24	DCAC 5 Day	CO-140														

SAMPLE

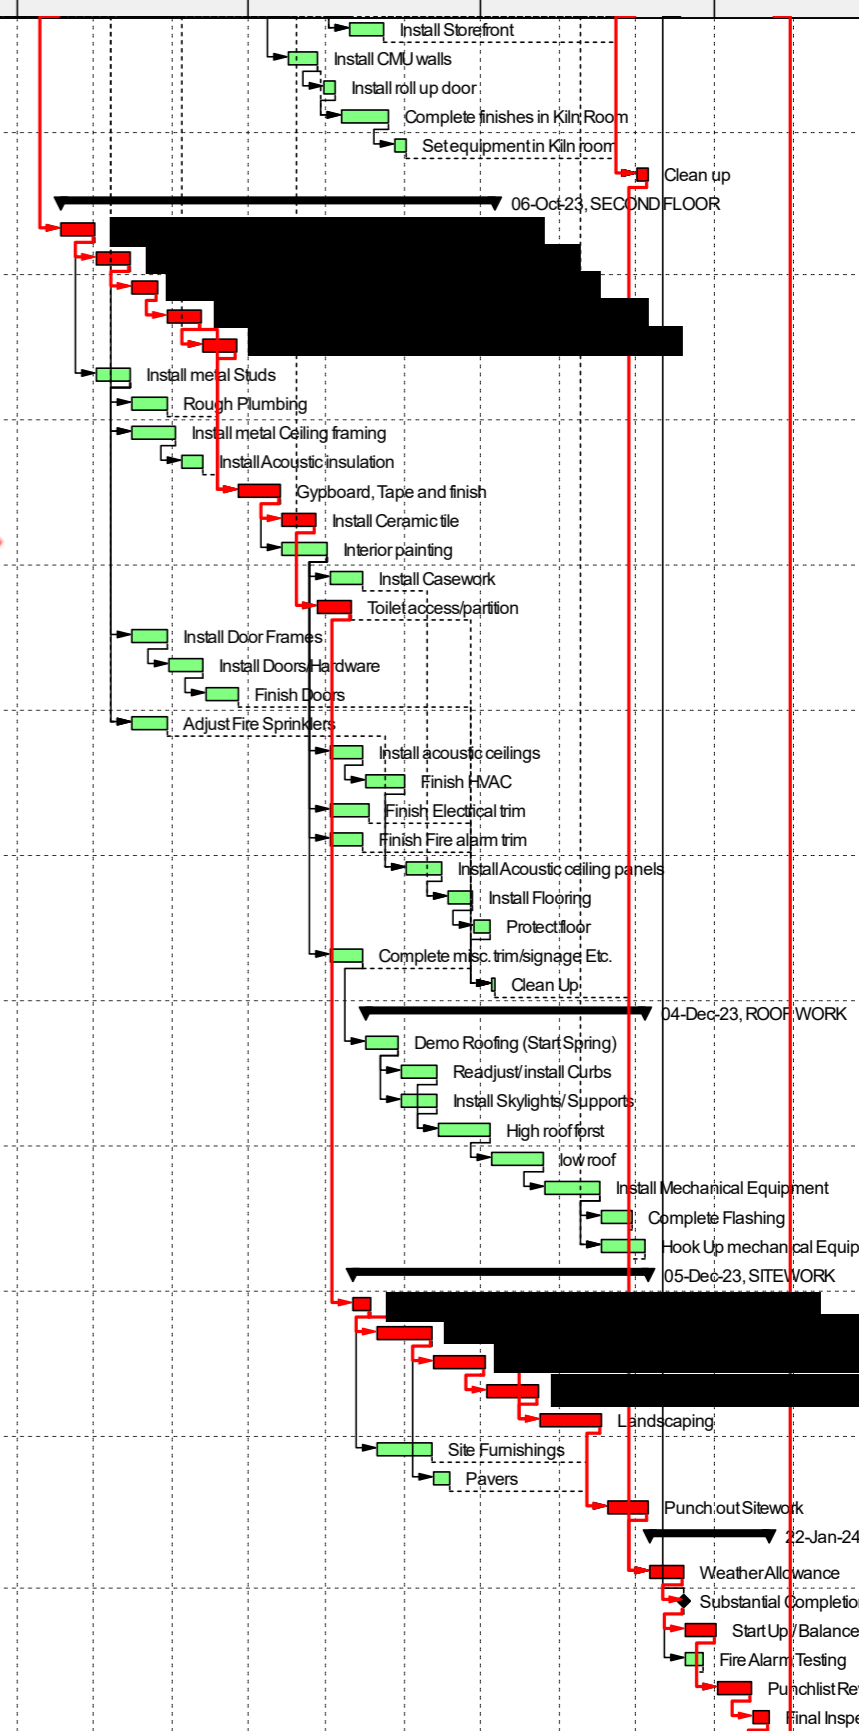

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining W...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone



Activity ID	Activity Name	Original Duration	Start	Finish	Calendar	Predecessors	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024
CO-160	Final Completion	0		22-Jan-24*	DCAC 5 Day	CO-150						Final Com

SAMPLE
