C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal & Rehab NOV-23 UPDATE		669	05-Jun-23 A	31-Dec-25	
MILESTONES		667	05-Jun-23 A	31-Dec-25	
001	Notice to Begin Work	0	05-Jun-23 A		100%
002	Contract Completion (12-31-2025)	0		31-Dec-25*	0%
ENGINEERING		236	05-Jun-23 A	02-Feb-24	
SUBMISSION		236	05-Jun-23 A	03-Jan-24	
005	IIPP	2	05-Jun-23 A	06-Jun-23 A	100%
006	Written Safety Program and Code of Safe Practices	12	05-Jun-23 A	19-Jun-23 A	100%
007	[redacted]				
008					
009					
010					
011					
012	SWPPP	17	05-Jun-23 A	26-Jun-23 A	100%
013	Pre-Construction Video and Photos	26	05-Jun-23 A	16-Jul-23 A	100%
014	Hazardous Waste Disposal Plan	26	05-Jun-23 A	09-Jul-23 A	100%
015	Name of Disposal Facility	26	05-Jun-23 A	09-Jul-23 A	100%
016	Name/representative of Transporting Agency	26	05-Jun-23 A	09-Jul-23 A	100%
017	Mobilization List of Equipment	40	05-Jun-23 A	19-Jul-23 A	100%
018	Plans, Methods and Sequences for Selective Demolition	35	05-Jun-23 A	24-Jul-23 A	100%
019	Methods and Detailed Dewatering Plan	30	05-Jun-23 A	13-Jul-23 A	100%
020	[redacted]				
021					
022					
023					
024					
025	Backfill Source and Gradation	151	05-Jun-23 A	03-Jan-24	84.11%
026	Source and Gradation of Drain Rock and Sand Filter	151	05-Jun-23 A	03-Jan-24	84.11%
027	Excavation Plan	151	05-Jun-23 A	03-Jan-24	84.11%
028	Gradation, Density and Source for RSP	151	05-Jun-23 A	03-Jan-24	84.11%
029	Geotextile Fabric Product Data	151	05-Jun-23 A	03-Jan-24	84.11%
030	Steel Pipe and Fitting Product Info and MFG Literature	151	05-Jun-23 A	03-Jan-24	84.11%
031	Steel Pipe and Fitting Material Certification	151	05-Jun-23 A	03-Jan-24	84.11%
032	Steel Pipe and Fitting QC Plan	151	05-Jun-23 A	03-Jan-24	84.11%
033	Pipe Layout Drawings	151	05-Jun-23 A	03-Jan-24	84.11%
034	Steel Pipe and Fitting Fabrication and Installation Sequence	151	05-Jun-23 A	03-Jan-24	84.11%
035	Steel Pipe and Fitting Welding Procedure and Certs.	151	05-Jun-23 A	12-Nov-23 A	100%
036	AB Gradation and Certificates	151	05-Jun-23 A	13-Nov-23 A	100%
037	AB Grading and Compaction Methods and Equip	151	05-Jun-23 A	03-Jan-24	84.11%
038	Chain Link Fence Manufacturers Cert.	151	05-Jun-23 A	03-Jan-24	84.11%
039	[redacted]				
040					
041					
042					
043					
044	Seeding Certification of Materials	151	05-Jun-23 A	03-Jan-24	84.11%
045	Concrete Formwork	151	05-Jun-23 A	27-Nov-23 A	100%

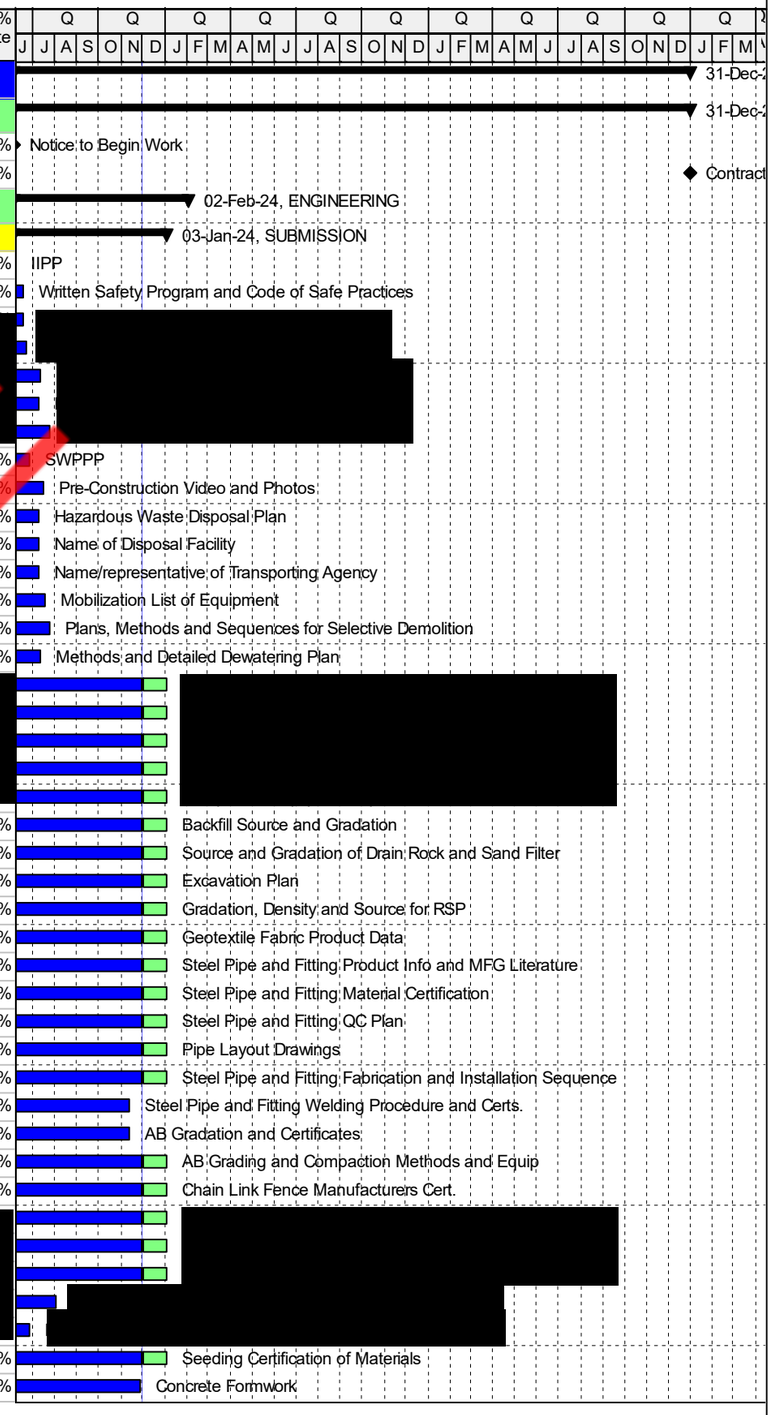

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
046	Reinforcing Steel Shop Drawings	151	05-Jun-23 A	21-Nov-23 A	100%
047	Concrete Conveyance and lift Drawings	151	05-Jun-23 A	15-Nov-23 A	100%
048	[redacted]				
049					
050					
051					
052					
053	Grouting Procedure, Equipment and Quality Control	151	05-Jun-23 A	03-Jan-24	84.11%
054	Welding Procedure Specifications and Qualification Test Results	151	05-Jun-23 A	09-Oct-23 A	100%
055	Welding Preheating Procedures	151	05-Jun-23 A	17-Nov-23 A	100%
056	Welding Assembly Sequences	151	05-Jun-23 A	03-Jan-24	84.11%
057	Stress Relieving Procedures	151	05-Jun-23 A	13-Nov-23 A	100%
058	Quality Assurance Plan	151	05-Jun-23 A	13-Nov-23 A	100%
059	Quality Control Program and Procedures Manual	151	05-Jun-23 A	13-Nov-23 A	100%
060	Certified Material and Test Reports	151	05-Jun-23 A	03-Jan-24	84.11%
061	Misc. Metal Product Data	151	05-Jun-23 A	03-Jan-24	84.11%
062	Misc. Metal Shop Drawings	151	05-Jun-23 A	03-Jan-24	84.11%
063	[redacted]				
064					
065					
066					
067					
068	Assembly Sequence of Stop Log Fabrication	151	05-Jun-23 A	03-Jan-24	84.11%
069	Shop Test Procedures and Schedules	151	05-Jun-23 A	03-Jan-24	84.11%
070	Field Test Procedures and Schedules	151	05-Jun-23 A	03-Jan-24	84.11%
071	Sealant Certification of Compliance	151	05-Jun-23 A	03-Jan-24	84.11%
072	Sealant Technical Data Guides	151	05-Jun-23 A	03-Jan-24	84.11%
073	Metalizing Product Data	151	05-Jun-23 A	03-Jan-24	84.11%
074	General Coating Product Data	151	05-Jun-23 A	03-Jan-24	84.11%
075	Coating Manufacturers Certification of Compliance	151	05-Jun-23 A	03-Jan-24	84.11%
076	Work Plan for Video, Photo and 3-D Survey Inspection of Culvert Pipes and Gate Structure	151	05-Jun-23 A	03-Jan-24	84.11%
077	Grounding Product Catalog Data	151	05-Jun-23 A	03-Jan-24	84.11%
078	Raceways and Boxes Product Data	151	05-Jun-23 A	03-Jan-24	84.11%
079	Conduit System Layout	151	05-Jun-23 A	03-Jan-24	84.11%
REVIEW AND APPROVAL		241	07-Jun-23 A	02-Feb-24	
081	IIPP	1	07-Jun-23 A	07-Jun-23 A	100%
082	Written Safety Program and Code of Safe Practices	2	20-Jun-23 A	22-Jun-23 A	100%
083	Site Specific Emergency Response Plan	2	20-Jun-23 A	22-Jun-23 A	100%
084	[redacted]				
085					
086					
087					
088					
089	File SWPPP NOI	5	27-Jun-23 A	21-Jul-23 A	100%
090	Pre-Construction Video and Photos	10	17-Jul-23 A	11-Aug-23 A	100%
091	Hazardous Waste Disposal Plan	7	10-Jul-23 A	17-Jul-23 A	100%
092	Name of Disposal Facility	7	10-Jul-23 A	17-Jul-23 A	100%
093	Name/representative of Transporting Agency	7	10-Jul-23 A	17-Jul-23 A	100%

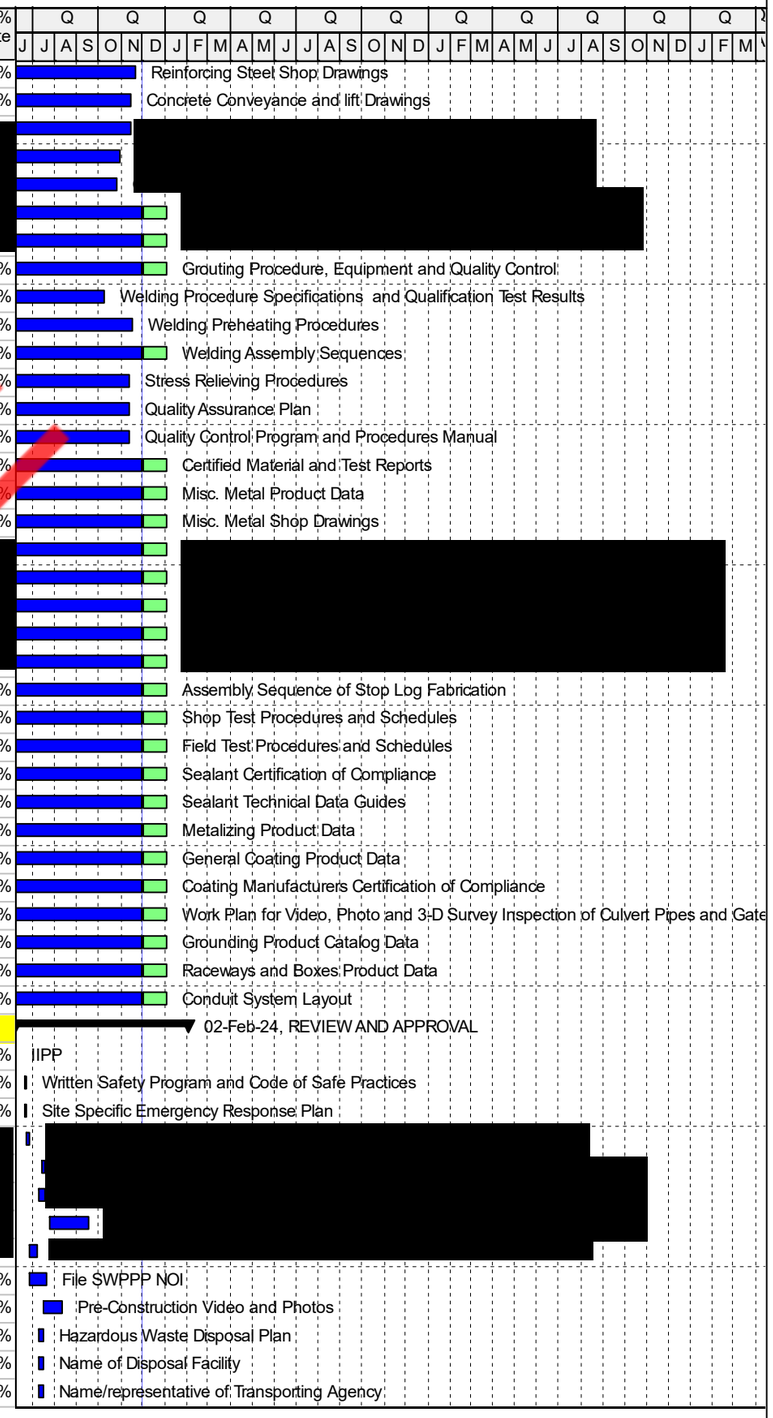

SAMPLE

Actual Work | Critical Remaining Work | Summary | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
094	Mobilization List of Equipment	7	20-Jul-23 A	01-Aug-23 A	100%
095	[redacted]				
096					
097					
098					
099					
100	Excavation Equipment Specs and Methods	30	04-Jan-24	02-Feb-24	0%
101	Compaction Equipment Specs	30	04-Jan-24	02-Feb-24	0%
102	Backfill Source and Gradation	30	04-Jan-24	02-Feb-24	0%
103	Source and Gradation of Drain Rock and Sand Filter	30	04-Jan-24	02-Feb-24	0%
104	Excavation Plan	30	04-Jan-24	02-Feb-24	0%
105	Gradation, Density and Source for RSP	30	04-Jan-24	02-Feb-24	0%
106	Geotextile Fabric Product Data	30	04-Jan-24	02-Feb-24	0%
107	Steel Pipe and Fitting Product Info and MFG Literature	30	04-Jan-24	02-Feb-24	0%
108	[redacted]				
109					
110					
111					
112					
113	AB Gradation and Certificates	30	01-Dec-23	30-Dec-23	0%
114	AB Grading and Compaction Methods and Equip	30	04-Jan-24	02-Feb-24	0%
115	Chain Link Fence Manufacturers Cert.	30	04-Jan-24	02-Feb-24	0%
116	Chain Link Fence Product Data	30	04-Jan-24	02-Feb-24	0%
117	Chain Link Fence Shop Drawings	30	04-Jan-24	02-Feb-24	0%
118	Chain Link Fence Cert of performance Criteria	30	04-Jan-24	02-Feb-24	0%
119	Bird Nesting Management Plan	30	04-Aug-23 A	02-Sep-23 A	100%
120	Bird Deterrent Product Data	30	14-Jul-23 A	02-Aug-23 A	100%
121	Seeding Certification of Materials	30	04-Jan-24	02-Feb-24	0%
122	Concrete Formwork	30	27-Nov-23 A	28-Nov-23 A	100%
123	Reinforcing Steel Shop Drawings	30	21-Nov-23 A	08-Dec-23	75%
124	Concrete Conveyance and lift Drawings	30	15-Nov-23 A	17-Nov-23 A	100%
125	Concrete Lift Drawings	30	15-Nov-23 A	17-Nov-23 A	100%
126	Ready-mix Concrete Product Data	30	30-Oct-23 A	31-Oct-23 A	100%
127	CLSM Product Data	30	26-Oct-23 A	31-Oct-23 A	100%
128	[redacted]				
129					
130					
131					
132					
133					
134	Stress Relieving Procedures	30	13-Nov-23 A	17-Nov-23 A	100%
135	Quality Assurance Plan	30	13-Nov-23 A	17-Nov-23 A	100%
136	Quality Control Program and Procedures Manual	30	13-Nov-23 A	17-Nov-23 A	100%
137	Certified Material and Test Reports	30	04-Jan-24	02-Feb-24	0%
138	Misc. Metal Product Data	30	04-Jan-24	02-Feb-24	0%
139	Misc. Metal Shop Drawings	30	04-Jan-24	02-Feb-24	0%
140	Misc. Metal Welder Certificates	30	04-Jan-24	02-Feb-24	0%
141	Stop Log Product Data and Catalogs	30	04-Jan-24	02-Feb-24	0%

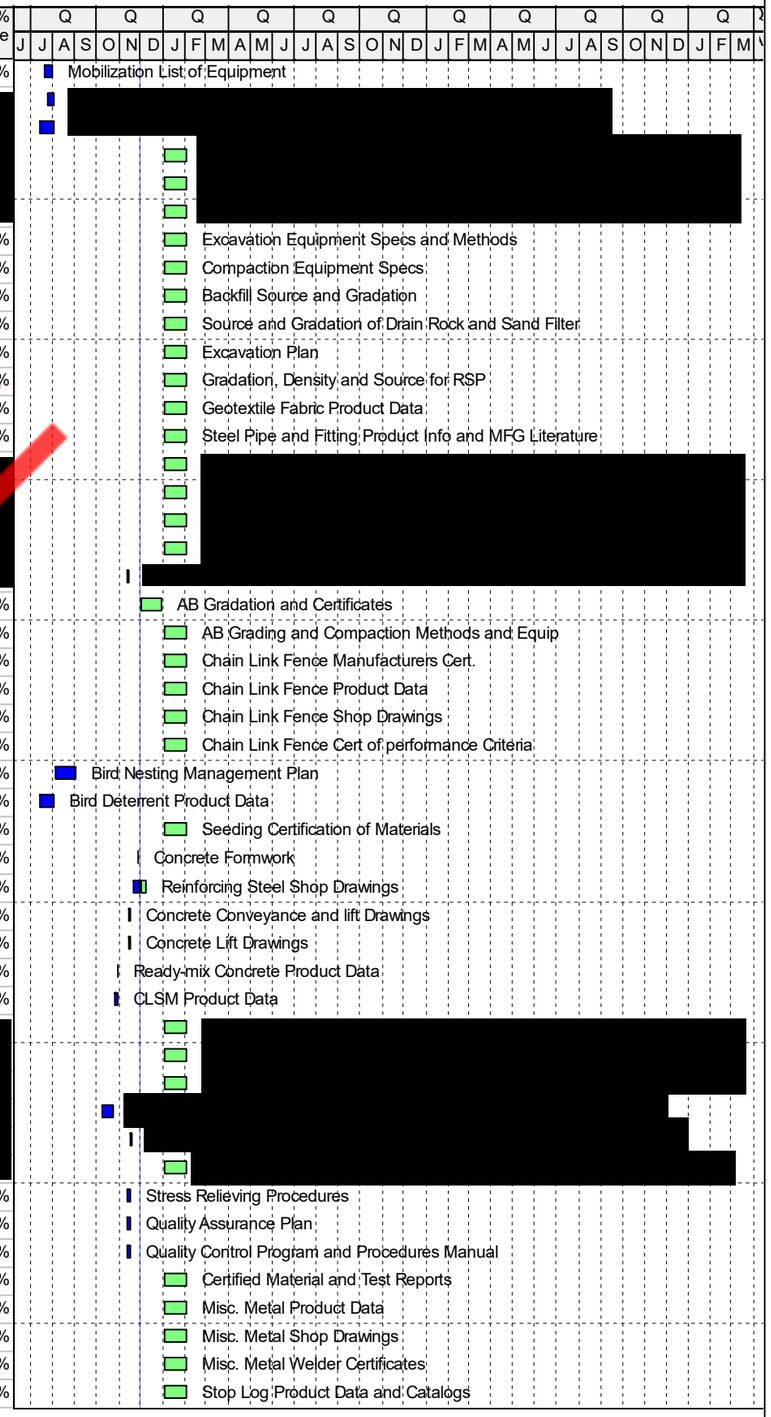

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
142	Stop Log Shop Drawings	30	04-Jan-24	02-Feb-24	0%
143	Plans and Procedures for Fabrication and Installation of Stop Logs	30	04-Jan-24	02-Feb-24	0%
144	[redacted]				
145					
146					
147					
148					
149					
150	Metalizing Product Data	30	04-Jan-24	02-Feb-24	0%
151	General Coating Product Data	30	04-Jan-24	02-Feb-24	0%
152	Coating Manufacturers Certification of Compliance	30	04-Jan-24	02-Feb-24	0%
153	Work Plan for Video, Photo and 3-D Survey Inspection of Culvert Pipes and Gate Structure	30	04-Jan-24	02-Feb-24	0%
154	Grounding Product Catalog Data	30	04-Jan-24	02-Feb-24	0%
155	Raceways and Boxes Product Data	30	04-Jan-24	02-Feb-24	0%
156	Conduit System Layout	30	04-Jan-24	02-Feb-24	0%
PROCUREMENT		60	03-Feb-24	02-Apr-24	
158	Stop Log Panels	60	03-Feb-24	02-Apr-24	0%
159	[redacted]				
160					
161					
162	Handrail	60	03-Feb-24	02-Apr-24	0%
CONSTRUCTION		669	05-Jun-23 A	31-Dec-25	
Construction Season 1 - 2023		669	05-Jun-23 A	31-Dec-25	
164	Migratory Bird Nesting Season (Effects Building Demo Work)	88	05-Jun-23 A	31-Aug-23 A	100%
165	Site Mobilization 2023	2	07-Aug-23 A	08-Aug-23 A	100%
166	Site Demobilization 2023	2	24-Oct-23 A	25-Oct-23 A	100%
167	2023 GGS No Work Period (No Ground Disturbing Work)	210	01-Oct-23 A	30-Apr-24	27.62%
168	Project Float	808	24-Oct-23 A	31-Dec-25	5.69%
Abandoned Pumping Plant No. 2		82	07-Aug-23 A	01-Dec-23	
171	Close flap gates and screw gates - DWR	1	07-Aug-23 A	07-Aug-23 A	100%
172	Close Irrigation Ditch Inlet Gates-DWR	1	07-Aug-23 A	07-Aug-23 A	100%
173	Install Exclusion Fencing	1	08-Aug-23 A	14-Aug-23 A	100%
174	Install BMPs	1	08-Aug-23 A	10-Aug-23 A	100%
175	[redacted]				
176					
177					
178					
179					
180					
181	Hazardous Abatement	6	07-Sep-23 A	13-Sep-23 A	100%
182	Demo Existing Building @ Abandoned Pumping Plant	6	20-Sep-23 A	03-Oct-23 A	100%
183	Install Bird Deterrent Mesh	1	01-Dec-23	01-Dec-23	0%
184	Remove Dewatering System	1	10-Oct-23 A	10-Oct-23 A	100%
185	Remove Exclusion fencing and BMPs	1	13-Oct-23 A	13-Oct-23 A	100%
Abandoned Pumping Plant No. 1		83	22-Aug-23 A	04-Dec-23	
187	Close flap gates and screw gates - DWR	1	01-Sep-23 A	01-Sep-23 A	100%
188	Close Irrigation Ditch Inlet Gates-DWR	1	01-Sep-23 A	01-Sep-23 A	100%
189	Clean and Close Gate with Missing Actuator (T&M)	3	01-Sep-23 A	01-Sep-23 A	100%

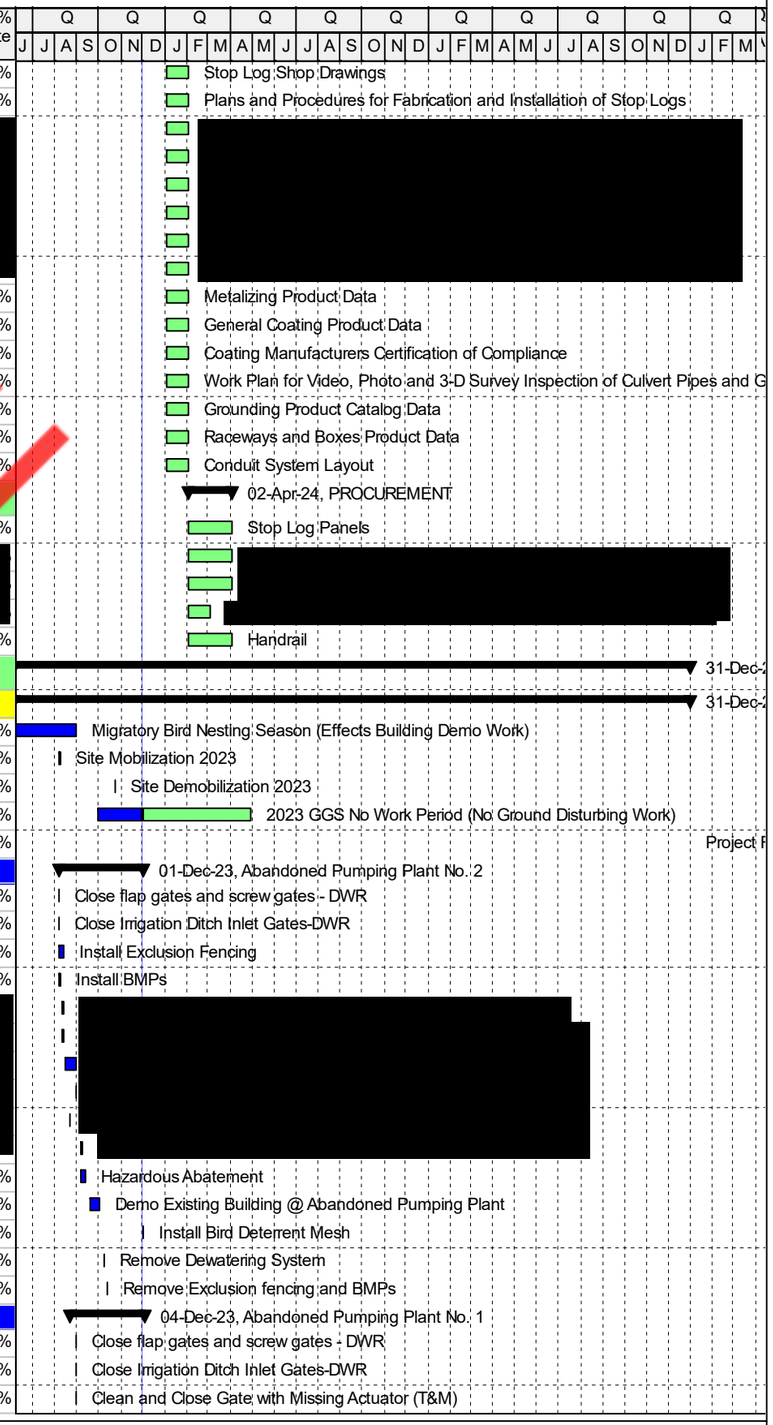

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
190	Install Exclusion Fencing	1	28-Aug-23 A	29-Aug-23 A	100%
191	Install BMPs	1	22-Aug-23 A	23-Aug-23 A	100%
192	Clear and Grub Work Area	2	23-Aug-23 A	24-Aug-23 A	100%
193	[redacted]				
194					
195					
196					
197					
198					
199	Install Bird Deterrent Mesh	1	04-Dec-23	04-Dec-23	0%
200	Remove Dewatering Pumps	1	12-Oct-23 A	12-Oct-23 A	100%
201	Remove Exclusion Fence and BMP's	1	13-Oct-23 A	13-Oct-23 A	100%
Construction Season 2- 2024		542	28-Nov-23 A	31-Dec-25	
203	Migratory Bird Nesting Season (Only affects work if Nesting Birds are Found in Work Area)	213	01-Feb-24	31-Aug-24*	0%
204	Bird Nesting Survey/ Monitoring	61	01-Feb-24*	25-Apr-24	0%
205	PG&E to Relocated Overhead Utilities	32	01-Dec-23	01-Jan-24*	0%
206	Site Mobilization 2024	2	01-May-24	02-May-24	0%
207	Site Demobilization 2024	3	04-Sep-24	06-Sep-24	0%
208	2024 GGS No Work Period (No Ground Disturbing Work)	212	01-Oct-24*	30-Apr-25	0%
209	Project Float	484	04-Sep-24	31-Dec-25	0%
Abandoned Pumping Plant No. 1		126	28-Nov-23 A	30-Jul-24	
General Site Work		125	05-Feb-24	30-Jul-24	
213	Install Exclusion Fencing	1	07-May-24	07-May-24	0%
214	Install BMPs	1	08-May-24	08-May-24	0%
215	[redacted]				
216					
217					
218	Remove Exclusion Fencing and BMPs	1	30-Jul-24	30-Jul-24	0%
Dewatering Work		59	28-Nov-23 A	18-Jul-24	
220	Close flap gates and screw gates - DWR	1	26-Apr-24	26-Apr-24	0%
221	Close Irrigation Ditch Inlet Gates-DWR	1	26-Apr-24	26-Apr-24	0%
222	Clean and Close Gate with Missing Actuator (T&M)	2	29-Apr-24	30-Apr-24	0%
223	Install Dewatering System	1	28-Nov-23 A	28-Nov-23 A	100%
224	Dewater Basin	2	29-Nov-23 A	30-Nov-23 A	100%
225	Fish Rescue	1	30-Nov-23 A	30-Nov-23 A	100%
226	15 Day Wait Period	15	01-May-24	15-May-24	0%
227	Remove Dewatering System	2	17-Jul-24	18-Jul-24	0%
Concrete Work		39	16-May-24	10-Jul-24	
229	Sawcut and Demo Existing Basin Slab	1	16-May-24	16-May-24	0%
230	Subgrade Prep + U/S Rock	1	17-May-24	17-May-24	0%
231	Drill and Dowel for Basin Slab	3	20-May-24	22-May-24	0%
232	[redacted]				
233					
234					
235	Strip Basin Slab Edge Forms	1	28-May-24	28-May-24	0%
236	Cure Basin Slab Concrete	5	29-May-24	02-Jun-24	0%
237	Drill and Dowel for Culvert Extensions	2	29-May-24	30-May-24	0%
238	Install 24" ID Culvert Extensions	1	31-May-24	31-May-24	0%

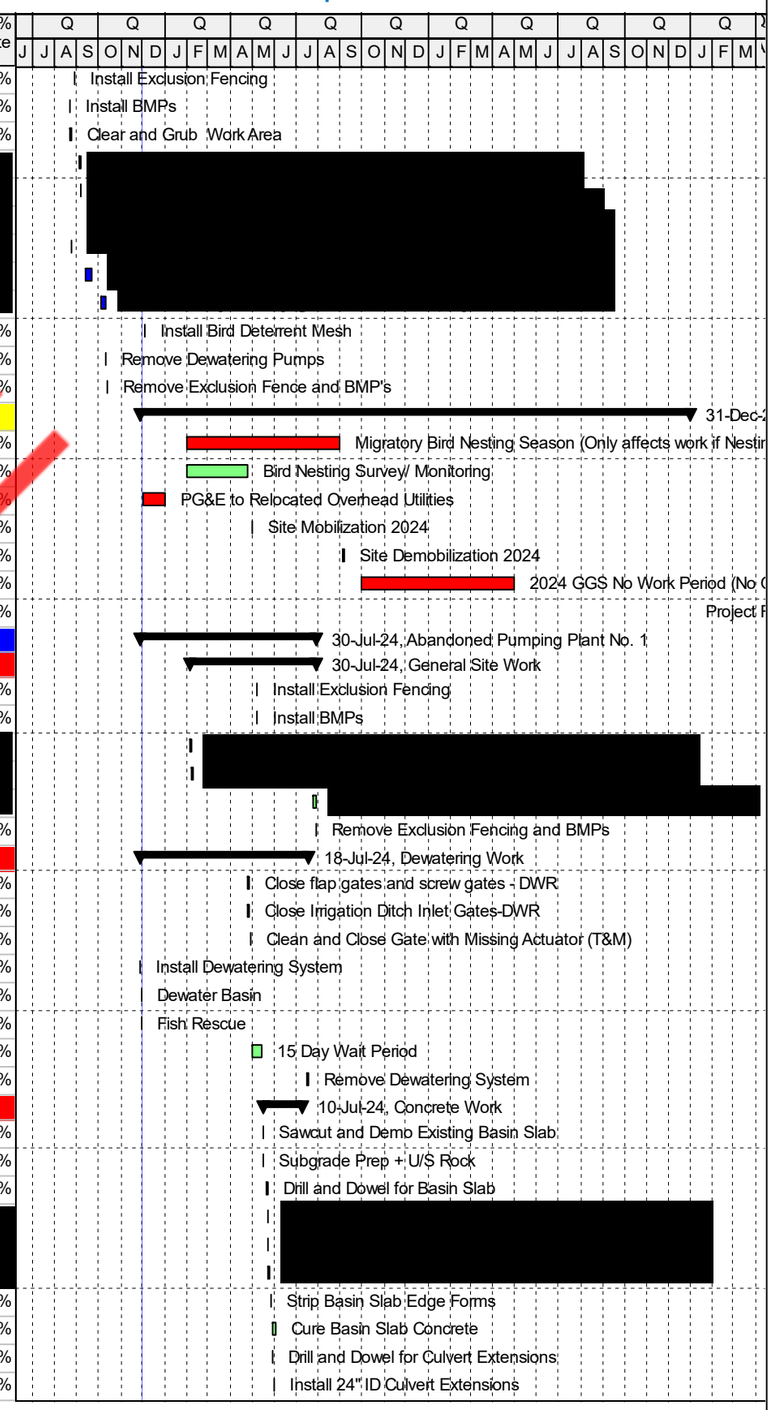

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
239	Install 30" ID Culvert Extension	1	03-Jun-24	03-Jun-24	0%
240	One Side Form Box Culvert Extension	2	04-Jun-24	05-Jun-24	0%
241	Install Box Culvert Extension Rebar	1	06-Jun-24	06-Jun-24	0%
242	Close Box Culvert Extension Form	1	07-Jun-24	07-Jun-24	0%
243	[redacted]				
244					
245					
246					
247					
248					
249	Place Headwall Concrete	1	21-Jun-24	21-Jun-24	0%
250	Strip Headwall Forms	2	24-Jun-24	25-Jun-24	0%
251	Cure Headwall Concrete	5	22-Jun-24	26-Jun-24	0%
252	One Side Pier Wall Forms	3	26-Jun-24	28-Jun-24	0%
253	Install Pier Wall Rebar	1	01-Jul-24	01-Jul-24	0%
254	Close Pier Wall Forms	2	02-Jul-24	03-Jul-24	0%
255	Place Pier Wall Concrete	1	05-Jul-24	05-Jul-24	0%
256	Strip Pier Wall Forms	3	08-Jul-24	10-Jul-24	0%
257	Cure Pier Wall Concrete	5	06-Jul-24	10-Jul-24	0%
258	Place CLSM Around Culvert Extensions	1	27-Jun-24	27-Jun-24	0%
Misc. Metals		8	11-Jul-24	22-Jul-24	
260	Install Trash Rack Wall and Floor Guides	3	11-Jul-24	15-Jul-24	0%
261	[redacted]				
262					
263	Install Handrail	2	19-Jul-24	22-Jul-24	0%
Earth Work		17	28-Jun-24	23-Jul-24	
265	Place Drain Rock and Drain Pipe	2	28-Jun-24	01-Jul-24	0%
266	Place and Compact Backfill within Bays	2	02-Jul-24	03-Jul-24	0%
267	Place and Compact AB @ Picking Pad	1	05-Jul-24	05-Jul-24	0%
268	Place and Compact AB on Access Road	1	23-Jul-24	23-Jul-24	0%
Abandoned Pumping Plant No. 2		91	29-Apr-24	03-Sep-24	
General Site Work		81	09-May-24	03-Sep-24	
271	Install Exclusion Fencing	1	09-May-24	09-May-24	0%
272	Install BMPs	1	10-May-24	10-May-24	0%
273	[redacted]				
274					
275	Fencing	4	27-Aug-24	30-Aug-24	0%
276	Remove Exclusion Fencing and BMPs	1	03-Sep-24	03-Sep-24	0%
Dewatering Work		80	29-Apr-24	19-Aug-24	
278	Close flap gates and screw gates - DWR	1	29-Apr-24	29-Apr-24	0%
279	Close Irrigation Ditch Inlet Gates-DWR	1	30-Apr-24	30-Apr-24	0%
280	Install Dewatering System	1	13-May-24	13-May-24	0%
281	Dewater Basin	2	14-May-24	15-May-24	0%
282	Fish Rescue	1	16-May-24	16-May-24	0%
283	15 Day Dry Wait Period	15	16-May-24	30-May-24	0%
284	Remove Dewatering System	1	19-Aug-24	19-Aug-24	0%
Concrete Work		47	31-May-24	06-Aug-24	
286	Sawcut and Demo Existing Basin Slab	1	31-May-24	31-May-24	0%
287	Subgrade Prep + U/S Rock	1	03-Jun-24	03-Jun-24	0%

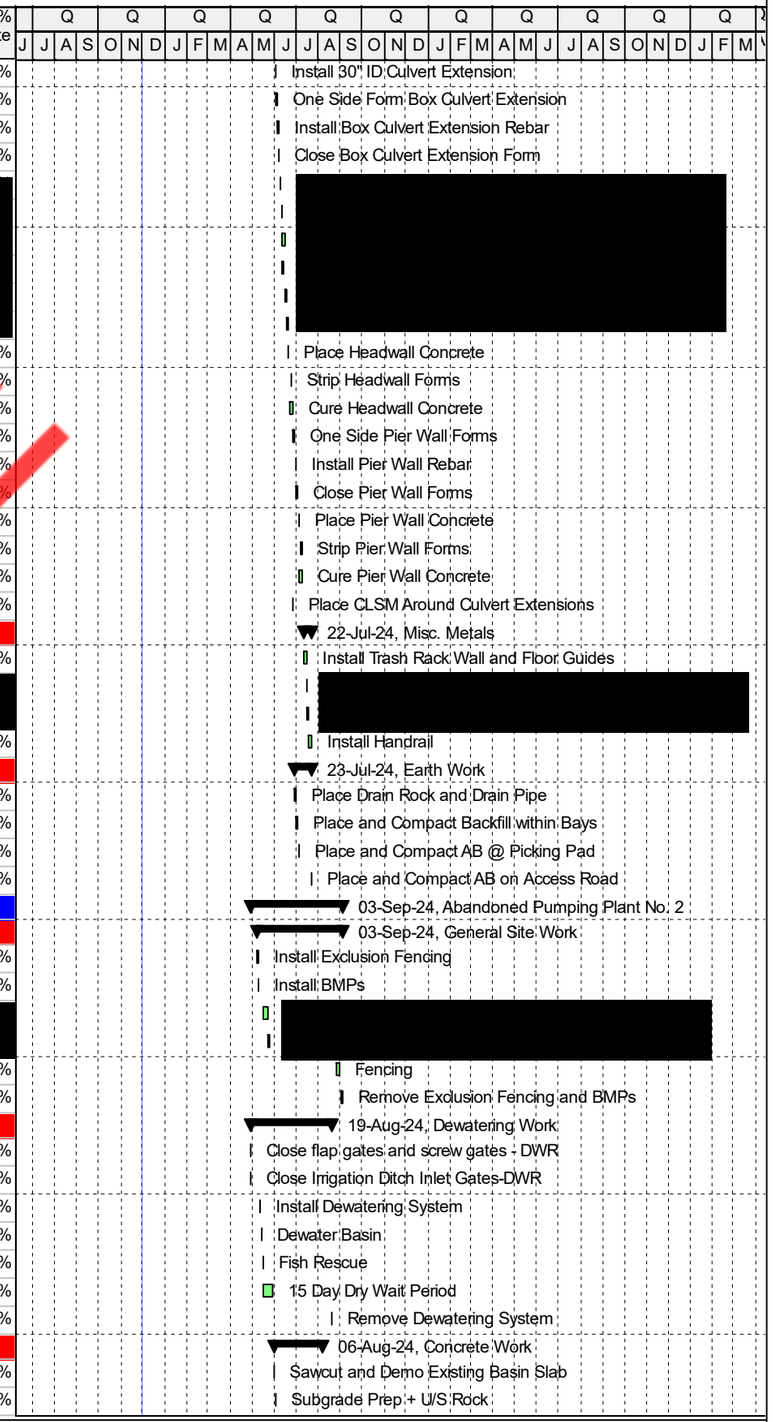

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
288	Drill and Dowel for Basin Slab	3	04-Jun-24	06-Jun-24	0%
289	[redacted]				
290					
291					
292					
293					
294	Drill and Dowel for Culvert Extensions	2	13-Jun-24	14-Jun-24	0%
295	One Side Form Box Culvert Extension	4	17-Jun-24	20-Jun-24	0%
296	Install Box Culvert Extension Rebar	2	21-Jun-24	24-Jun-24	0%
297	Close Box Culvert Extension Form	3	25-Jun-24	27-Jun-24	0%
298	Place Box Culvert Extension Concrete	1	28-Jun-24	28-Jun-24	0%
299	Strip Box Culvert Extension Forms	2	01-Jul-24	02-Jul-24	0%
300	Cure Box Culvert Extension Concrete	5	29-Jun-24	03-Jul-24	0%
301	One Side Form Box Culvert Structure Headwall	4	03-Jul-24	09-Jul-24	0%
302	Install Headwall Rebar	2	10-Jul-24	11-Jul-24	0%
303	Close Headwall Forms	2	12-Jul-24	15-Jul-24	0%
304	Place Headwall Concrete	1	16-Jul-24	16-Jul-24	0%
305	Strip Headwall Forms	3	17-Jul-24	19-Jul-24	0%
306	Cure Headwall Concrete	5	17-Jul-24	21-Jul-24	0%
307	One Side Pier Wall Forms	4	22-Jul-24	25-Jul-24	0%
308	Install Pier Wall Rebar	2	26-Jul-24	29-Jul-24	0%
309	[redacted]				
310					
311					
312					
313					
Misc. Metals		12	07-Aug-24	22-Aug-24	
315	Install Trash Rack Wall and Floor Guides	6	07-Aug-24	14-Aug-24	0%
316	Install Trash Racks	2	15-Aug-24	16-Aug-24	0%
317	Reinstall Salvaged Metals	2	19-Aug-24	20-Aug-24	0%
318	Install Handrail	2	21-Aug-24	22-Aug-24	0%
Earth Work		25	23-Jul-24	26-Aug-24	
320	Place Drain Rock and Drain Pipe	1	23-Jul-24	23-Jul-24	0%
321	Place and Compact Backfill within Bays	3	24-Jul-24	26-Jul-24	0%
322	Place and Compact AB @ Picking Pad	1	29-Jul-24	29-Jul-24	0%
323	Place and Compact AB on Access Road	2	23-Aug-24	26-Aug-24	0%
Abandoned Pumping Plant No. 3		76	01-May-24	15-Aug-24	
General Site Work		73	03-May-24	15-Aug-24	
326	Install Exclusion Fencing	1	03-May-24	03-May-24	0%
327	[redacted]				
328					
329					
330	Camera and Survey Culverts and Existing Screw Gate	1	30-May-24	30-May-24	0%
331	Remove Exclusion Fencing and BMPs	1	15-Aug-24	15-Aug-24	0%
Dewatering Work		73	01-May-24	12-Aug-24	
333	Close flap gates and screw gates - DWR	1	01-May-24	01-May-24	0%
334	Sheet Pile Cofferdam	5	07-May-24	13-May-24	0%
335	Install Dewatering Wells	3	14-May-24	16-May-24	0%

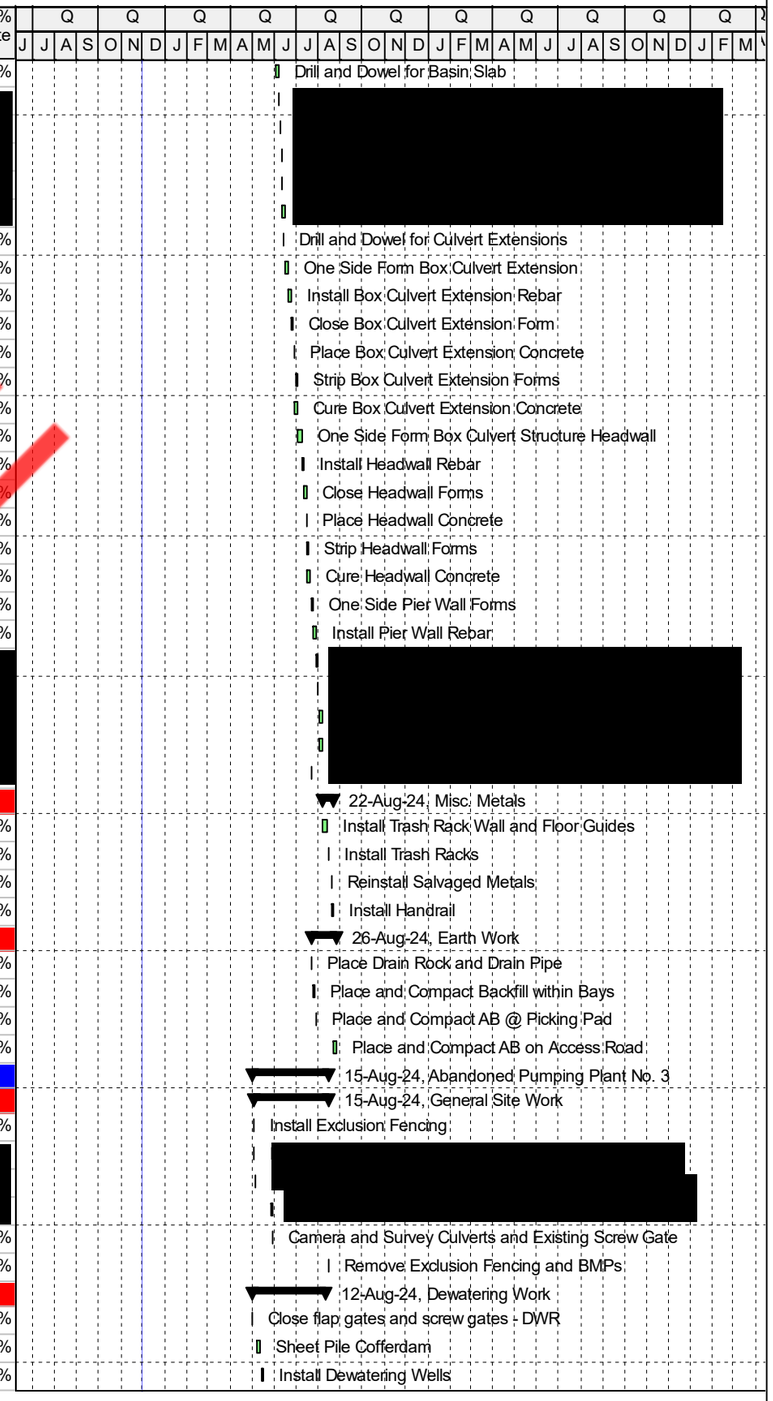

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
336	Dewater Basin	2	17-May-24	20-May-24	0%
337	Fish Rescue	1	21-May-24	21-May-24	0%
338	15 Day Dry Wait Period	21	22-May-24	11-Jun-24	0%
339	Remove Wells	1	07-Aug-24	08-Aug-24	0%
340	Remove Sheet Pile	2	08-Aug-24	12-Aug-24	0%
Demolition, Pipe Extension and Earthwork		**45**	**12-Jun-24**	**14-Aug-24**	
342	Sawcut and Remove Existing Steel Pipes Extending from Culvert	1	12-Jun-24	12-Jun-24	0%
343	[redacted]				
344					
345					
346					
347					
348					
349	Weld on Pipe Extensions	1	11-Jul-24	11-Jul-24	0%
350	Place & Compact Sand Filter	2	12-Jul-24	15-Jul-24	0%
351	Place & Compact Levee Fill	7	16-Jul-24	24-Jul-24	0%
352	Finish / Trim Slopes	2	25-Jul-24	26-Jul-24	0%
353	Cut 36" Pipe & Weld Seep Ring	1	29-Jul-24	29-Jul-24	0%
354	Subgrade Prep + U/S Rock	1	03-Jul-24	03-Jul-24	0%
355	Place Drain Rock	0	06-Aug-24	06-Aug-24	0%
356	Str. Backfill	3	07-Aug-24	12-Aug-24	0%
357	Place Fabric and RSP	1	12-Aug-24	13-Aug-24	0%
358	Place & Compact AB	1	14-Aug-24	14-Aug-24	0%
Concrete Work		**23**	**05-Jul-24**	**06-Aug-24**	
360	Install Rebar for Trash Rack Structure Footings	1	05-Jul-24	05-Jul-24	0%
361	Place Trash Rack Structure Footings Concrete	1	08-Jul-24	08-Jul-24	0%
362	Cure Trash Rack Structure Footings Concrete	7	09-Jul-24	15-Jul-24	0%
363	Form Trash Rack Structure Footings Slab	2	09-Jul-24	10-Jul-24	0%
364	Install Rebar for Trash Rack Structure Slab	1	11-Jul-24	11-Jul-24	0%
365	[redacted]				
366					
367					
368					
369					
370					
371	Close Trash Rack Structure Wall Forms	2	24-Jul-24	26-Jul-24	0%
372	Place Trash Rack Structure Wall Concrete	1	26-Jul-24	29-Jul-24	0%
373	Strip Trash Rack Structure Wall Forms	3	29-Jul-24	01-Aug-24	0%
374	Cure Trash Rack Structure Wall Concrete	5	01-Aug-24	06-Aug-24	0%
Misc. Metals		**6**	**06-Aug-24**	**14-Aug-24**	
376	Install Trash Rack Wall and Floor Guides	1	06-Aug-24	07-Aug-24	0%
377	Install Trash Racks	1	07-Aug-24	08-Aug-24	0%
378	Relocate Willow Slough Stop Log	1	08-Aug-24	09-Aug-24	0%
379	Install Stop Log	1	09-Aug-24	12-Aug-24	0%
380	Reinstall Salvaged Metals	1	12-Aug-24	13-Aug-24	0%
381	Install Handrail	1	14-Aug-24	14-Aug-24	0%
Construction Season 3 -2025		**542**	**01-Dec-23**	**31-Dec-25**	
383	Migratory Bird Nesting Season (Only affects work if Nesting Birds are Found in Work Area)	212	01-Feb-25	31-Aug-25*	0%

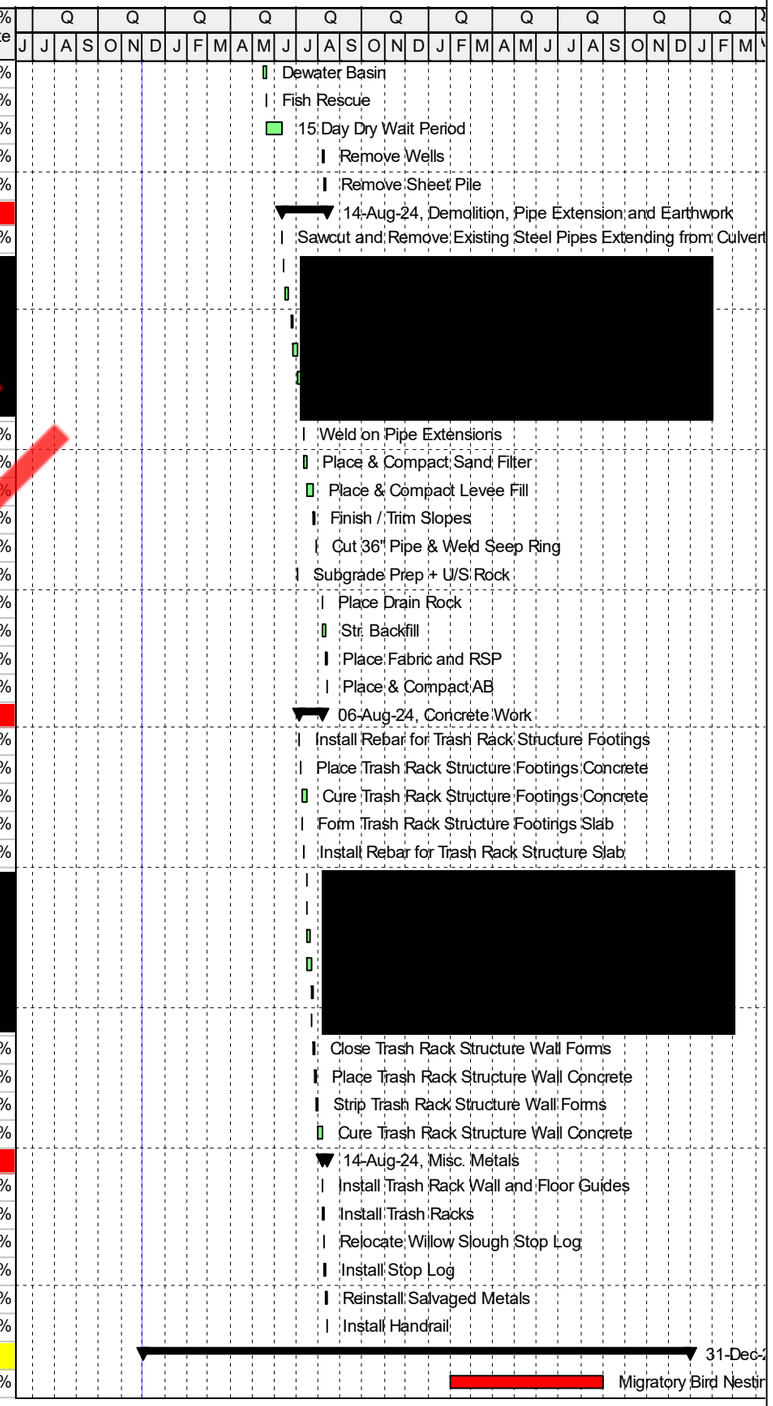

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
384	Bird Nesting Survey/ Monitoring	60	03-Feb-25*	25-Apr-25	0%
385	Site Mobilization 2025	3	01-May-25	05-May-25	0%
386	Site Demobilization 2025	2	02-Oct-25	03-Oct-25	0%
387	PG&E to Relocated Overhead Utilities	1	01-Dec-23	01-Dec-23	0%
388	Project Float	91	02-Oct-25	31-Dec-25	0%
Pumping Plant No. 1 Stop Log		76	06-May-25	20-Aug-25	
General Site Work		75	06-May-25	20-Aug-25	
392	Install Exclusion Fencing	1	06-May-25	06-May-25	0%
393	Install BMPs	1	07-May-25	07-May-25	0%
394	Remove Exclusion Fencing & BMPS	1	20-Aug-25	20-Aug-25	0%
Dewatering Work		71	09-May-25	18-Aug-25	
396	Sheet Pile Cofferdam	5	09-May-25	15-May-25	0%
397	Install Dewatering System	1	16-May-25	16-May-25	0%
398	[redacted]				
399					
400					
401	Remove Dewatering System	1	14-Aug-25	14-Aug-25	0%
402	Remove Sheet Pile Cofferdam	2	15-Aug-25	18-Aug-25	0%
Concrete Work		39	16-Jun-25	10-Aug-25	
404	Drill and Dowel into Existing Concrete	3	16-Jun-25	18-Jun-25	0%
405	Form Stop Log Structure Slab	1	19-Jun-25	19-Jun-25	0%
406	[redacted]				
407					
408					
409					
410					
411					
412					
413	Install Stop Log Wall Embed Slots	2	08-Jul-25	09-Jul-25	0%
414	Close Stop Log Structure Walls & Pier Walls Forms	2	10-Jul-25	11-Jul-25	0%
415	Place Stop Log Structure Wall Concrete	1	14-Jul-25	14-Jul-25	0%
416	Strip Stop Log Structure Wall Forms	4	15-Jul-25	18-Jul-25	0%
417	Cure Stop Log Structure Wall Concrete	5	19-Jul-25	23-Jul-25	0%
418	Install Concrete Lining Edge Form	1	30-Jul-25	30-Jul-25	0%
419	Install Concrete Lining Rebar	2	31-Jul-25	01-Aug-25	0%
420	Place Concrete Lining Concrete	1	04-Aug-25	04-Aug-25	0%
421	Strip Concrete Lining Edge Form	1	05-Aug-25	05-Aug-25	0%
422	Cure Concrete Lining Concrete	5	06-Aug-25	10-Aug-25	0%
Stop Logs + Misc. Metals		15	24-Jul-25	13-Aug-25	
424	Install Stop Log Panels	3	24-Jul-25	28-Jul-25	0%
425	[redacted]				
426					
427					
428	Install Handrail	4	08-Aug-25	13-Aug-25	0%
Demolition & Earthwork		72	08-May-25	19-Aug-25	
430	Move RSP as Needed for Sheet Pile Installation	1	08-May-25	08-May-25	0%
431	Sawcut and Demo Existing Transition Walls	2	06-Jun-25	09-Jun-25	0%
432	Excavate for Wing Walls and Keyways	2	10-Jun-25	11-Jun-25	0%
433	Prepare Subgrade & Excavate Key Ways For Slab	1	12-Jun-25	12-Jun-25	0%

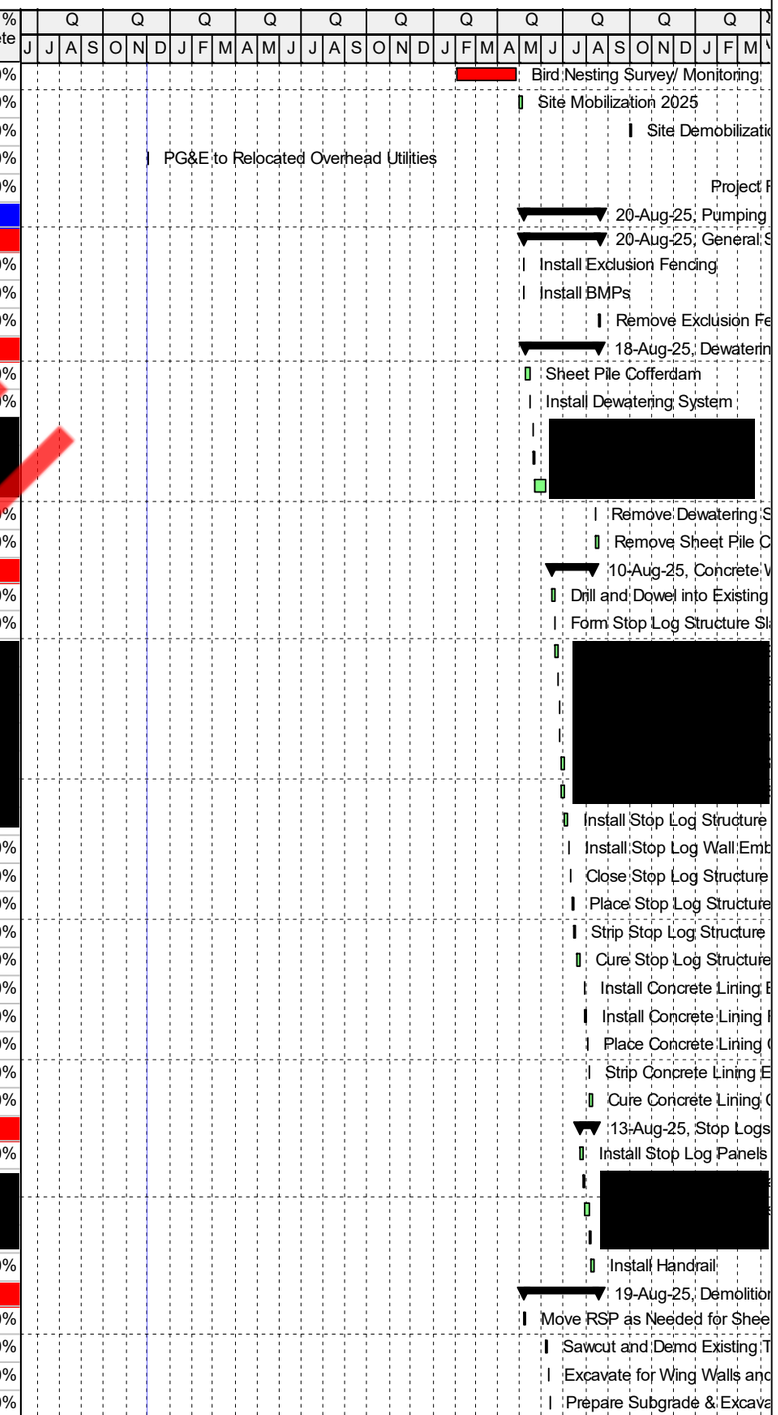

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
434	U/S Rock	1	13-Jun-25	13-Jun-25	0%
435	[redacted]				
436					
437					
Electrical Work		9	09-May-25	21-May-25	
439	Exc. For Electrical Pull Boxes and Conduit	2	09-May-25	12-May-25	0%
440	Install Pull Boxes and Conduit	4	13-May-25	16-May-25	0%
441	Place Duct Bank Lean Concrete	1	19-May-25	19-May-25	0%
442	Backfill and Compact at Pull Boxes and Conduit	2	20-May-25	21-May-25	0%
Pumping Plant No. 2 Stop Log		105	07-May-25	01-Oct-25	
General Site Work		103	07-May-25	01-Oct-25	
445	Install Exclusion Fencing	1	07-May-25	07-May-25	0%
446	Install BMPs	1	08-May-25	08-May-25	0%
447	Remove Exclusion Fencing & BMPS	1	01-Oct-25	01-Oct-25	0%
Dewatering Work		96	16-May-25	29-Sep-25	
449	Sheet Pile Cofferdam	5	16-May-25	22-May-25	0%
450	Install Dewatering System	1	23-May-25	23-May-25	0%
451	[redacted]				
452					
453					
454	Remove Dewatering System	1	25-Sep-25	25-Sep-25	0%
455	Remove Sheet Pile Cofferdam	2	26-Sep-25	29-Sep-25	0%
Concrete Work		55	24-Jun-25	09-Sep-25	
457	Drill and Dowel into Existing Concrete	3	24-Jun-25	26-Jun-25	0%
458	Form Stop Log Structure Slab	1	06-Aug-25	06-Aug-25	0%
459	Install Stop Log Structure Slab Rebar	2	07-Aug-25	08-Aug-25	0%
460	[redacted]				
461					
462					
463					
464					
465					
466	Install Stop Log Wall Embed Slots	2	22-Aug-25	25-Aug-25	0%
467	Close Stop Log Structure Walls & Pier Walls Forms	2	26-Aug-25	27-Aug-25	0%
468	Place Stop Log Structure Wall Concrete	1	28-Aug-25	28-Aug-25	0%
469	Strip Stop Log Structure Wall Forms	4	29-Aug-25	04-Sep-25	0%
470	Cure Stop Log Structure Wall Concrete	5	05-Sep-25	09-Sep-25	0%
Stop Logs + Misc. Metals		15	10-Sep-25	30-Sep-25	
472	Install Stop Log Panels	3	10-Sep-25	12-Sep-25	0%
473	[redacted]				
474					
475					
476	Install Handrail	4	25-Sep-25	30-Sep-25	0%
Demolition & Earthwork		63	16-Jun-25	12-Sep-25	
478	Sawcut and Demo Existing Transition Walls	2	16-Jun-25	17-Jun-25	0%
479	Excavate for Wing Walls and Keyways	2	18-Jun-25	19-Jun-25	0%
480	Prepare Subgrade	1	20-Jun-25	20-Jun-25	0%
481	U/S Rock	1	23-Jun-25	23-Jun-25	0%
482	Backfill & Compact Behind Stop Log Walls	3	10-Sep-25	12-Sep-25	0%

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
Electrical Work		9	22-May-25	04-Jun-25	
484	Exc. For Electrical Pull Boxes and Conduit	2	22-May-25	23-May-25	0%
485	Install Pull Boxes and Conduit	4	27-May-25	30-May-25	0%
486	Place Duct Bank Lean Concrete	1	02-Jun-25	02-Jun-25	0%
487	Backfill and Compact at Pull Boxes and Conduit	2	03-Jun-25	04-Jun-25	0%
Pumping Plant No. 3 Stop Log		100	09-May-25	26-Sep-25	
General Site Work		98	09-May-25	26-Sep-25	
490	Install Exclusion Fencing	1	09-May-25	09-May-25	0%
491	Install BMPs	1	12-May-25	12-May-25	0%
492	Remove Exclusion Fencing & BMPS	1	26-Sep-25	26-Sep-25	0%
Dewatering Work		89	23-May-25	25-Sep-25	
494	Sheet Pile Cofferdam	5	23-May-25	30-May-25	0%
495	Install Dewatering System	1	02-Jun-25	02-Jun-25	0%
496	[redacted]				
497					
498					
499	Remove Dewatering System	1	23-Sep-25	23-Sep-25	0%
500	Remove Sheet Pile Cofferdam	2	24-Sep-25	25-Sep-25	0%
Concrete Work		58	01-Jul-25	20-Sep-25	
502	Drill and Dowel into Existing Concrete	3	01-Jul-25	03-Jul-25	0%
503	Form Stop Log Structure Slab	1	06-Aug-25	06-Aug-25	0%
504	[redacted]				
505					
506					
507					
508					
509	One Side Form Stop Log Structure Walls & Pier Walls	4	14-Aug-25	19-Aug-25	0%
510	Install Stop Log Structure Wall Rebar	2	20-Aug-25	21-Aug-25	0%
511	Install Stop Log Wall Embed Slots	2	22-Aug-25	25-Aug-25	0%
512	Close Stop Log Structure Walls & Pier Walls Forms	2	26-Aug-25	27-Aug-25	0%
513	Place Stop Log Structure Wall Concrete	1	28-Aug-25	28-Aug-25	0%
514	Strip Stop Log Structure Wall Forms	4	29-Aug-25	04-Sep-25	0%
515	Cure Stop Log Structure Wall Concrete	5	29-Aug-25	02-Sep-25	0%
516	Install Concrete Lining Edge Form	1	09-Sep-25	09-Sep-25	0%
517	Install Concrete Lining Rebar	2	10-Sep-25	11-Sep-25	0%
518	[redacted]				
519					
520					
Stop Logs + Misc. Metals		15	03-Sep-25	23-Sep-25	
522	Install Stop Log Panels	3	03-Sep-25	05-Sep-25	0%
523	Reinstall Salvaged Metals	2	08-Sep-25	09-Sep-25	0%
524	Install Grating Supports	4	10-Sep-25	15-Sep-25	0%
525	Install Grating	2	16-Sep-25	17-Sep-25	0%
526	Install Handrail	4	18-Sep-25	23-Sep-25	0%
Demolition & Earthwork		92	13-May-25	22-Sep-25	
528	Move RSP as Needed for Sheet Pile Installation	1	13-May-25	13-May-25	0%
529	[redacted]				
530					
531	Prepare Subgrade	1	27-Jun-25	27-Jun-25	0%

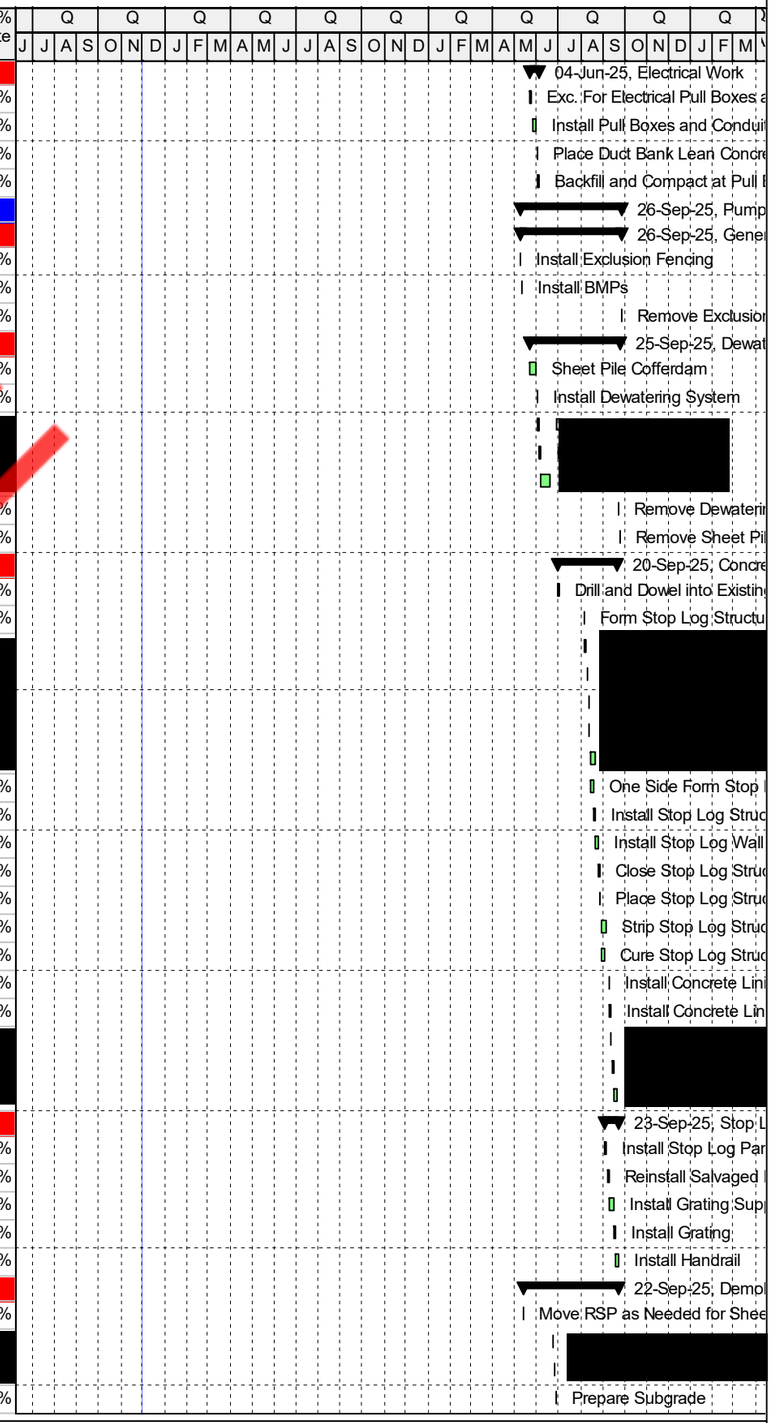

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
532	U/S Rock	1	30-Jun-25	30-Jun-25	0%
533	Backfill & Compact Behind Stop Log Walls	3	03-Sep-25	05-Sep-25	0%
534	Cut Slope for Concrete Lining	1	08-Sep-25	08-Sep-25	0%
535	Replace Moved RSP	1	22-Sep-25	22-Sep-25	0%
Electrical Work		9	05-Jun-25	17-Jun-25	
537	Exc. For Electrical Pull Boxes and Conduit	2	05-Jun-25	06-Jun-25	0%
538	Install Pull Boxes and Conduit	4	09-Jun-25	12-Jun-25	0%
539	Place Duct Bank Lean Concrete	1	13-Jun-25	13-Jun-25	0%
540	Backfill and Compact at Pull Boxes and Conduit	2	16-Jun-25	17-Jun-25	0%
EXTRA ADDED SCOPE		127	19-Jul-23 A	30-Nov-23 A	
MD01 - GENERAL PERMIT FEE		7	27-Jul-23 A	07-Aug-23 A	
541	Receive MD 01	1	27-Jul-23 A	27-Jul-23 A	100%
542	Complete SWPPP Filing with State	7	28-Jul-23 A	07-Aug-23 A	100%
MD02 - PP1 OPERATE GATE IN IRRIGATION CANAL		90	19-Jul-23 A	11-Oct-23 A	
544	Receive MD 02	1	19-Jul-23 A	19-Jul-23 A	100%
545	Prep and close canal gate	10	08-Aug-23 A	09-Aug-23 A	100%
546	[redacted]				
547					
548					
549	Install cofferdam	2	11-Sep-23 A	12-Sep-23 A	100%
550	Install blank plate	2	20-Sep-23 A	21-Sep-23 A	100%
551	Dewater Basin	2	21-Sep-23 A	22-Sep-23 A	100%
552	Rebuild Cofferdam	5	11-Oct-23 A	11-Oct-23 A	100%
MD03 - OPERATE FLAP GATES		110	09-Aug-23 A	28-Nov-23 A	
553	Receive MD 03	1	09-Aug-23 A	09-Aug-23 A	100%
554	Close Flap Gates at PP2	1	11-Aug-23 A	11-Aug-23 A	100%
555	[redacted]				
556					
557					
558	Remove Seal at Flap Gate PP2	5	10-Oct-23 A	10-Oct-23 A	100%
559	Remove Seal at Flap Gate PP1	5	12-Oct-23 A	12-Oct-23 A	100%
579	Install Steel Plat at PP. 1 Flap Gates	5	27-Nov-23 A	28-Nov-23 A	100%
MD04 - FISH RESCUE SUPPORT		110	17-Aug-23 A	30-Nov-23 A	
561	Receive MD 04	1	17-Aug-23 A	17-Aug-23 A	100%
562	Support Fish Rescue PP2	1	01-Sep-23 A	01-Sep-23 A	100%
563	Support Fish Rescue PP1	1	03-Oct-23 A	03-Oct-23 A	100%
583	Support Fish Rescue PP1	5	30-Nov-23 A	30-Nov-23 A	100%
MD05 - SEDIMENT REMOVAL		88	11-Sep-23 A	09-Oct-23 A	
565	Receive MD05	1	13-Sep-23 A	13-Sep-23 A	100%
566	Clear and Grub for Sediment/Vegitation PP2	2	11-Sep-23 A	12-Sep-23 A	100%
567	[redacted]				
568					
569					
MD06 - Winter Work at Abandoned Plant No. 1		42	28-Sep-23 A	27-Nov-23 A	
571	Receive MD 06	5	28-Sep-23 A	28-Sep-23 A	100%
581	Pumping Plant Operational for Agriculture Water	22	13-Oct-23 A	15-Nov-23 A	100%
591	Mobilize for Winter Work	1	13-Nov-23 A	13-Nov-23 A	100%
601	Reinstall Exclusion Fencing at PP. 1	1	14-Nov-23 A	14-Nov-23 A	100%

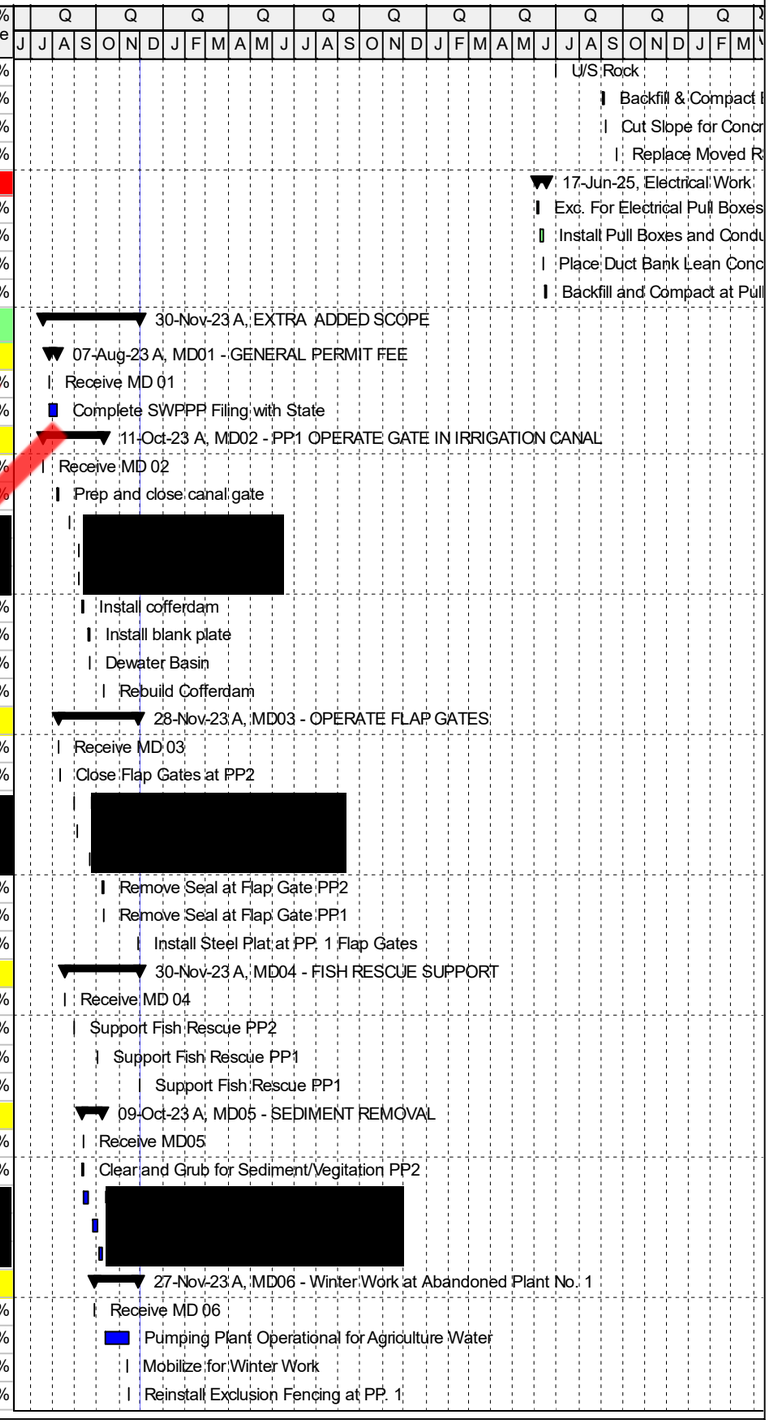

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

C51640 - 2329. DWR Sutter Bypass Pumping Plant Removal Rehab NOV-23 Update Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete
611	Abandoned PP Operational During Existing PP Repairs	8	15-Nov-23 A	27-Nov-23 A	100%
MD07 - Pumping Plant No. 1 Collapsed Culvert Work		29	17-Oct-23 A	29-Nov-23 A	
573	Receive MD 07	1	17-Oct-23 A	17-Oct-23 A	100%
574	Excavate Material From Culvert Collapse	2	20-Oct-23 A	21-Oct-23 A	100%
575	[redacted]				
576					
577					
578	Order 60" Culvert Sections	29	30-Oct-23 A	27-Nov-23 A	100%
588	Receive 60" Culvert Sections	1	28-Nov-23 A	28-Nov-23 A	100%
598	Remove Cofferdam at Collapsed Culvert	2	28-Nov-23 A	29-Nov-23 A	100%
MD08 - Pumping Plant No. 1 Existing Culvert Modifications		5	31-Oct-23 A	31-Oct-23 A	
560	Receive MD 08	5	31-Oct-23 A	31-Oct-23 A	100%

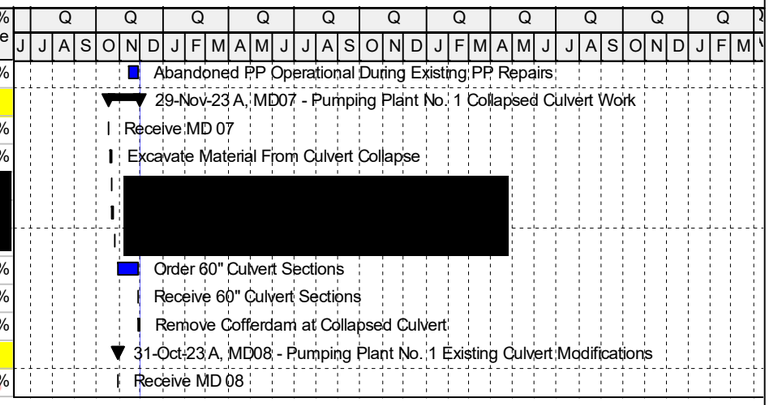

SAMPLE

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation
