P.S. 117-QUEENS RESO A AUDITORIUM UPGRADE
PROJECT SCHEDULE

Activity ID	Activity Name	Original Duration	Start	Finish
P.S. 117 - QUEENS RESO A AUDITORIUM UPGRADE		**283**	**Jun-20-22**	**Jul-19-23**
NTP-100	Notice to Proceed (NTP)	0	Jun-20-22	
SUBMITTALS		**21**	**Jun-21-22**	**Jul-19-22**
[redacted]				
SUB-160	Paint	6	Jun-21-22	Jun-28-22
SUB-170	Gypsum Board	6	Jun-21-22	Jun-28-22
SUB-180	Ceramic Tile	6	Jun-21-22	Jun-28-22
[redacted]				
SUB-250	Wiring Systems Affidavit & Schedule	7	Jul-04-22	Jul-12-22
SUB-260	Raceways Affidavit & Schedule	7	Jul-04-22	Jul-12-22
SUB-270	Hilti FS-ONE MAX & Thermafiber	7	Jul-04-22	Jul-12-22
SUB-280	DOB Electrical Permit	7	Jun-27-22	Jul-05-22
SUB-290	SAF Form	7	Jun-27-22	Jul-05-22
SUB-300	Platform Curtains	7	Jul-06-22	Jul-14-22
SUB-310	Window Curtains	7	Jul-06-22	Jul-14-22
SUB-320	Fixed Audience Seating	10	Jul-06-22	Jul-19-22
SUB-330	Stainless Steel Railing & Handrail	10	Jul-06-22	Jul-19-22
SUB-340	Stainless Steel Guards	10	Jul-06-22	Jul-19-22
SUB-350	Signage	10	Jul-06-22	Jul-19-22
DEMOLITION WORKS		**30**	**Jul-06-22**	**Aug-16-22**
DW-100	Removal of Existing Projector Screen	2	Jul-06-22	Jul-07-22
DW-110	Removal of Existing Wiring, Circuit Breaker & Phone Box	3	Jul-08-22	Jul-12-22
DW-120	Removal of Existing Auditorium Seating	7	Jul-13-22	Jul-21-22
DW-130	Removal of Existing Platform Curtains	3	Jul-22-22	Jul-26-22
DW-140	Removal of Existing Window Curtains	3	Jul-27-22	Jul-29-22
DW-150	Removal of Existing Sealed Concrete Finish	3	Aug-01-22	Aug-03-22
[redacted]				
ARCHITECTURAL WORKS		**219**	**Aug-17-22**	**Jun-19-23**
AW-100	Installation of New Stud Wall	12	Aug-17-22	Sep-01-22
AW-110	Installation of Wall Gypsum Board	15	Sep-02-22	Sep-22-22
AW-120	Installation of Wall Ceramic Tiles	18	Sep-23-22	Oct-18-22
AW-130	Patch & Repair & Paint Existing Walls	40	Oct-19-22	Dec-13-22
[redacted]				
AW-160	Installation of New Platform Curtains	18	Feb-24-23	Mar-21-23
AW-170	Installation of New Window Curtains	17	Mar-22-23	Apr-13-23
AW-180	Installation of New Stainless Steel Guards	17	Apr-14-23	May-08-23

SAMPLE

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved
Jul-19-22	00		

© Primavera Systems, Inc.

P.S. 117-QUEENS RESO A AUDITORIUM UPGRADE
PROJECT SCHEDULE

Activity ID	Activity Name	Original Duration	Start	Finish
AW-190	Installation of Railing & Handrail	15	May-09-23	May-29-23
AW-200	Installation of Signage	15	May-30-23	Jun-19-23
PLUMBING WORKS		132	Aug-17-22	Feb-16-23
PW-100	Installation of Sanitary, Storm & Vent System	14	Aug-17-22	Sep-05-22
[redacted]				
PW-140	Cleaning of Existing Drain & Sumps	15	Jan-13-23	Feb-02-23
PW-150	Installation of Pumps	10	Feb-03-23	Feb-16-23
ELECTRICAL WORKS		126	Aug-17-22	Feb-08-23
EW-100	Installation of New Wiring	14	Aug-17-22	Sep-05-22
EW-110	Installation of Circuit Breakers	10	Sep-06-22	Sep-19-22
[redacted]				
EW-140	Relocation of Existing Telephone & Lock Box	7	Jan-11-23	Jan-19-23
EW-150	Replacing of Existing Double Cassette Deck with New CD Player	7	Jan-20-23	Jan-30-23
EW-160	Replacing Existing Compact Disc Player with New DVD Player	7	Jan-31-23	Feb-08-23
PROJECT CLOSEOUT		22	Jun-19-23	Jul-19-23
PCO-100	Substantial Completion	0		Jun-19-23
PCO-110	Final Inspection & Testing	6	Jun-20-23	Jun-27-23
PCO-120	Punchlist & Rectifications	10	Jun-28-23	Jul-11-23
PCO-130	O&M's	2	Jul-12-23	Jul-13-23
PCO-140	As Built Submittal	2	Jul-14-23	Jul-17-23
PCO-150	Certificate of Occupancy	2	Jul-18-23	Jul-19-23
PCO-160	Final Completion	0		Jul-19-23

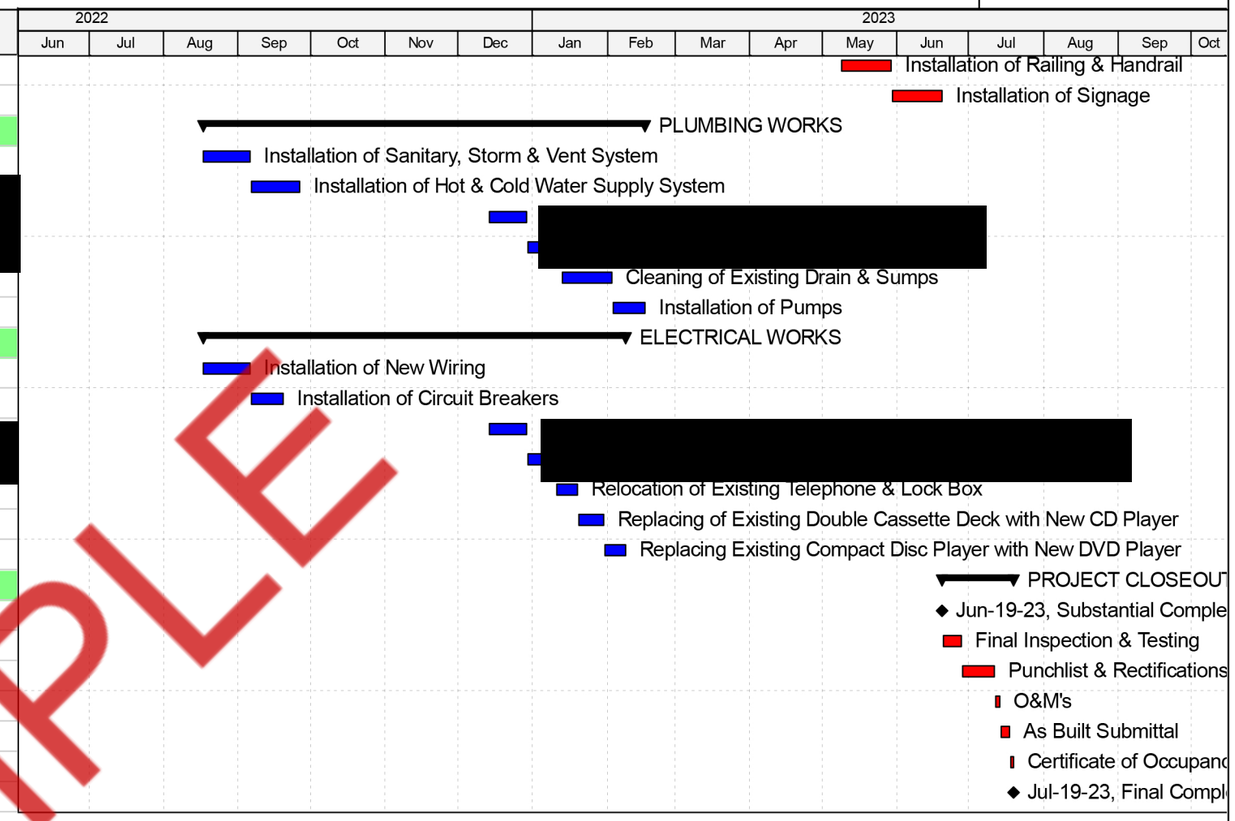

SAMPLE

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved
Jul-19-22	00		

© Primavera Systems, Inc.
